



TOWN OF CASCO

635 MEADOW ROAD
CASCO, MAINE 04015

Winter Sand

BID PROPOSAL FORM

Due Date: Must be received no later than 3:00 PM, August 13, 2026.

Name of Company: R. Rolfe Corporation

Location of pit: 0 Trails Edge Way Bridgton, ME 04009

Approved by Municipality or DEP: YES

Price per Yard \$ 18.00

Starting Date: AS SOON AS 9/1/26

The undersigned having reviewed the request for bids and all associated information including but not limited to general requirements for screened winter sand material, hereby agrees, if awarded the bid/contract, to supply all the necessary materials, tools, equipment, and labor to perform and complete the work in accordance with said requirements and specifications.

Signature: Spencer Morse

Printed Name: Spencer Morse Date: 8/4/26

Title: General Manager

Address: 91 Home Run Rd Bridgton ME 04009

Telephone: 207-647-9500

Reminder: attach sieve screen test results.



Report of Gradation

ASTM C136 & C117

Project Name:

Bridgton ME - Hotel Bridgton
 Sitework - Construction
 Materials Testing Services
 Bennett Excavation, LLC
 Manufactured Sand
 Bennett Excavation

Project #:

24-0037.2

Lab ID:

34486G

Date Received:

7/8/2026

Date Completed:

7/13/2026

Tested By:


Leah Young

Client:

Sample Description:

Material Source:

Standard Designation (mm/μm)	Sieve Size	Amount Passing (%)	Fractional Percentage (NHDOT 304.1 Sand)	NHDOT 304.1 Sand % Range
152.4 mm	6"	100%		> 100% Pass
127 mm	5"	100%		
100 mm	4"	100%		
76.1 mm	3"	100%		
50.8 mm	2"	100%		
37.5 mm	1-1/2"	100%		
25 mm	1"	100%		
19 mm	3/4"	100%		
12.5 mm	1/2"	100%		
6.3 mm	1/4"	91%		70% - 100% Pass
4.75 mm	No. 4	84%		
2 mm	No. 10	58%		
850 μm	No. 20	35%		
425 μm	No. 40	21%		
250 μm	No. 60	14%		
150 μm	No. 100	10%		
75 μm	No. 200	6.3%	7.5% of No. 4	0% - 12% Pass

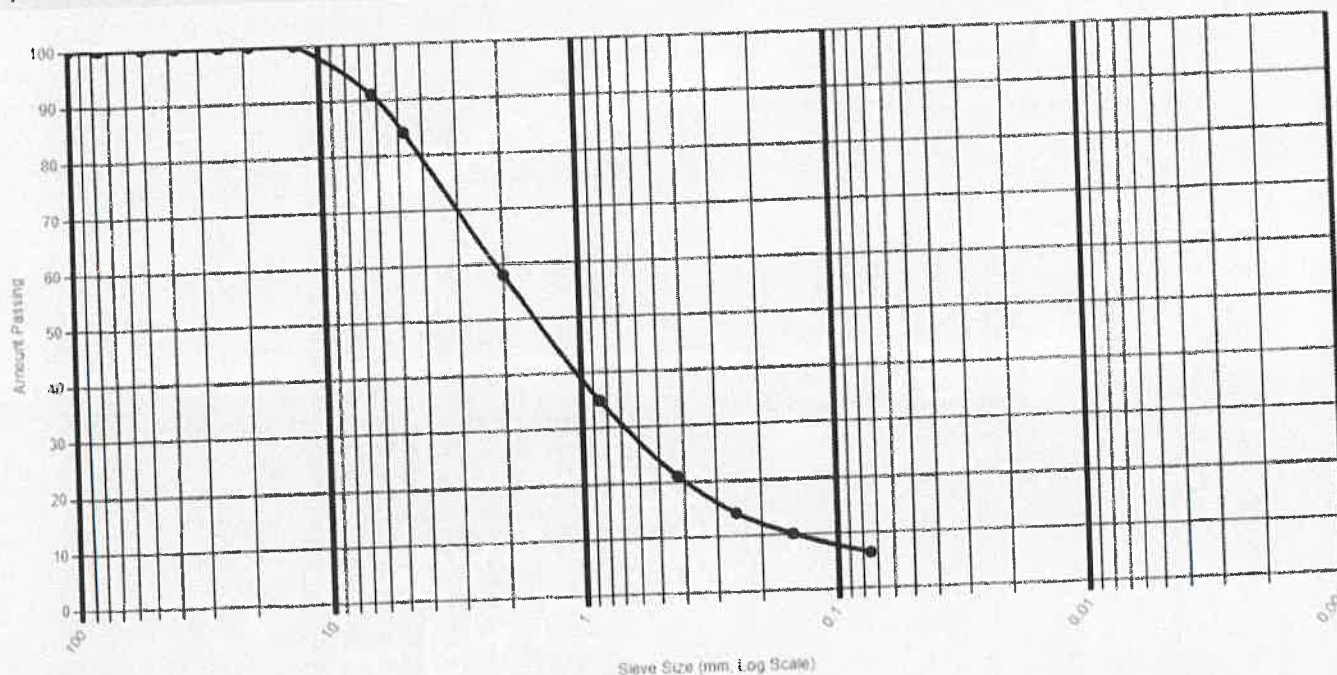

Remarks:

Sarah Sylvia

Reviewed By
