City of Beaumont, Annual Citywide Street Rehab Maint_211103 Revised — **All American Asphalt Job # 33949_211103** — 03-Nov-21 12:35

Activity ID	Activity Name	Original Duration	Start	Finish
City of Beaumont, Annual Citywide Street Rel		90	12-Oct-21	17-Feb-22
A1000	Pre Con, Submittal Development & Delivery	1	12-Oct-21	12-Oct-21
A1010	Passout Notices, USA	1	25-Oct-21	25-Oct-21
A1020	Place Project Signs, Tie Out Survey Monuments	1	01-Nov-21	01-Nov-21
A1030	NTP	0	08-Nov-21	
A1040	Implement BMPs	71	08-Nov-21	17-Feb-22
A1050	Sawcut for PCC Improvements	5	08-Nov-21	15-Nov-21
A1060	Pothole for R&R & PCC Improvements	5	08-Nov-21	15-Nov-21
A1070	Demo & Grade for PCC Improvements & Restoration (Start Location Ring Ranch & Wind Bound)	25	10-Nov-21	17-Dec-21
A1080	Veterans Day (Non Working Day)	1	11-Nov-21*	11-Nov-21
A1090	Form & Pour PCC Improvements, Place ADA Domes (Start Location Ring Ranch & Wind Bound)	25	12-Nov-21	20-Dec-21
A1100	AC Digouts (Start Location Ring Ranch & Wind Bound)	25	15-Nov-21	21-Dec-21
A1110	Thanksgiving Holiday (Non Working Days	4	25-Nov-21*	28-Nov-21
A1120	Union Holiday Local 12 (Non Working Day)	1	04-Dec-21*	04-Dec-21
A1230	Excavate & Grade Antonell	4	06-Dec-21	09-Dec-21
A1130	Crackfill	25	06-Dec-21	07-Jan-22
A1140	Coldmill (.10)	7	07-Dec-21	15-Dec-21
A1250	Base & CAP Pave Antonell	1	10-Dec-21	10-Dec-21
A1150	AC CAP	6	13-Dec-21	20-Dec-21
A1160	Striping Removal, Slurry Areas	5	20-Dec-21	24-Dec-21

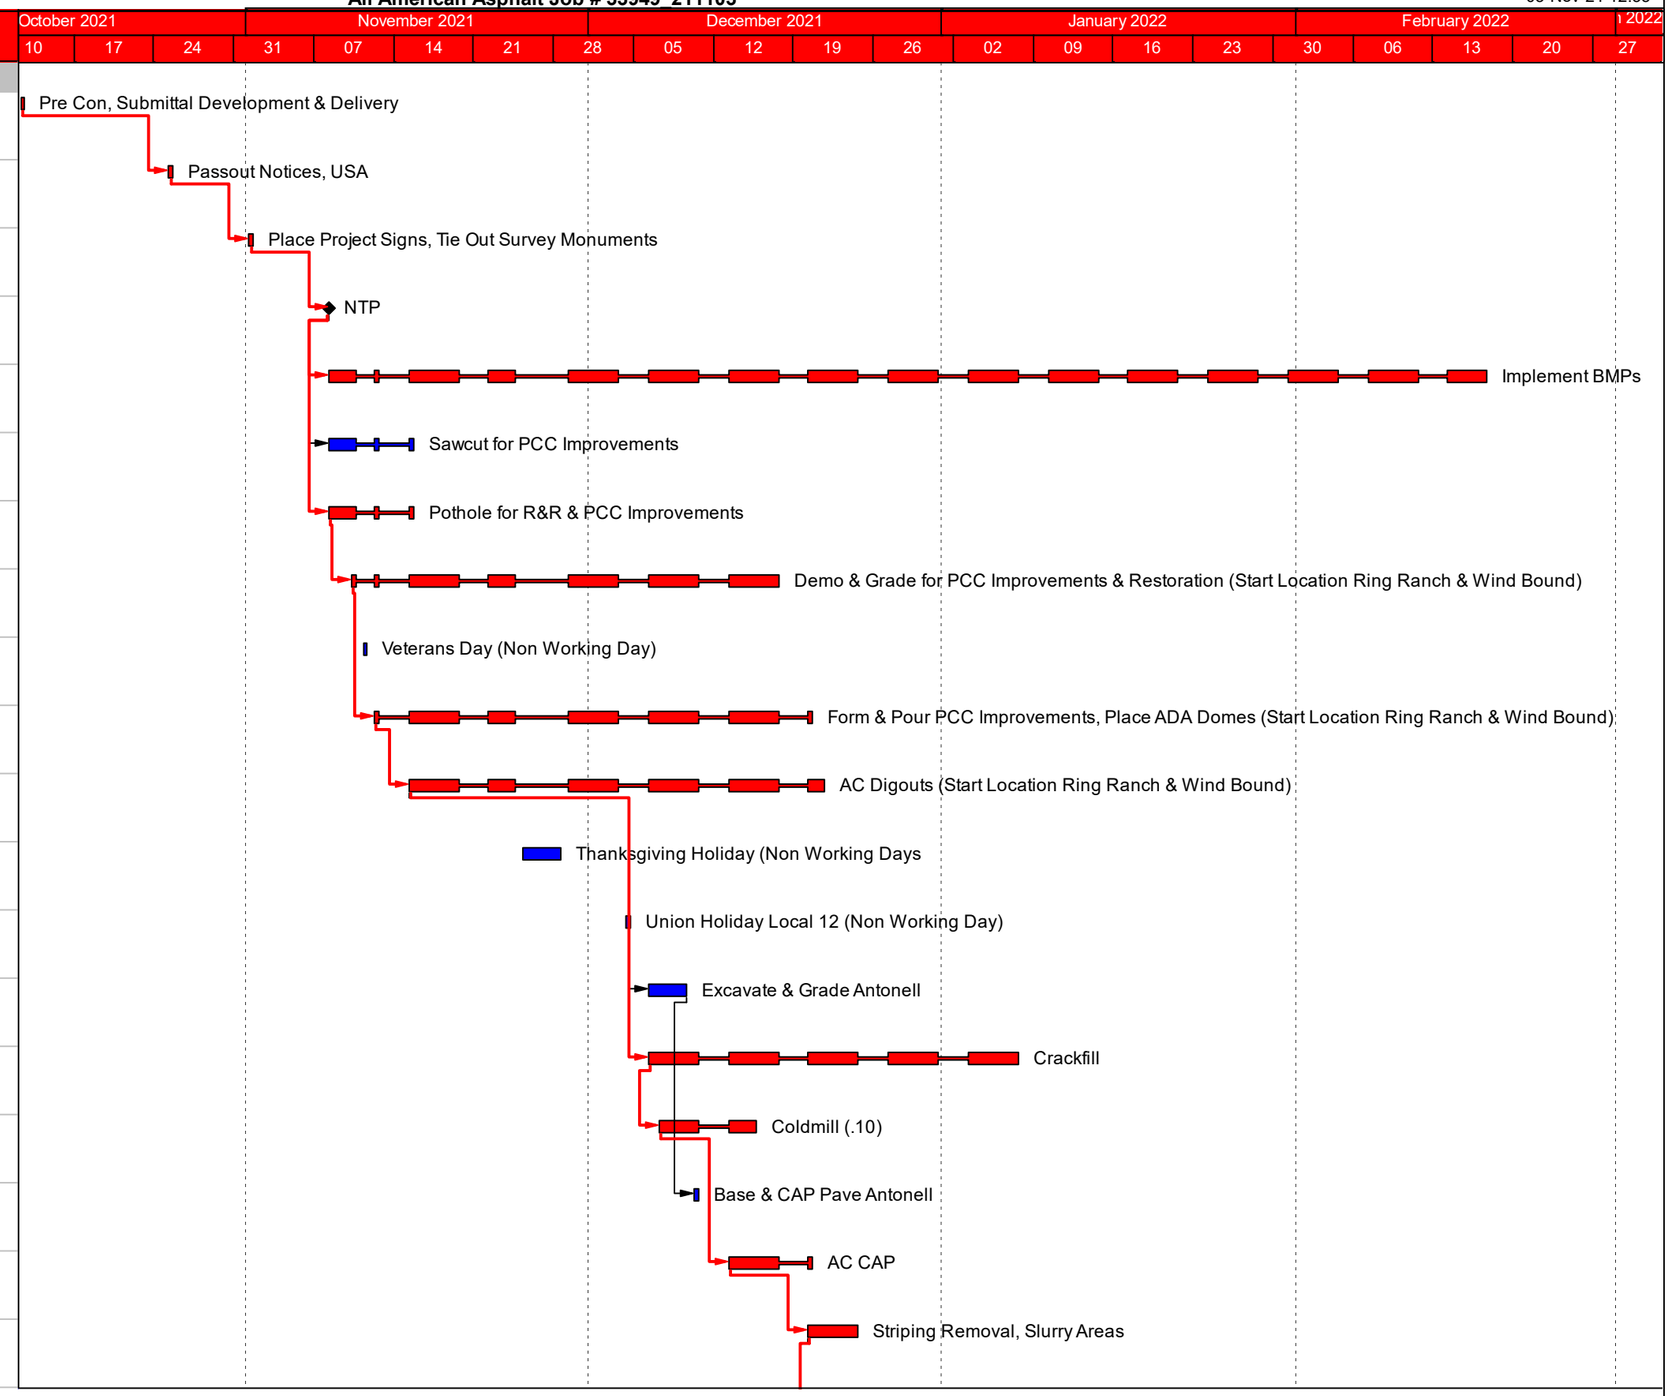

Actual Work — Critical Remaining Work — Remaining Work — Milestone

Prepared by cdominguez

City of Beaumont, Annual Citywide Street Rehab Maint_211103 Revised **All American Asphalt Job # 33949_211103** 03-Nov-21 12:35

Activity ID	Activity Name	Original Duration	Start	Finish
A1240	Adjust Utilities	5	21-Dec-21	27-Dec-21
A1170	Cattrack	1	21-Dec-21	21-Dec-21
A1180	Christmas Holiday (Non Working Days)	3	24-Dec-21*	26-Dec-21
A1190	Install Traffic Loops	4	27-Dec-21	30-Dec-21
A1200	Edge Mill for ARAM	3	28-Dec-21	30-Dec-21
A1210	New Years Holiday (Non Working Days)	3	31-Dec-21*	02-Jan-22
A1220	Install Aram & Slurry	33	03-Jan-22	16-Feb-22
A1235	Cattrack Slurry Streets	4	31-Jan-22	03-Feb-22
A1260	Final Stripe, Install Pavement Markings & Signage	8	07-Feb-22	16-Feb-22
A1270	Restore Survey Monuments	2	07-Feb-22	08-Feb-22
A1280	Clean up, Punchlist	1	14-Feb-22	14-Feb-22
A1290	Demob, Complete	1	17-Feb-22	17-Feb-22

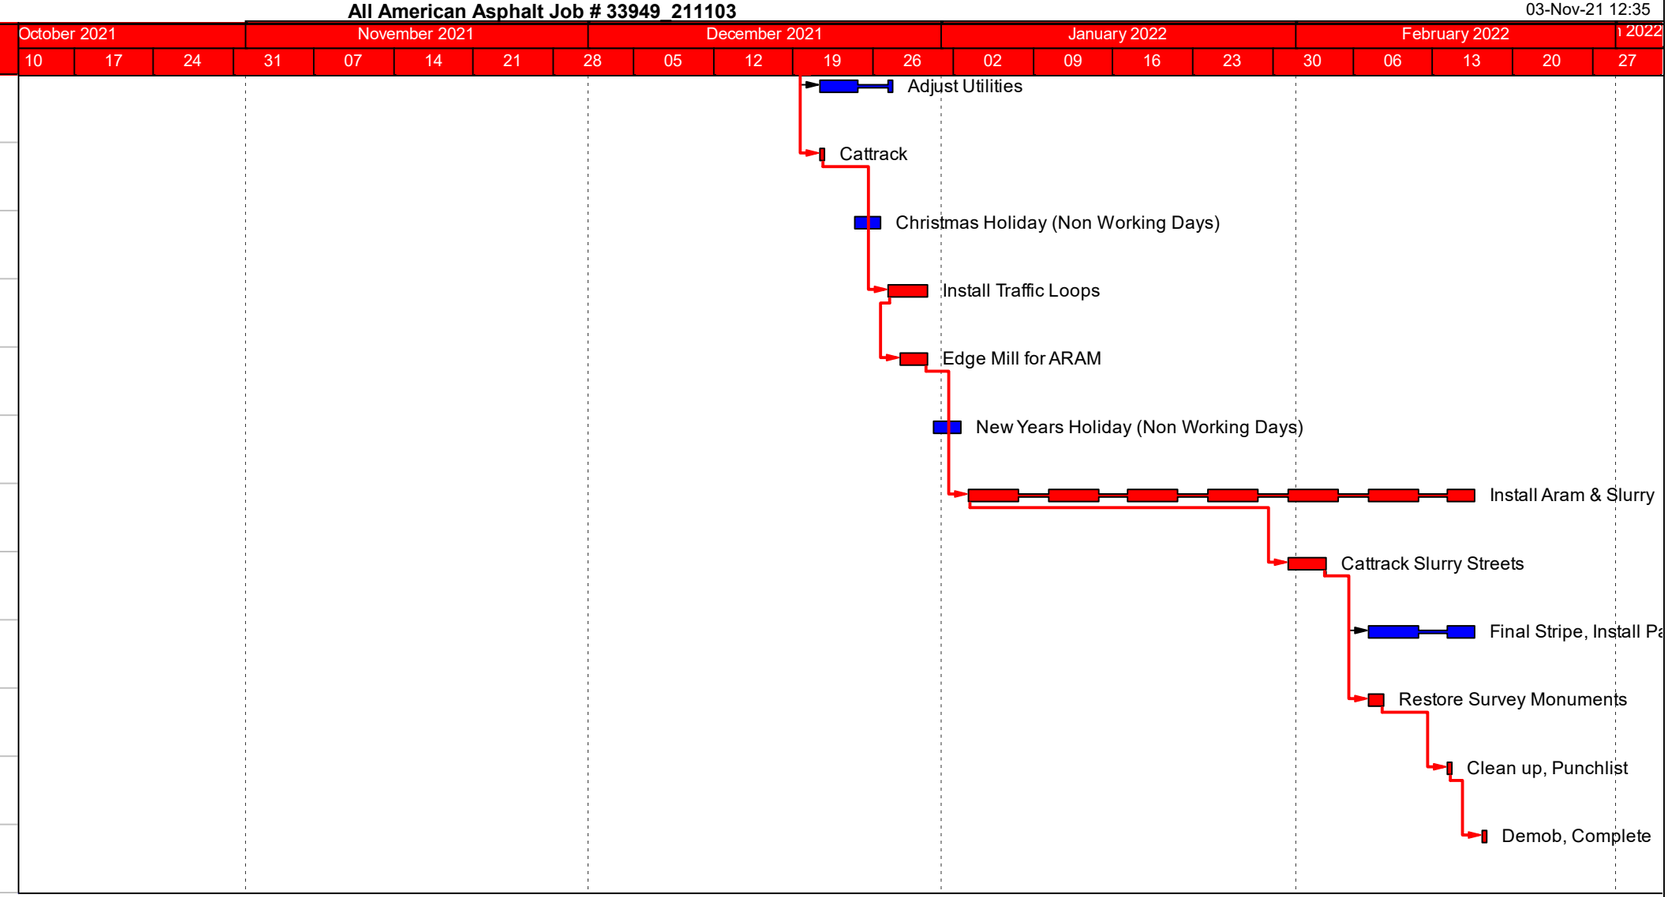

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Prepared by cdominguez
