Columbus GEORGIA

We do amazing.

CITY COUNCIL INFRASTRUCTURE UPDATE

NOVEMBER 10, 2026

FUNDING SOURCES

- Transportation Special Purpose Local Option Sales Tax (TSPLOST) 2012
- Transportation Special Purpose Local Option Sales Tax (TSPLOST) 2022
- TSPLOST Discretionary Funds
- Special Purpose Local Option Sales Tax (SPLOST) 2021
- Other Local Option Sales Tax (OLOST) Infrastructure Fund
- Stormwater Fund
- Paving Fund
- Georgia Department of Transportation (GDOT) Grants and Programs
- Private Donations and Public-Private Partnerships (Friends of the Dragonfly Trail, Columbus Regional Tennis Association (CORTA), Columbus, GA Pickleball Association and others)
- Columbus Building Authority Bonds

PROJECTS UNDER CONSTRUCTION

FLOOD ABATEMENT PROJECT – 19TH STREET SYSTEM



Installation of a new box culvert and flood basin to contain the CSS and reduce flooding issues. The project will run on the West side of Veterans Parkway from Apex Road to the flood basin located near 29th Street. Earthwork and culvert installation is ongoing. Installation is currently taking place on the North side of 35th Street.

Budget: $14,904,274.32

Funded by Stormwater, SPLOST and Bonds

Start Date: January 14, 2025

Scheduled Completion: Winter 2026

Percent Complete: 72%

PROJECTS UNDER CONSTRUCTION (CONT'D)

I-185/BUENA VISTA ROAD DIVERGING DIAMOND INTERCHANGE (DDI)



GDOT Managed (90% Complete)

Funding Source: FY12 TSPLOST

Current Budget: $52,730,628

Estimated Completion: December 2026

PROJECTS UNDER CONSTRUCTION (CONT'D)

I-185/CUSSETA ROAD INTERCHANCE



GDOT Managed (88% Complete)

Funding Source: FY12 TSPLOST

Current Budget: $71,971,219

Estimated Completion: Spring 2027

PROJECTS UNDER CONSTRUCTION (CONT'D)

SR1/US 27 WIDENING



GDOT Managed (62% Complete)

Funding Source: FY12 TSPLOST

Current Budget: $72,356,173

Estimated Completion: Summer 2027

PROJECTS UNDER CONSTRUCTION (CONT'D)

SPIDERWEB PHASE II



- Constructing Bridge over NS RR, replacing bridges over Bull Creek and Lindsey Creek (Morris Road), and constructing roundabouts at Illges/Ace Way and Morris/Ace Way
- Budget: $45.8M
- Project Started: April 8, 2025
- 61% Complete
- Anticipated Completion Date: April 2027
- 24-month intersection closure
- Funding Source: FY12 TSPLOST, LMIG, LRA, GDOT, TSPLOST Discretionary

PROJECTS UNDER CONSTRUCTION (CONT'D)

8TH STREET IMPROVEMENTS



- Installing new ramps to meet ADA requirements, replacing damaged sidewalks, and installing traffic calming measures. These measures consist of raised table-top crosswalks at 1st Avenue and 3rd Avenue and a mini roundabout at 2nd Avenue. New paving and striping will be completed in existing asphalt areas between Front Avenue and Veterans Parkway
- Project Started: January 26, 2026
- Anticipated Completion Date: August 2026
- Funding Source: 2022 TSPLOST Discretionary
- 75% Complete

PROJECTS UNDER CONSTRUCTION (CONT'D)

INFANTRY ROAD AND FOLLOW ME TRAIL EXTENSION



- New road from S. Lumpkin to Fort Benning Road and new trail along Fort Benning Road. Waiting on GDOT to provide revised construction agreement.
- Bids Received: August 7, 2024
- Budget: $2,439,946.30
- Start Date: March 2, 2026
- Anticipated Completion: Q2 2027

PROJECTS UNDER CONSTRUCTION (CONT'D)

DRAGONFLY TRAILS MIDTOWN CONNECTOR PHASE I



- Approximately 4,650 LF of new 10-foot wide multi-use trail which will connect to the existing trail at the intersection of Warren Williams Road and Wynnton Road. It follows Bradley Drive and Warren Williams Road to Dinglewood Park And continues to the intersection of 18th Avenue and 13th Street.
- Project Start Date: April 13th, 2026
- Project Completion Date: April 12th, 2027
- Project Budget: $1,495,236.19

PROJECTS UNDER CONSTRUCTION (CONT'D)

NORTHSTAR DRIVE @ KENNEDY STREET ROUNDABOUT



- New Roundabout at the intersection of Northstar Drive and Kennedy Street
- Construction Began:
- Budget: $2,439,946.30
- Anticipated Completion: Q1 2027

RECENTLY COMPLETED

COLLEGE DRIVE DRAINAGE REHABILITATION



- Enlarging existing detention pond and installing new outlet structure. In addition to increasing the pond's storage capacity, the outfall flow will be reduced to decrease the stress on the downstream system.
- Project Started: January 7, 2026
- Completion Date: June 22, 2026
- Funding Source: Stormwater/Drainage

RECENTLY COMPLETED (cont'd)

OXBROW CREEK BRIDGE REPLACEMENT





RECENTLY COMPLETED (cont'd)

2ND AVENUE @ 14TH STREET – SIGNAL UPGRADES





RECENTLY COMPLETED (cont'd)

BROWN AVENUE @ MARTIN LUTHER KING JUNIOR BOULEVARD – SIGNAL UPGRADES



RECENTLY COMPLETED (CONT'D)

11TH STREET TUNNEL RESURFACING



RECENTLY COMPLETED (CONT'D)

SIDEWALK AND ADA IMPROVEMENTS












RESURFACING

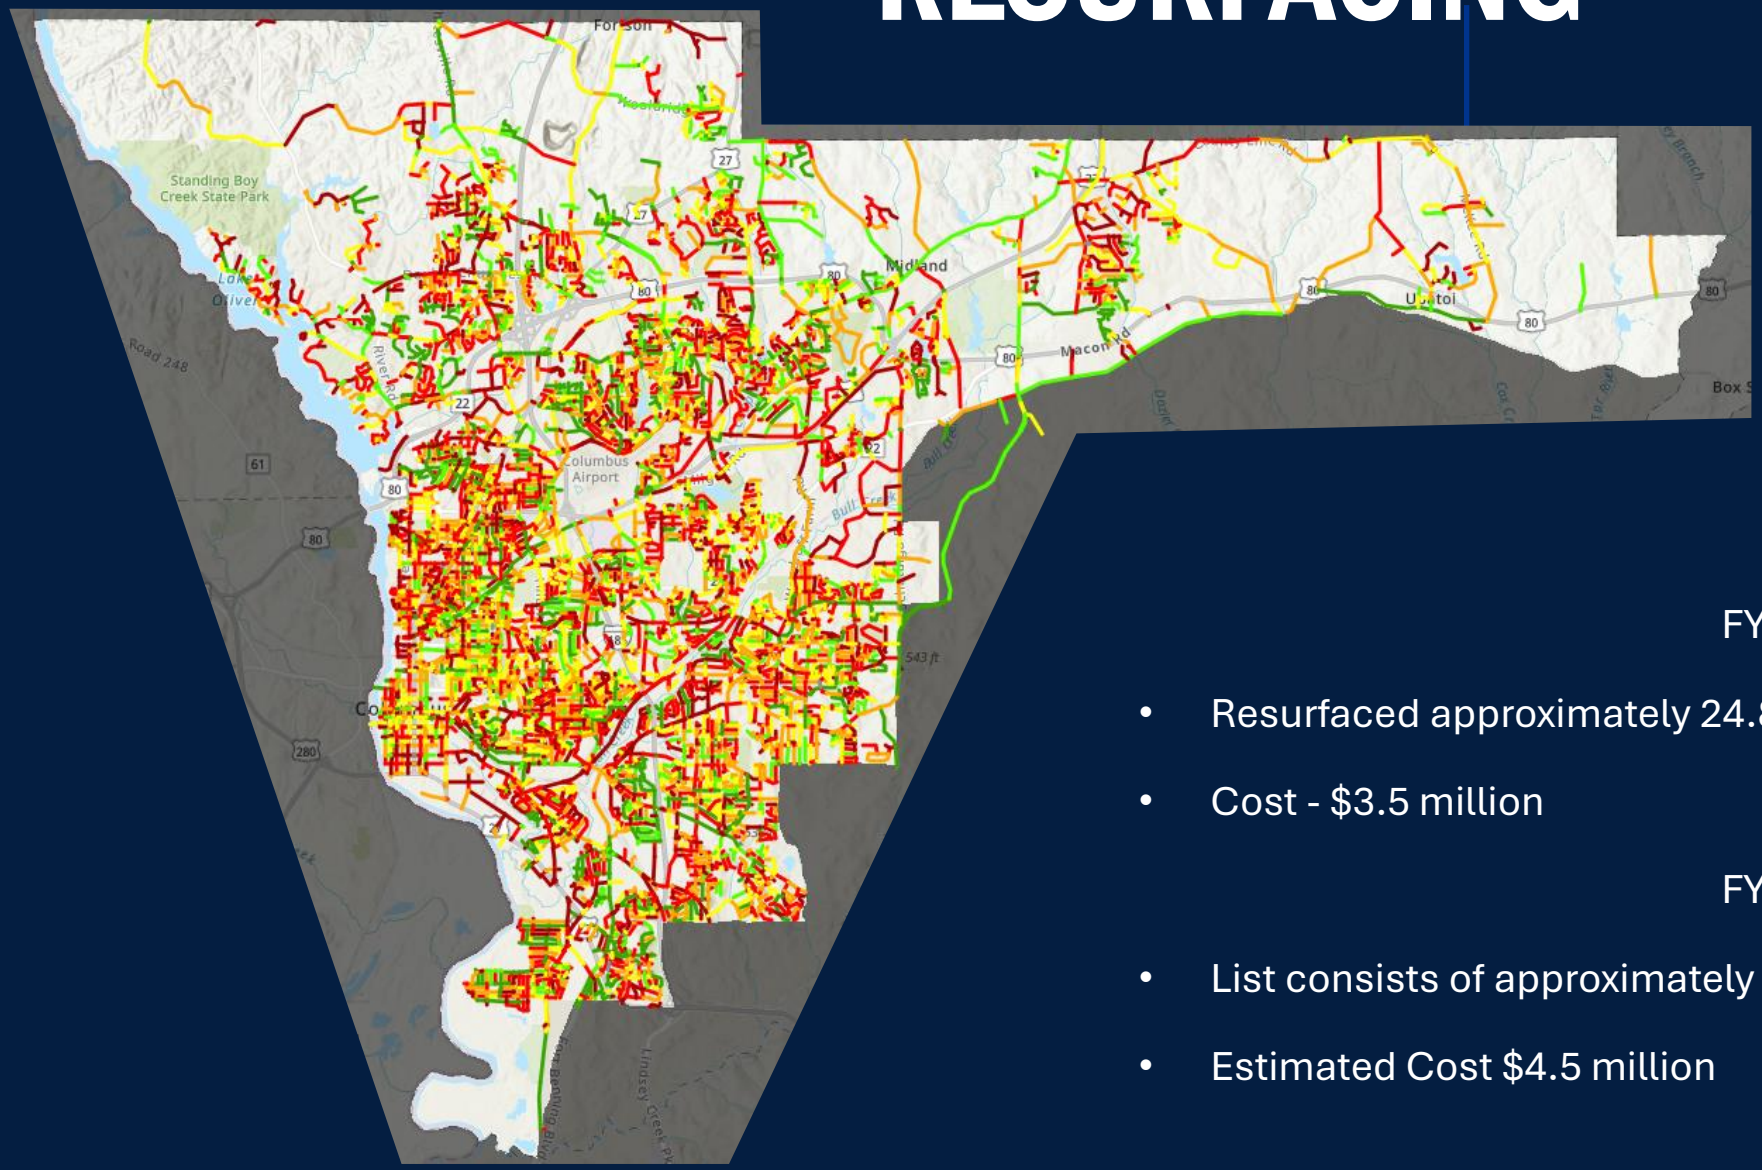

FY 25

- Resurfaced approximately 24.8 Miles.
- Cost - $3.5 million


FY 26

- List consists of approximately 26.5 Miles
- Estimated Cost $4.5 million

UPCOMING PROJECTS

DRAGONFLY TRAILS RIVER ROAD/LAKE OLIVER SEGMENT

- Approximately 1300 LF of new multi-use trail
- Approximately 3,700 LF of on-street shared-use trail
- 160 LF Pedestrian Bridge
- Bids Due on October 14th, 2027

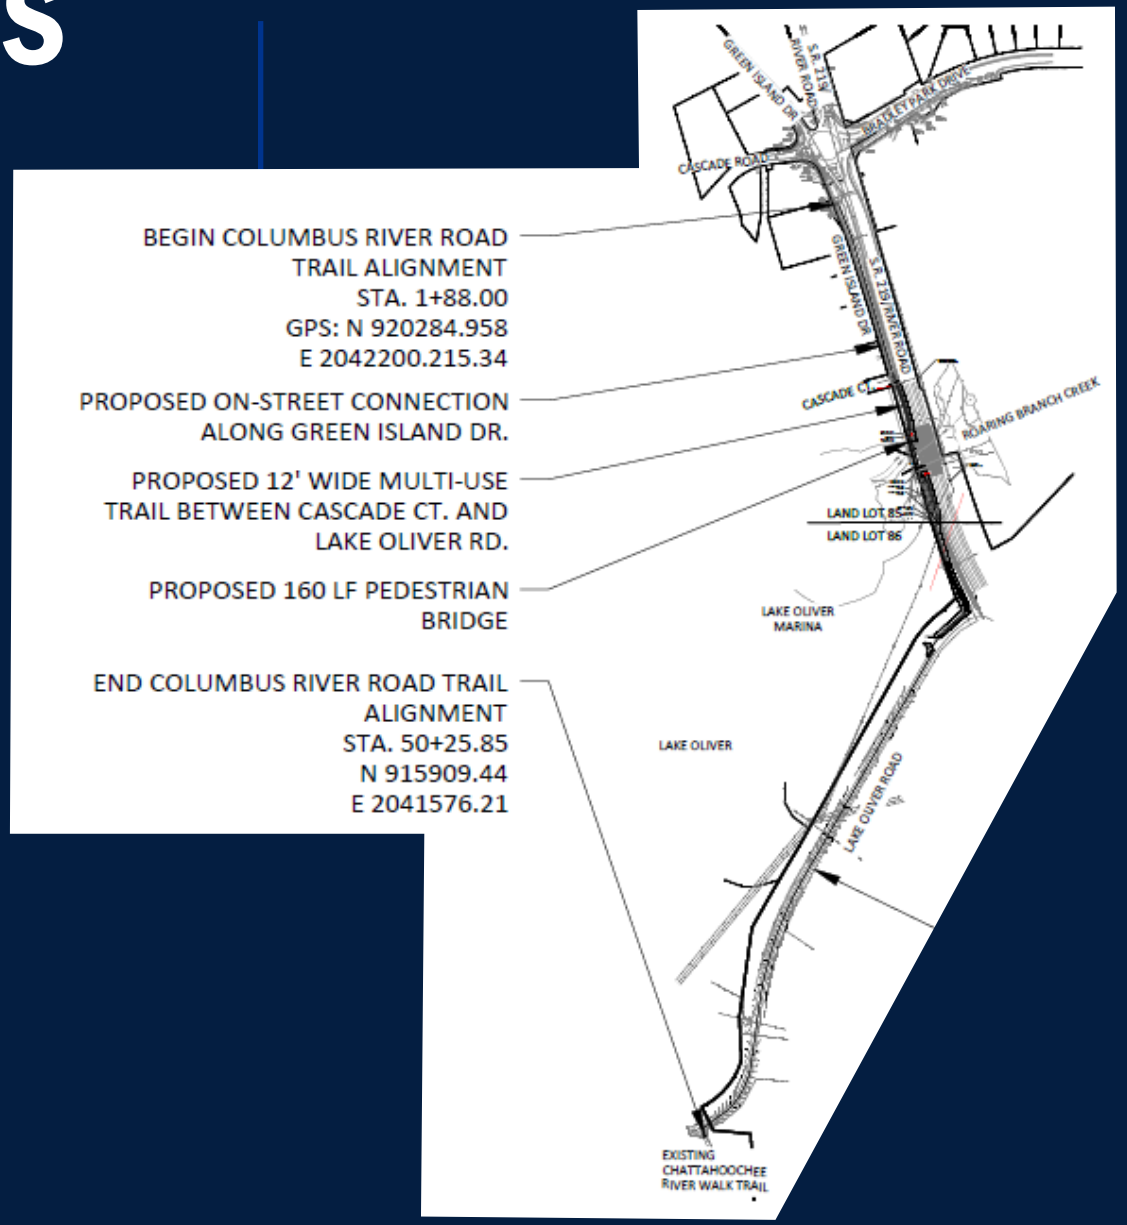

UPCOMING PROJECTS (CONT'D)

CONISHBURGH WAY CULVERT REPLACEMENT



New 9 x 6 Box Culvert

Final Plans are being prepared

Estimated Letting: December 2026

UPCOMING PROJECTS

8 STREETS RESURFACING – PI 0017691

Z230 Funding – Estimated Start – Spring 2027

- 54th Street – River Road to Veterans Parkway
- Billings Road – Warm Springs Road to Gateway Road
- Torch Hill Road – South Lumpkin Road to Fort Benning Road
- North Lumpkin Road – Cusseta to Victory Drive
- Andrews Road – Cusseta Road to Buena Vista Road
- Morris Road – Buena Vista Road to Forrest Road
- Double Churches Road – River Road to I-185 Overpass
- 30th Street – Victory Drive to Cusseta Road

TIA BAND 1 PROJECTS

STEAM MILL ROAD

Road improvements from Buena Vista Road to Pinecrest Drive with pedestrian bridge over I-185 and roundabouts at Dogwood Drive, McCartha Drive and Northstar Drive.

Est. Design Completion: December 2026

Est. Cost: $22.5M to $26M

Funding Source: FY22 TSPLOST

Critical Path: ROW Acquisition – 165 parcels: 37 agreements; 13 closed.



TIA BAND 1 PROJECTS

WHITESVILLE ROAD

Road widening will start on the north side of the bridge over SR 22/US 80/J R Allen Parkway and will end at the intersection of Williams Road. The design will go from 2 lanes to 3 lanes) with intersection improvements or roundabouts with a sidewalk and multiuse trail.

Estimated Letting: Spring 2027


Estimated Cost: $14.3 Million


ROW Acquisition: next phase



TIA BAND 1 PROJECTS

13TH AVENUE, 17TH STREET AND LINWOOD BOULEVARD ROUNDABOUT

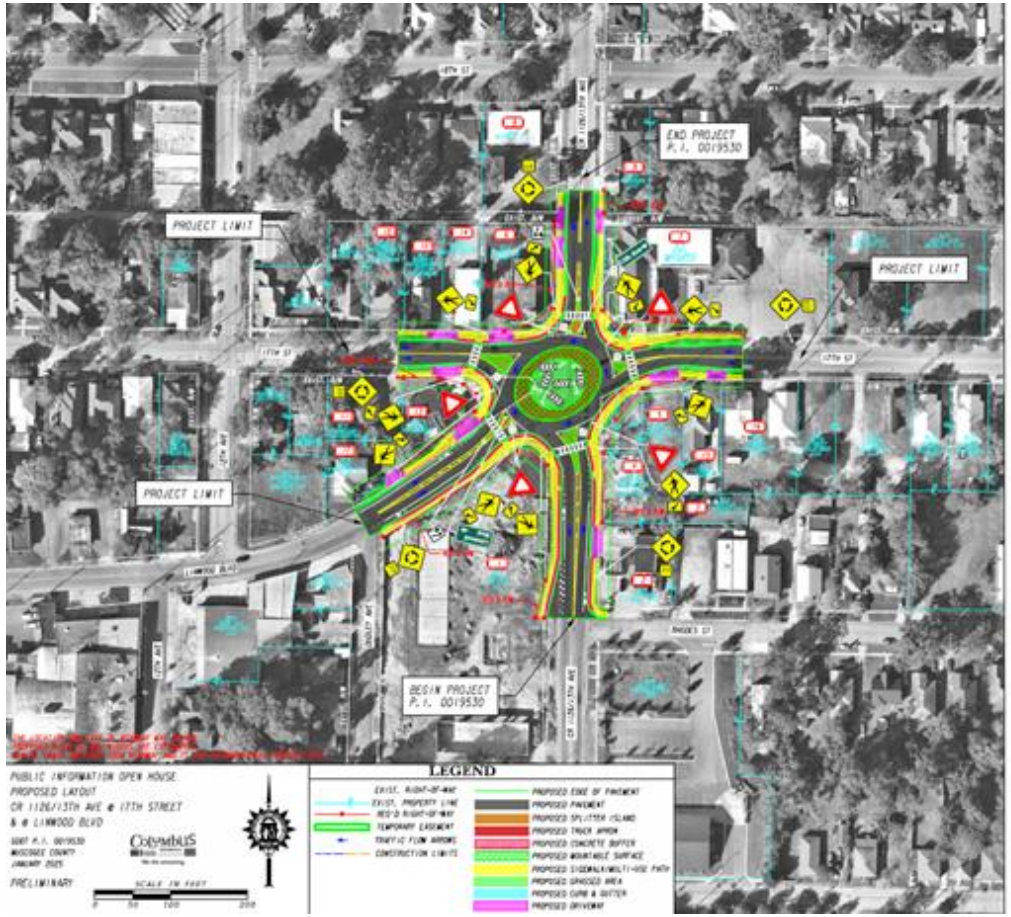

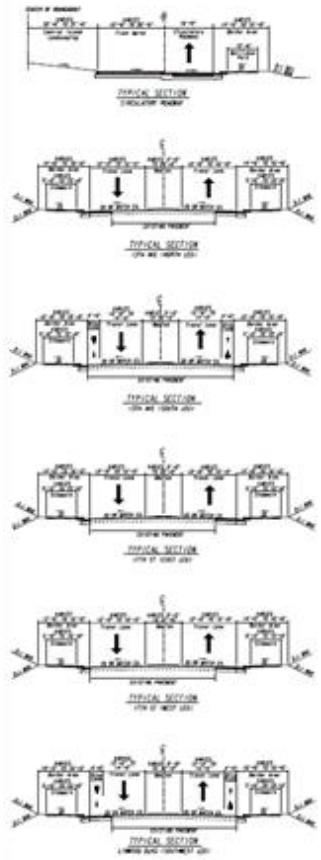

Est. Design Completion: December 2025

Funding Source: FY22 TSPLOST

Est. Cost: $6,650,000

Critical Path: ROW underway

TIA BAND 1 PROJECTS

SOUTH LUMPKIN ROAD

Project begins at the intersection of Victory Drive and terminates at the existing roundabout.

Prelim Plans expected in January

3-Lane option selected by City Council

Funding Source: FY22 TSPLOST

Estimated Cost: $9.6M (3-lane)



TIA BAND 1 PROJECTS

5TH AVENUE TRAIL EXTENSION



5th Avenue Multi-use path from 10th St. to 14th St.

Redesign to move trail to east side

Est. Design Completion: December 2025

Est. Cost: $690,000

Waiting on utility relocations on private property

TIA BAND 1 PROJECTS

BUENA VISTA ROAD CORRIDOR IMPROVEMENTS

Buena Vista Road Corridor Improvements (Widening from two and four lanes to three lanes) - from Wynnton Road to Annette Ave with sidewalks and multiuse trail.

Estimated Letting: June 2028

Estimated Cost: $10.7 Million

Prelim Field Plan Review next

START



END

TIA Band 1 Projects

- Andrews Road Improvements - (Buena Vista Road to Cusseta Road) - GDOT Administered – Under Design
- Brennan Road Improvements - (St. Mary's Road to Cusseta Road) - GDOT Administered – ROW acquisition phase
- University Avenue Road Diet- (Gentian Boulevard to Macon Road) – GDOT Administered – Concept Report approved
- Manchester Expressway @ Central Church Road Intersection Improvements – GDOT Administered – Completed
- Columbus Riverwalk Repaving and Maintenance – (CCG Scoping Project) – CCG Administered – Engineering Department working on bid package
- Liberty Theater Block Enhancement – (Streetscape improvements along 8th Avenue) - Design in progress

TIA BAND 2 PROJECTS

FORREST ROAD WIDENING


Widen Forrest Road from Macon Road to Woodruff Farm Road from 2 lanes to 3 lanes with a roundabouts at Trinity Drive, Morris Road and Avalon Road. This project will include sidewalks and multi-use trail.


Estimated Letting: 2029

Estimated Cost: $15.4 Million

Public Open House: Held August 31, 2026

START

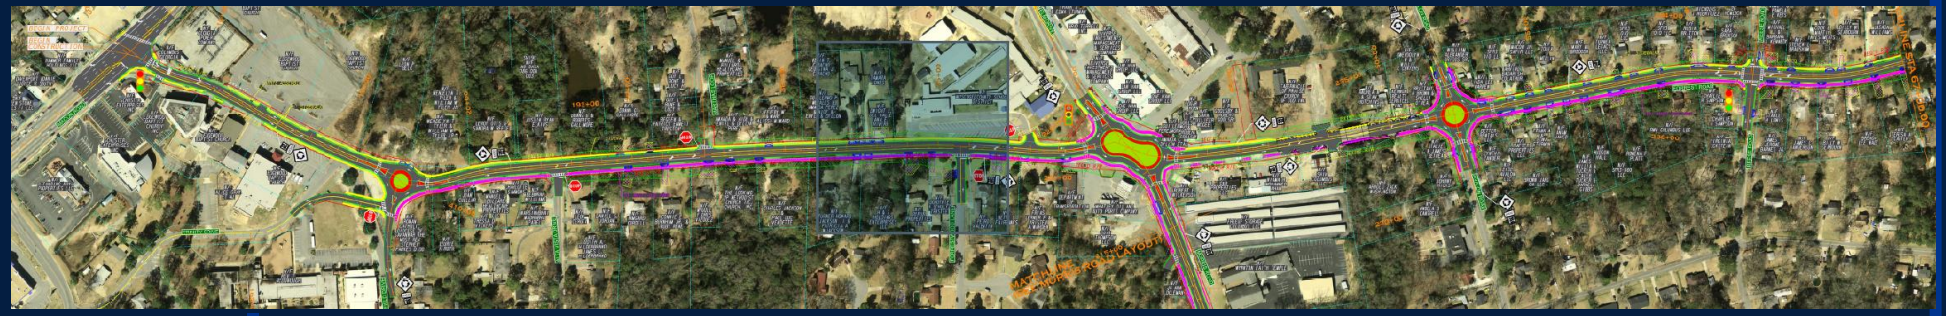

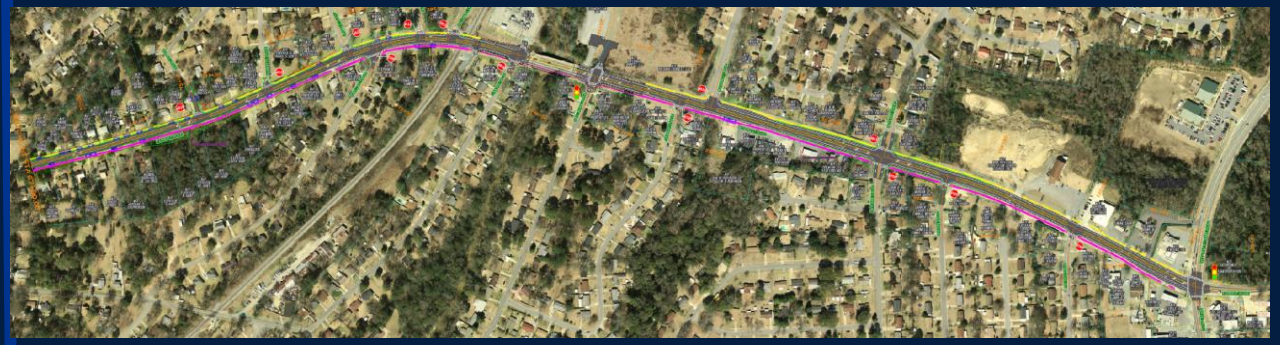

END

TIA BAND 2 PROJECTS

MORRIS ROAD WIDENING

Morris Road from Buena Vista Road to Forrest Road. Widen from 2 to 3 lanes with sidewalks, multiuse trail and landscaping

Estimated Letting: 2029

Estimated Cost: $12 Million

Public Open House held August 31, 2026

START



END

TIA BAND 2 PROJECTS

US 80 @ SCHOMBURG ROAD AND BLACKMON ROAD ITERSECTION IMPROVEMENTS





Intersection Improvements at ramp termini on US 80 at Schomburg Rd and Blackmon Rd

Est. Design Completion: 2028

Project Budget: $11,300,000

Public Open House held October 13, 2026

TIA Band 2 Projects

- Second Avenue Improvements - (Talbotton Road to Manchester Expressway) - GDOT Administered – Under Design – Letting April 2028

- Columbus Airport Improvements – CCG Administered – only $2.5 million will now go to runway

TIA BAND 3 PROJECTS

WILLIAMS ROAD WIDENING

Williams Road Widening - SR1-US 27 (Veteran's Parkway) to I-185. Widen from 2 to 3 lanes with pedestrian-bicycle amenities. Install roundabout at Williams and I-185 with pedestrian-bicycle amenities.

Estimated Letting: 2030

Estimated Cost: $18.7 Million

Public Open House held September 10, 2026


START



END

TIA BAND 3 PROJECTS

ROUNDABOUT DIAMOND INTERCHANGE US 27 ALT @ COUNTY LINE ROAD

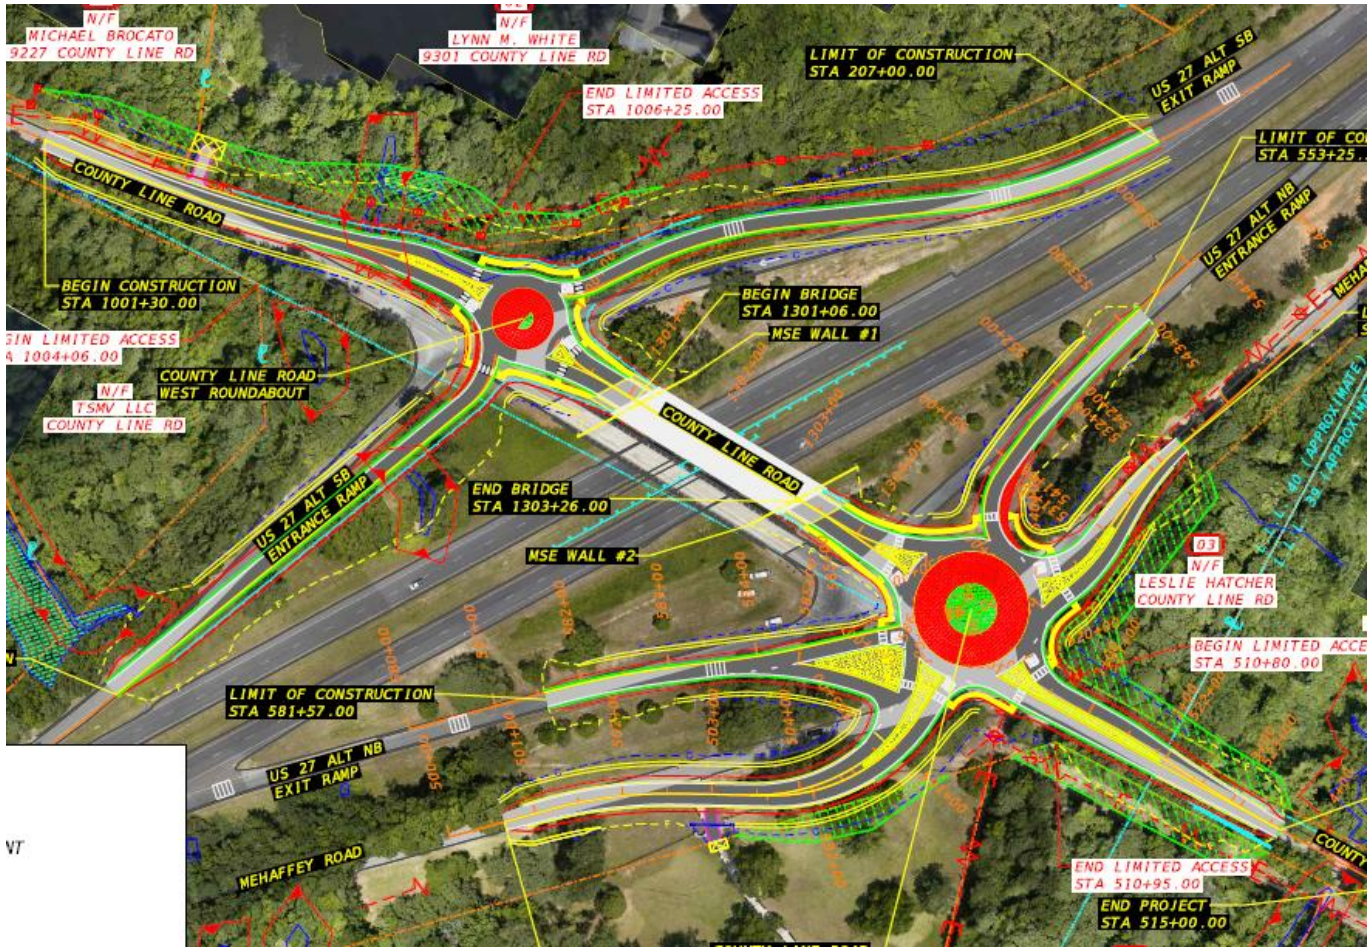

Interchange Reconstruction on Manchester Expy at County Line and Mahaffey Rd

Est. Design Completion: December 2030

Original Project Budget: $690,000

Public Open House held November 5, 2026

TIA Band 3 Projects

- Cusseta Road Widening - (10th Avenue to Roundabout) - GDOT Administered
- Double Churches Rd. Improvements - (Veterans Parkway to River Road) - CCG Administered
- Bull Creek Dragonfly Trail Connector – CWW working on sewer and trail rights
- Metra – Multi Band Projects

JOHN D. ALLEN JUDICIAL CENTER



All Courts operating in Judicial Center effective November 9, 2026.

Complete relocation estimated to be completed by December 18, 2026.

JOHN D. ALLEN JUDICIAL CENTER



JOHN D. ALLEN JUDICIAL CENTER



OTHER SPLOST PROJECTS

- Public Safety Building Renovation - $8M renovation of building constructed in 1996. Roof replacement ongoing; Interior work to start early 2027
- Golf Course Clubhouses – Oxbow Creek Renovation 95% complete; Bull Creek New Clubhouse under design
- 3 new Outdoor Pools Completed in 2025; 3 Splash Pads completed to date; 1 Splash Pad under Construction
- Trade Center Parking Garage – Under Design
- Fire Station #4 & #8 Additions/Renovations – Under Construction



Columbus GEORGIA

We do amazing.

THANK YOU

GET IN TOUCH

www.columbusga.gov

706-225-4441

1111 1st Avenue, Columbus GA, 31901
