HDR Engineering, Inc.
TBPE Firm F-754

Old Fitzhugh Rd.

ID	Task Name	Duration	Start	Finish	Pred	Successors
1	**OLD FITZHUGH ROAD**	**422 days**	**Mon 8/3/26**	**Fri 6/30/28**		
2	**TIME CALCULATOR (CALENDAR DAYS)**	**698 days**	**Mon 8/3/26**	**Fri 6/30/28**		
3	**PHASE 1**	**145 days**	**Mon 8/3/26**	**Wed 3/31/27**		**39,40**
4	BARRICADES AND TRAFFIC HANDLING	1 day	Mon 8/3/26	Mon 8/3/26		5,6
5	PLACE TCP	1 day	Tue 8/4/26	Tue 8/4/26	4	7
6	PLACE SW3P	1 day	Tue 8/4/26	Tue 8/4/26	4	7
7	PREPARING ROW	4 days	Wed 8/5/26	Mon 8/10/26	5,6	8
8	REMOVE TRT/UNT BASE & ASPH PAV	6 days	Tue 8/11/26	Wed 8/19/26	7	9,10,11,12,13,14,15,16
9	REMOV STR (PIPE)	1 day	Thu 8/20/26	Thu 8/20/26	8	17
10	REMOVING CONC (DRIVEWAYS)	1 day	Thu 8/20/26	Thu 8/20/26	8	17
11	REMOVING CONC (SIDEWALKS)	1 day	Thu 8/20/26	Thu 8/20/26	8	17
12	REMOVING CONC (CURB AND GUTTER)	1 day	Thu 8/20/26	Thu 8/20/26	8	17
13	REMOVING CONC (MISC)	1 day	Thu 8/20/26	Thu 8/20/26	8	17
14	CHAIN LINK FENCE (REMOVE)	1 day	Thu 8/20/26	Thu 8/20/26	8	17
15	RELOCATE EXISTING MAILBOX	2 days	Thu 8/20/26	Fri 8/21/26	8	17
16	REMOVAL OF PEDESTRIAN RAMPS	2 days	Thu 8/20/26	Fri 8/21/26	8	17
17	EXCAVATION (ROADWAY)	9 days	Mon 8/24/26	Thu 9/3/26	9,10,12,11,13,	18,19
18	EXCAVATION (DRAINAGE)	1 day	Fri 9/4/26	Fri 9/4/26	17	19
19	INSTALL DRAINAGE PIPE	53 days	Thu 9/10/26	Wed 12/9/26	17,18	20
20	INSTALL MANHOLES & JUNCTION BOXES	4 days	Thu 12/10/26	Tue 12/15/26	19	21
21	EMBANKMENT (ROADWAY)	2 days	Wed 12/16/26	Thu 12/17/26	20	22
22	EMBANKMENT (DRAINAGE)	1 day	Fri 12/18/26	Fri 12/18/26	21	23
23	FL BS (CMP IN PLC)(TYA GR1-2)(FNAL POS)	2 days	Mon 12/21/26	Tue 12/22/26	22	24
24	PRIME COAT (AC)	1 day	Wed 12/23/26	Wed 12/23/26	23	25
25	D-GR HMA TY-C PG76-22	1 day	Mon 12/28/26	Mon 12/28/26	24	26,34
26	INSTALL CONC CURB	17 days	Tue 12/29/26	Fri 1/22/27	25	27,28,29,30
27	INSTALL SIDEWALK & RAMPS	6 days	Mon 1/25/27	Wed 2/3/27	26	31
28	INSTALL DRIVEWAYS	4 days	Mon 1/25/27	Mon 2/1/27	26	31
29	TURNOUTS (CONC)	7 days	Mon 1/25/27	Thu 2/4/27	26	31
30	SPEED TABLE	4 days	Mon 1/25/27	Mon 2/1/27	26	31
31	CONSTRUCT INLETS	18 days	Fri 2/5/27	Thu 3/4/27	27,28,29,30	32
32	CONSTRUCT HEADWALLS	1 day	Fri 3/5/27	Fri 3/5/27	31	33,38
33	INSTALL RIPRAP	2 days	Tue 3/9/27	Wed 3/10/27	32	35,36
34	REMOVE SM RD SN SUP&AM	1 day	Tue 12/29/26	Tue 12/29/26	25	35,36
35	IN SM RD SN SUP&AM TY10BWG(1)SA(P)	1 day	Thu 3/11/27	Thu 3/11/27	33,34	37
36	TOPSOIL & HYDROSEEDING	5 days	Thu 3/11/27	Fri 3/19/27	33,34	37
37	PLACE TEMP STRIPING	1 day	Mon 3/22/27	Mon 3/22/27	35,36	39
38	INSTALL ILLUMINATION	15 days	Tue 3/9/27	Wed 3/31/27	32	39
39	**PHASE 2**	**232 days**	**Thu 4/1/27**	**Tue 4/18/28**	**38,3,37**	**76,77,78**
40	BARRICADES AND TRAFFIC HANDLING	1 day	Thu 4/1/27	Thu 4/1/27	3	41,42
41	PLACE TCP	1 day	Fri 4/2/27	Fri 4/2/27	40	43
42	PLACE SW3P	1 day	Mon 4/5/27	Mon 4/5/27	40	43
43	PREPARING ROW	1 day	Wed 4/7/27	Wed 4/7/27	41,42	44
44	INSTALL WATER LINE	80 days	Thu 4/8/27	Wed 8/25/27	43	45
45	REMOVE TRT/UNT BASE & ASPH PAV	6 days	Thu 8/26/27	Mon 9/6/27	44	46,47,48,49,50,53,51,52
46	REMOV STR (PIPE)	1 day	Tue 9/7/27	Tue 9/7/27	45	54
47	REMOVING CONC (DRIVEWAYS)	1 day	Tue 9/7/27	Tue 9/7/27	45	54
48	REMOVING CONC (SIDEWALKS)	1 day	Tue 9/7/27	Tue 9/7/27	45	54
49	REMOVING CONC (CURB AND GUTTER)	1 day	Tue 9/7/27	Tue 9/7/27	45	54
50	REMOVING CONC (MISC)	1 day	Tue 9/7/27	Tue 9/7/27	45	54
51	CHAIN LINK FENCE (REMOVE)	1 day	Tue 9/7/27	Tue 9/7/27	45	54

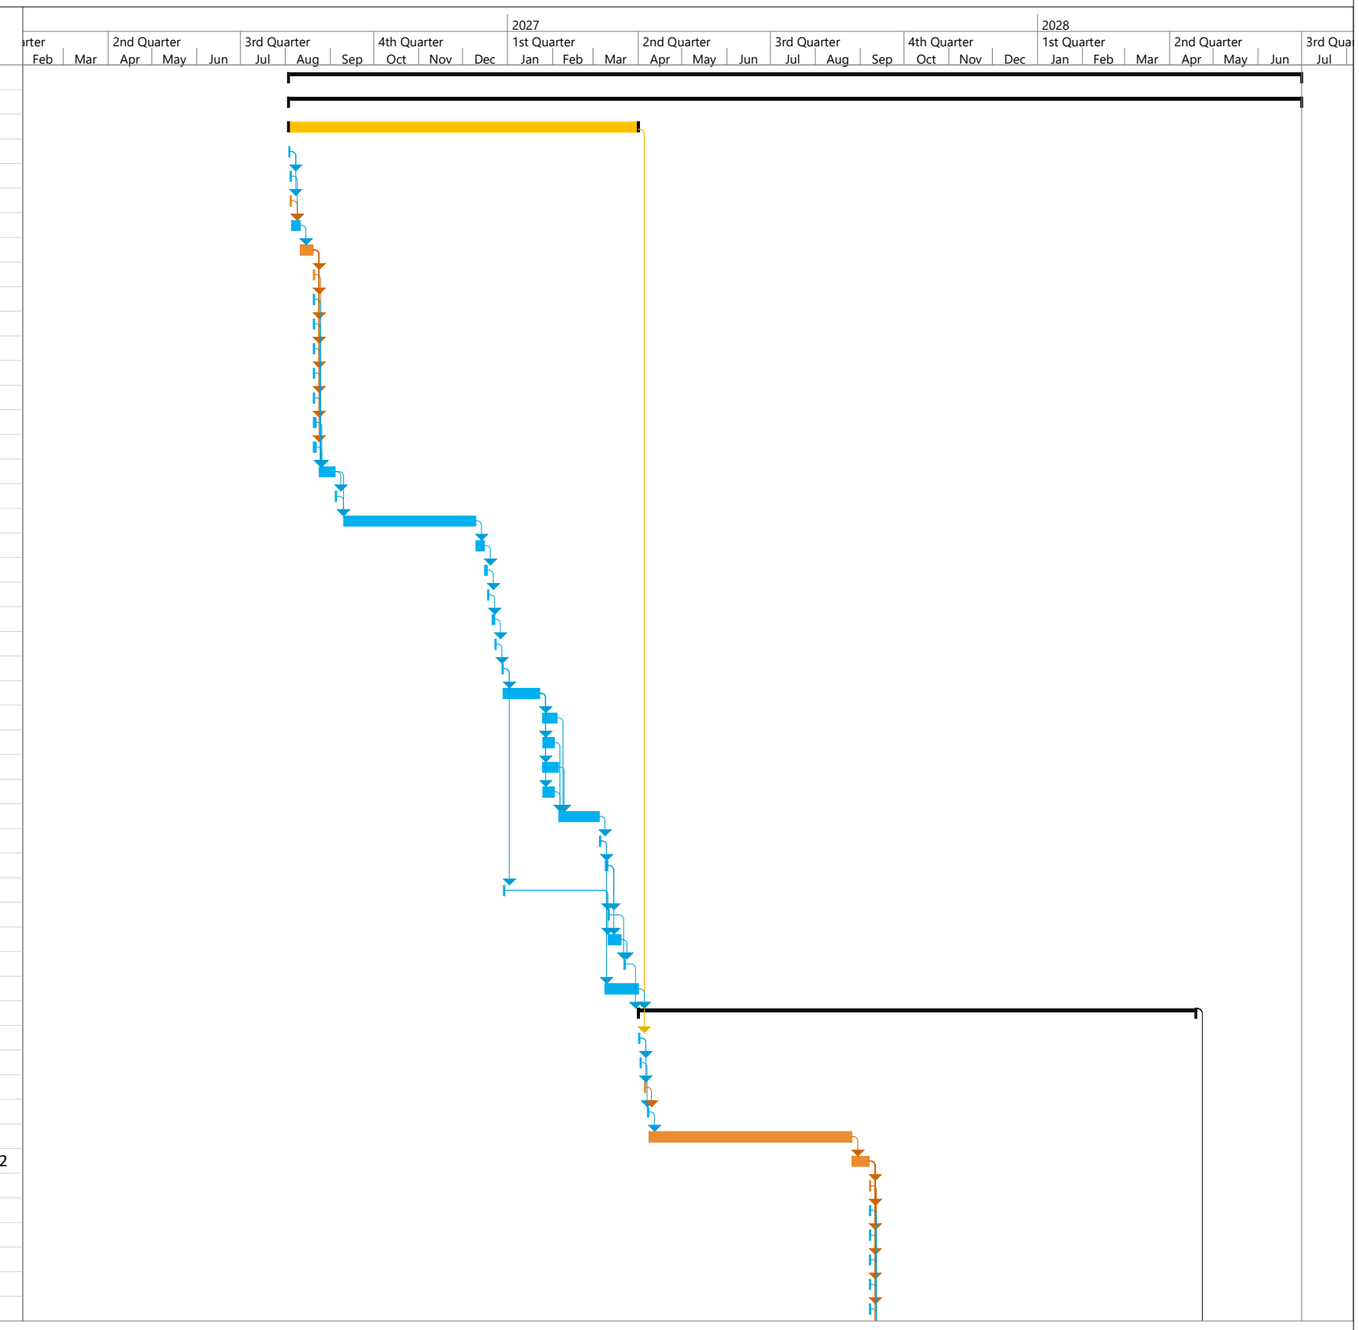

Prepared By:
Marwin Lopez, PE #131421

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

Fri 7/11/25

Jessica D Pollack 12.22.25

HDR Engineering, Inc.
TBPE Firm F-754

Old Fitzhugh Rd.

ID	Task Name	Duration	Start	Finish	Pred	Successors
52	RELOCATE EXISTING MAILBOX	2 days	Tue 9/7/27	Thu 9/9/27	45	54
53	REMOVAL OF PEDESTRIAN RAMPS	2 days	Tue 9/7/27	Thu 9/9/27	45	54
54	EXCAVATION (ROADWAY)	9 days	Fri 9/10/27	Mon 9/27/27	46,47,48,49,50	55
55	EXCAVATION (DRAINAGE)	1 day	Tue 9/28/27	Tue 9/28/27	54	56
56	INSTALL DRAINAGE PIPE	53 days	Wed 9/29/27	Mon 12/27/27	55	57
57	INSTALL MANHOLES & JUNCTION BOXES	4 days	Tue 12/28/27	Fri 12/31/27	56	58
58	EMBANKMENT (ROADWAY)	2 days	Mon 1/3/28	Tue 1/4/28	57	59
59	EMBANKMENT (DRAINAGE)	1 day	Wed 1/5/28	Wed 1/5/28	58	60
60	FL BS (CMP IN PLC)(TYA GR1-2)(FNAL POS)	2 days	Thu 1/6/28	Fri 1/7/28	59	61
61	PRIME COAT (AC)	1 day	Mon 1/10/28	Mon 1/10/28	60	62
62	D-GR HMA TY-C PG76-22	1 day	Tue 1/11/28	Tue 1/11/28	61	63
63	INSTALL CONC CURB	17 days	Wed 1/12/28	Tue 2/8/28	62	64,65,66,67,71
64	INSTALL SIDEWALK & RAMPS	6 days	Wed 2/9/28	Fri 2/18/28	63	68
65	INSTALL DRIVEWAYS	4 days	Wed 2/9/28	Wed 2/16/28	63	68
66	TURNOUTS (CONC)	7 days	Wed 2/9/28	Mon 2/21/28	63	68
67	SPEED TABLE	4 days	Wed 2/9/28	Wed 2/16/28	63	68
68	CONSTRUCT INLETS	18 days	Tue 2/22/28	Mon 3/20/28	64,66,67,65	69
69	CONSTRUCT HEADWALLS	1 day	Wed 3/22/28	Wed 3/22/28	68	70,75
70	INSTALL RIPRAP	2 days	Thu 3/23/28	Fri 3/24/28	69	72,73
71	REMOVE SM RD SN SUP&AM	1 day	Wed 2/9/28	Wed 2/9/28	63	72,73
72	IN SM RD SN SUP&AM TY10BWG(1)SA(P)	1 day	Mon 3/27/28	Mon 3/27/28	71,70	74
73	TOPSOIL & HYDROSEEDING	5 days	Mon 3/27/28	Fri 3/31/28	71,70	74
74	PLACE TEMP STRIPING	1 day	Wed 4/5/28	Wed 4/5/28	73,72	76
75	INSTALL ILLUMINATION	15 days	Thu 3/23/28	Tue 4/18/28	69	76
76	**PHASE 3**	**5 days**	**Wed 4/19/28**	**Tue 4/25/28**	**39,75,74**	**82,83,84**
77	PLACE TCP	1 day	Wed 4/19/28	Wed 4/19/28	39	79
78	PLACE SW3P	1 day	Wed 4/19/28	Wed 4/19/28	39	79
79	PLACE FINAL LIFT OF ASPHALT	2 days	Thu 4/20/28	Fri 4/21/28	77,78	80,81
80	PLACE FINAL STRIPING	1 day	Mon 4/24/28	Mon 4/24/28	79	
81	IN SM RD SN SUP&AM TY10BWG(1)SA(P)	2 days	Mon 4/24/28	Tue 4/25/28	79	82
82	**PHASE 4**	**40 days**	**Wed 4/26/28**	**Fri 6/30/28**	**76,81**	
83	PLACE TCP	1 day	Wed 4/26/28	Wed 4/26/28	76	85
84	PLACE SW3P	1 day	Wed 4/26/28	Wed 4/26/28	76	85
85	CONSTRUCT SIDEWALK EXTENSION	2 days	Thu 4/27/28	Fri 4/28/28	83,84	86
86	BIKE RACK	2 days	Fri 5/5/28	Mon 5/8/28	85	87
87	PET STATION	1 day	Tue 5/9/28	Tue 5/9/28	86	88
88	TRASH RECEPTACLES	1 day	Wed 5/10/28	Wed 5/10/28	87	89
89	INSTALL BENCHES	10 days	Thu 5/11/28	Wed 5/24/28	88	90
90	INSTALL FLAGSTONE PAVING	7 days	Thu 5/25/28	Wed 6/7/28	89	91
91	INSTALL TREES & LANDSCAPE PLANTING	10 days	Thu 6/8/28	Thu 6/22/28	90	92
92	INSTALL IRRIGATION	5 days	Fri 6/23/28	Thu 6/29/28	91	93
93	PERFORM FINAL CLEANUP	1 day	Fri 6/30/28	Fri 6/30/28	92	
94						
95						
96						
97						
98						
99						

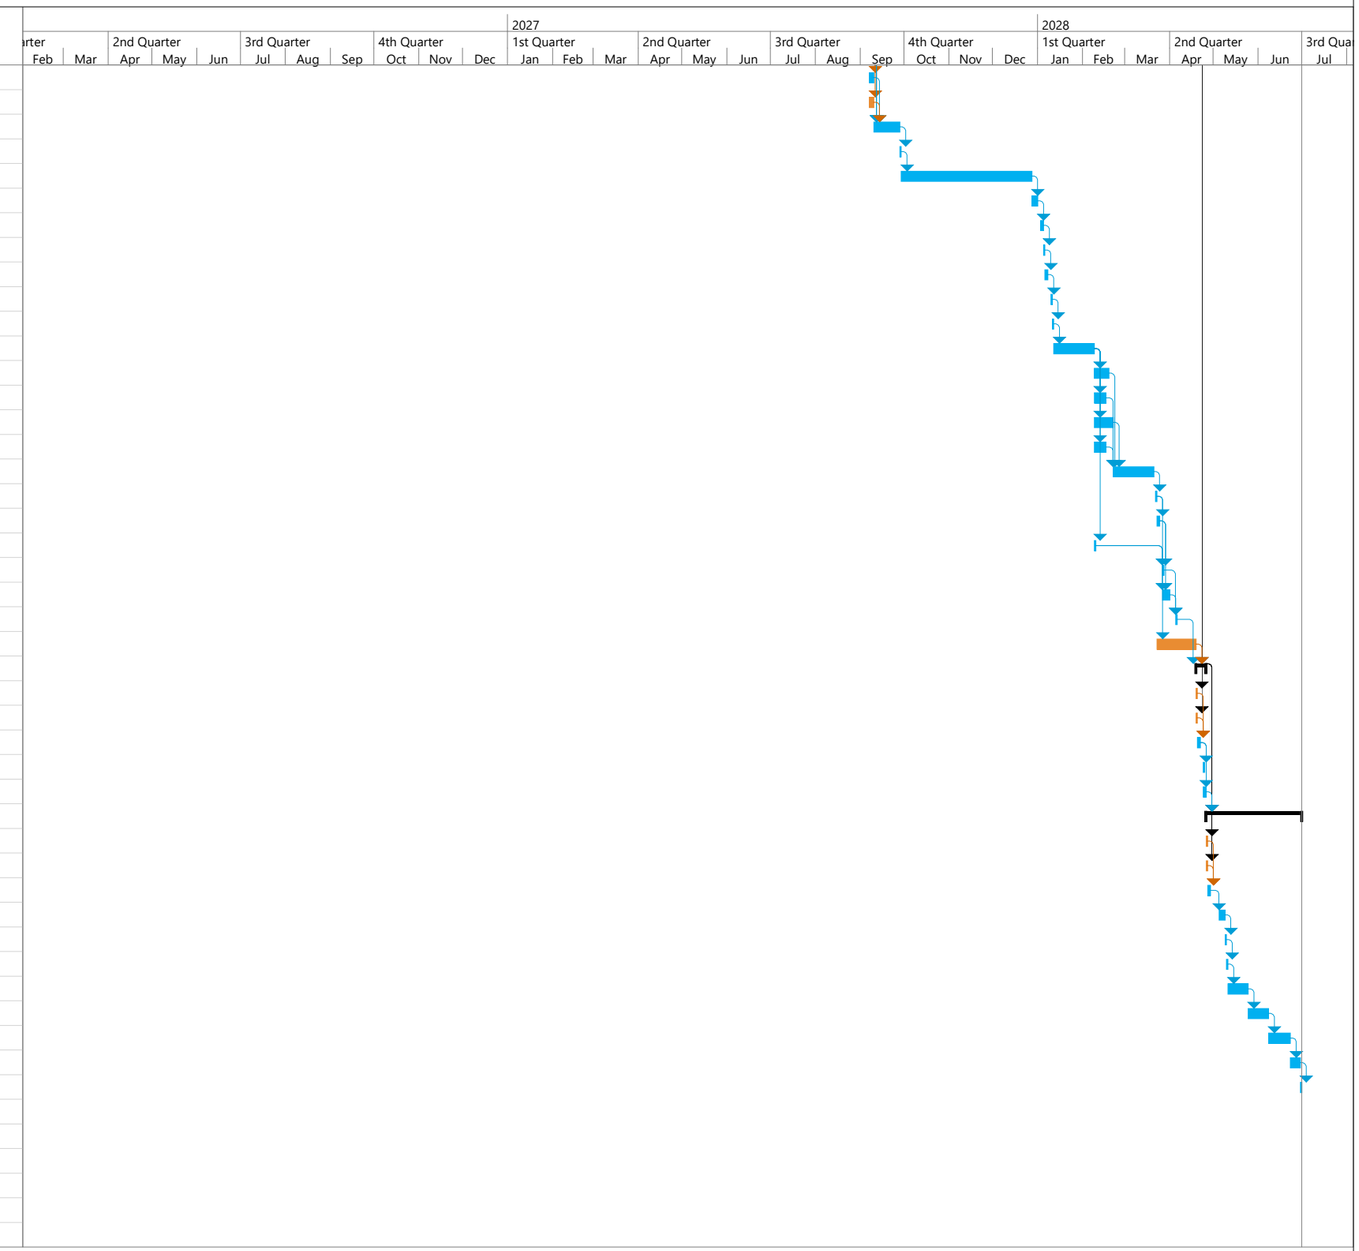

Prepared By:
Marwin Lopez, PE #131421

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

Fri 7/11/25

Jessica D Pollack 12.22.25
