
OLD FITZHUGH RD

PRE-LIMINARY BASELINE SCHEDULE

Lone★Star Sitework

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish
DRIPPING SPRINGS OLD FITZHUGH RD		507	507	0%	16-Nov-26	24-Oct-28
A1000	NTP	0	0	0%	16-Nov-26*	
A1010	Set PCMS	0	0	0%	16-Nov-26*	
A1040	Set Lead-in Barricades	1	1	0%	16-Nov-26	16-Nov-26
DRIPPING SPRINGS.1 PHASE 1		164	164	0%	17-Nov-26	02-Jul-27
A1020	Install Erosion Control	5	5	0%	17-Nov-26	23-Nov-26
A1030	Install 4" HDPE Temp Water Line w/ Permanent Long Services	15	15	0%	24-Nov-26	14-Dec-26
A1050	Install Phase 1 Traffic Control	1	1	0%	15-Dec-26	15-Dec-26
A1060	Excavation of Existing NB Lane	15	15	0%	15-Dec-26	04-Jan-27
A1070	Install Storm Drain A	81	81	0%	05-Jan-27	27-Apr-27
A1080	Construct NB Old Fitzhugh Rd Flex Base	10	10	0%	28-Apr-27	11-May-27
A1090	Concrete Curb	22	22	0%	12-May-27	10-Jun-27
A1100	Concrete Driveway	10	10	0%	11-Jun-27	24-Jun-27
A1110	1st Lift of Asphalt	2	2	0%	25-Jun-27	28-Jun-27
A1115	Exposed Aggregate Concrete Sidewalk	6	6	0%	25-Jun-27	02-Jul-27
DRIPPING SPRINGS.2 PHASE 2		304	304	0%	29-Jun-27	25-Aug-28
A1120	Install Phase 2 Traffic Control	1	1	0%	29-Jun-27	29-Jun-27
A1130	Construct Dripping Springs Water - Water Line	80	80	0%	29-Jun-27	18-Oct-27
A1140	Remove Existing Dripping Springs Water Water Line	31	31	0%	19-Oct-27	30-Nov-27
A1150	Excavation of Existing SB Lane	15	15	0%	01-Dec-27	21-Dec-27
A1160	Install Storm Drain B	91	91	0%	22-Dec-27	26-Apr-28
A1170	Construct NB Old Fitzhugh Rd Flex Base	10	10	0%	27-Apr-28	10-May-28
A1180	Concrete Curb	22	22	0%	11-May-28	09-Jun-28
A1190	Concrete Driveway	30	30	0%	12-Jun-28	21-Jul-28
A1210	1st Lift of Asphalt	2	2	0%	24-Jul-28	25-Jul-28
A1215	Exposed Aggregate Concrete Sidewalk	25	25	0%	24-Jul-28	25-Aug-28
DRIPPING SPRINGS.3 PHASE 3		5	5	0%	28-Aug-28	01-Sep-28
A1220	Install Final Lift of Asphalt Pavement	2	2	0%	28-Aug-28	29-Aug-28
A1240	Pavement Marking & Signage	3	3	0%	30-Aug-28	01-Sep-28
DRIPPING SPRINGS.4 PHASE 4		40	40	0%	30-Aug-28	24-Oct-28
A1230	Construct Sidewalk Extension to Roger Hanks Pkwy	7	7	0%	30-Aug-28	07-Sep-28
A1250	Install Hardscape & Landscape	40	40	0%	30-Aug-28	24-Oct-28
A1260	Substantial Completion	0	0	0%		24-Oct-28

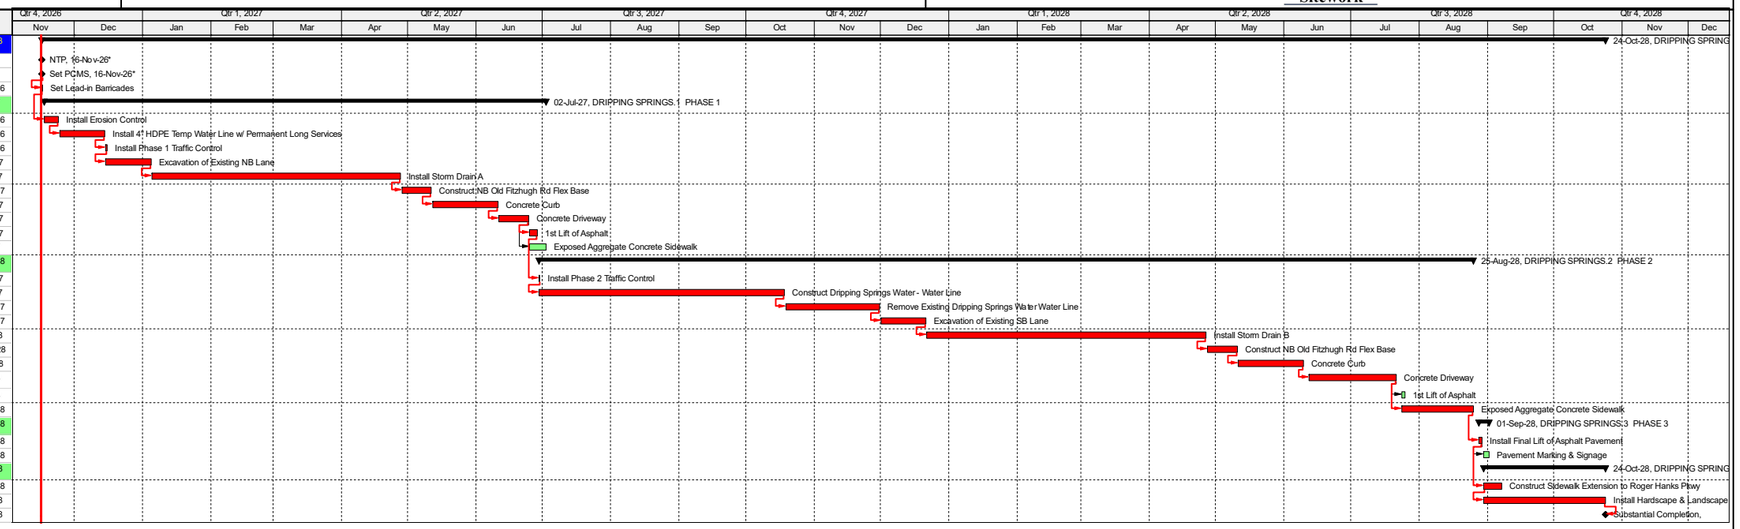

Date	Revision	Checked	Approved
23-Oct-26	PRELIMINARY BASELINE SCHEDULE		
