| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 1 | ***CR 57 Roadway Expansion*** | 435 days | Mon 7/15/24 | Fri 3/13/26 | |
| 2 | **CR 57 Phase 1 (Caldwell Crossing)** | 223 days | Mon 7/15/24 | Wed 5/21/25 | |
| 3 | **Design** | 30 days | Mon 7/15/24 | Fri 8/23/24 | |
| 4 | Roadway Plans | 30 days | Mon 7/15/24 | Fri 8/23/24 | |
| 5 | Submittal | 0 days | Fri 8/23/24 | Fri 8/23/24 | 4 |
| 6 | Agency Review & Address Comments | 25 days | Mon 8/26/24 | Fri 9/27/24 | 5 |
| 7 | Agency Approval | 10 days | Mon 9/30/24 | Fri 10/11/24 | 6 |
| 8 | Advertisement | 21 days | Mon 9/30/24 | Mon 10/28/24 | 6,7FS-10 days |
| 9 | Award Contracts | 19 days | Tue 10/29/24 | Fri 11/22/24 | 8 |
| 10 | **Construction (120/140 Calendar Days)** | 101 days | Mon 11/25/24 | Mon 4/14/25 | |
| 11 | Roadway Construction | 95 days | Mon 11/25/24 | Fri 4/4/25 | 9 |
| 12 | Stage II WSD | 6 days | Mon 4/7/25 | Mon 4/14/25 | 11 |
| 13 | **Construction Done/Inspection Scheduled** | **0 days** | **Mon 4/14/25** | **Mon 4/14/25** | 12 |
| 14 | Punchlist Items | 28 days | Mon 4/14/25 | Wed 5/21/25 | 13FS-1 day |
| 15 | **Acceptance of CR 57 Phase 1** | **0 days** | **Wed 5/21/25** | **Wed 5/21/25** | **14** |
| 16 | | | | | |
| 17 | **CR 57 Phase 2 (Caldwell Lakes)** | 283 days | Mon 11/11/24 | Wed 12/10/25 | |
| 18 | **Design** | 30 days | Mon 11/11/24 | Fri 12/20/24 | |
| 19 | Roadway& Signal Plans | 30 days | Mon 11/11/24 | Fri 12/20/24 | 4FS+55 days |
| 20 | Submittal | 0 days | Fri 12/20/24 | Fri 12/20/24 | 19 |
| 21 | Agency Review & Address Comments | 25 days | Mon 12/23/24 | Fri 1/24/25 | 20 |
| 22 | Agency Approval | 10 days | Mon 1/27/25 | Fri 2/7/25 | 21 |
| 23 | Advertisement | 21 days | Mon 2/10/25 | Mon 3/10/25 | 22,21 |
| 24 | Award Contracts | 19 days | Tue 3/11/25 | Fri 4/4/25 | 23 |
| 25 | **Construction (140/210 Calendar Days)** | 151 days | Mon 4/7/25 | Mon 11/3/25 | |
| 26 | **Roadway Construction** | **101 days** | **Mon 4/7/25** | **Mon 8/25/25** | 22,24,11 |
| 27 | Signal Construction | 145 days | Mon 4/7/25 | Fri 10/24/25 | 24 |
| 28 | Stage II WSD | 6 days | Mon 10/27/25 | Mon 11/3/25 | 27 |
| 29 | **Construction Done/Inspection Scheduled** | **0 days** | **Mon 11/3/25** | **Mon 11/3/25** | 28 |
| 30 | Punchlist Items | 28 days | Mon 11/3/25 | Wed 12/10/25 | 29FS-1 day |
| 31 | **Acceptance of CR 57 Phase 2** | **0 days** | **Wed 12/10/25** | **Wed 12/10/25** | **30** |
| 32 | | | | | |
| 33 | **CR 57 Phase 3 (Offsite)** | 280 days | Mon 2/17/25 | Fri 3/13/26 | |
| 34 | **Design** | 40 days | Mon 2/17/25 | Fri 4/11/25 | |
| 35 | Roadway Plans | 40 days | Mon 2/17/25 | Fri 4/11/25 | 19FS+40 days |
| 36 | Submittal | 0 days | Fri 4/11/25 | Fri 4/11/25 | 35 |
| 37 | Agency Review & Address Comments | 30 days | Mon 4/14/25 | Fri 5/23/25 | 36 |
| 38 | Agency Approval | 20 days | Mon 5/26/25 | Fri 6/20/25 | 37 |
| 39 | Advertisement | 28 days | Mon 5/26/25 | Wed 7/2/25 | 37 |
| 40 | Award Contracts | 32 days | Thu 7/3/25 | Fri 8/15/25 | 39 |
| 41 | **Construction (140/160 Calendar Days)** | 116 days | Mon 8/25/25 | Mon 2/2/26 | |
| 42 | Roadway Construction | 110 days | Mon 8/25/25 | Fri 1/23/26 | 40,26FS-1 day |
| 43 | Stage II WSD | 6 days | Mon 1/26/26 | Mon 2/2/26 | 42 |
| 44 | **Construction Done/Inspection Scheduled** | **0 days** | **Mon 2/2/26** | **Mon 2/2/26** | 43 |
| 45 | Punchlist Items | 30 days | Mon 2/2/26 | Fri 3/13/26 | 44FS-1 day |
| 46 | **Acceptance of CR 57 Phase 3** | **0 days** | **Fri 3/13/26** | **Fri 3/13/26** | **45** |

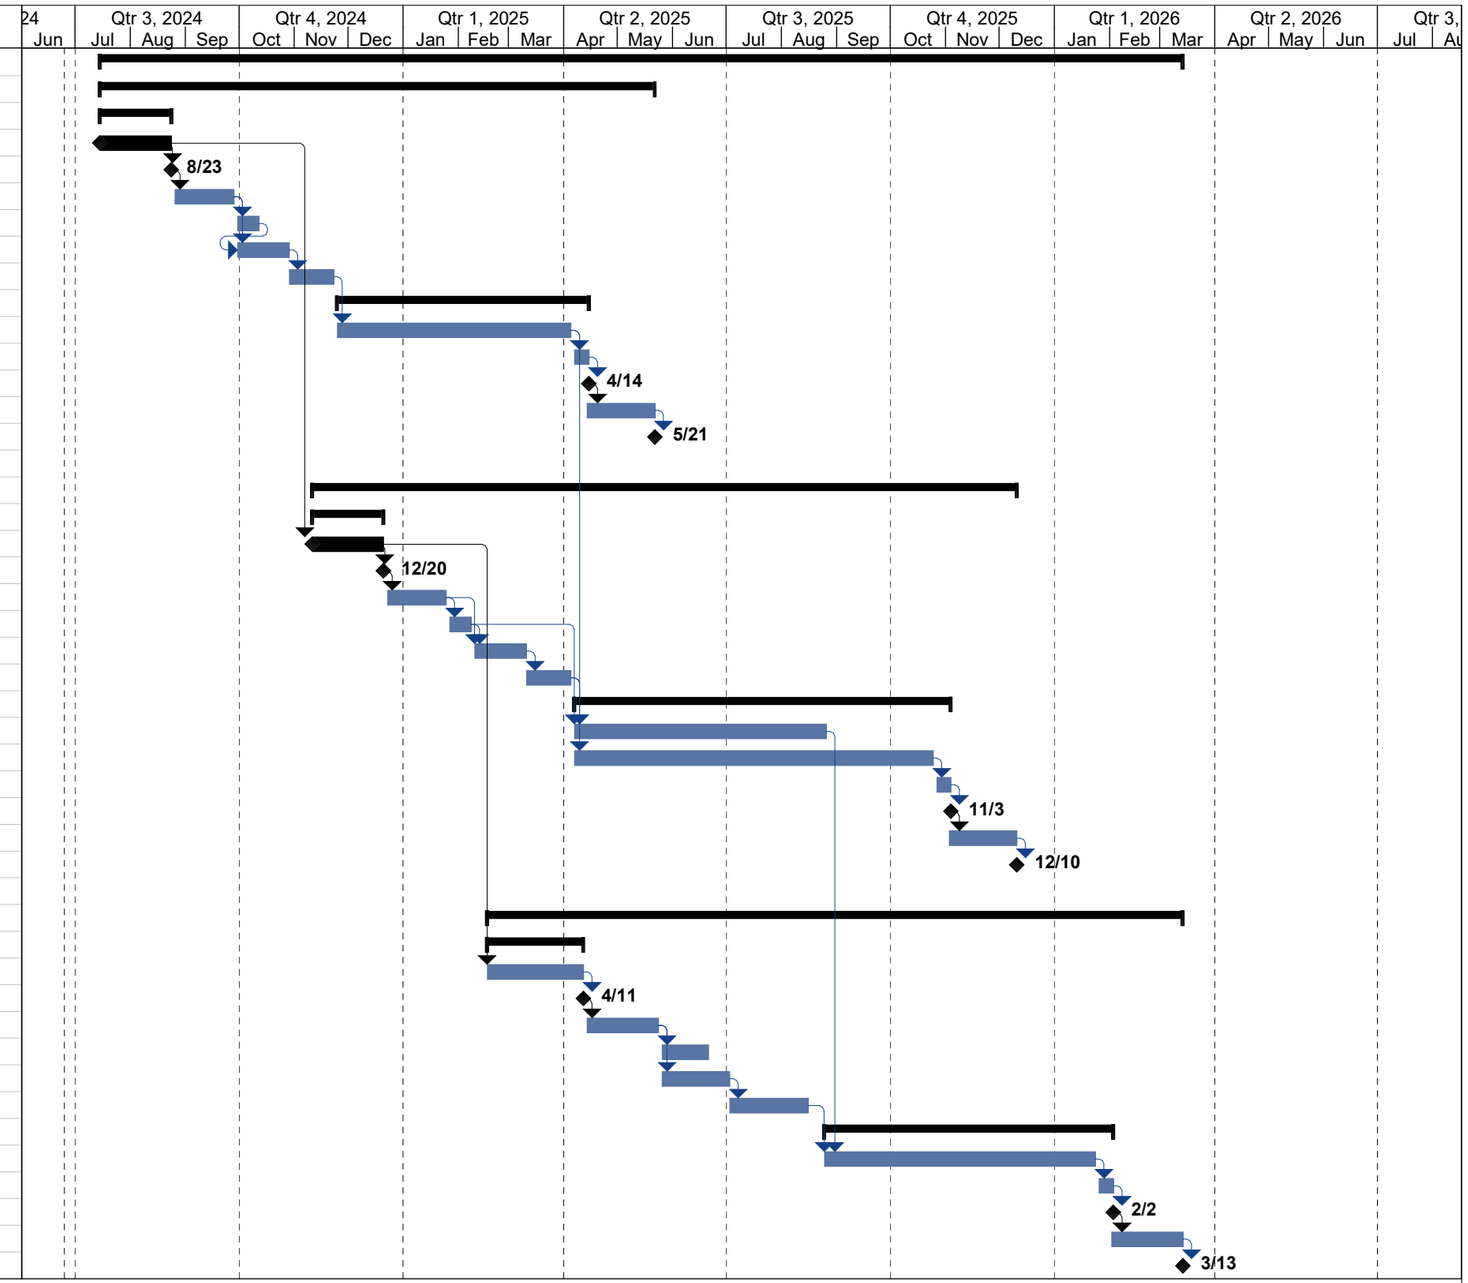


Project: Caldwell Crossing/Caldwell La
Date: Tue 6/25/24

| | | | | |
|---|---|---|---|---|
| Task | Rolled Up Split | External Milestone | Manual Summary Rollup | External Milestone |
| Split | Rolled Up Milestone | Inactive Milestone | Manual Summary | Progress |
| Milestone | Rolled Up Progress | Inactive Summary | Start-only | Deadline |
| Summary | External Tasks | Manual Task | Finish-only | |
| Rolled Up Task | Project Summary | Duration-only | External Tasks | |



\\ljaeng.com\Shares\Work\LAND\4025\BC MUD 87\Agreements\County Road 57 Expansion Schedule.mpp
