ID	Task Name	Resource Names	Duration	Start	Finish
1	**Local Roads**	**Rent A Flash**	**41 days**	**Tue 5/27/25**	**Wed 7/23/25**
2	Mobilization/Traffic & Erosion Control	Ridge,Rent A Flash	1 day	Tue 5/27/25	Tue 5/27/25
3	**Pinedale Lane**		**39 days**	**Wed 5/28/25**	**Tue 7/22/25**
4	Pulverize/Knockdown/Compact	Haas	1 day	Wed 5/28/25	Wed 5/28/25
5	Grade & Balance Road	Haas	2 days	Thu 5/29/25	Fri 5/30/25
6	Install Cross Drains (7EA)	Haas	2 days	Wed 6/4/25	Thu 6/5/25
7	Fine Grade/Sawcut	Haas	1 day	Mon 7/7/25	Mon 7/7/25
8	Pave Binder Asphalt	American	1 day	Tue 7/8/25	Tue 7/8/25
9	Adjustments (7 WVs- 7 MHs)	Haas	2 days	Wed 7/9/25	Thu 7/10/25
10	Pave Surface Asphalt	American	1 day	Fri 7/11/25	Fri 7/11/25
11	Shouldering	Haas	1 day	Tue 7/22/25	Tue 7/22/25
12	**Windwood Road**		**39 days**	**Wed 5/28/25**	**Tue 7/22/25**
13	Pulverize/Knockdown/Compact	Haas	1 day	Wed 5/28/25	Wed 5/28/25
14	Grade & Balance Road	Haas	1 day	Fri 5/30/25	Fri 5/30/25
15	Install Cross Drains (4 EA)	Haas	1 day	Fri 6/6/25	Fri 6/6/25
16	Fine Grade/Sawcut	Haas	1 day	Mon 7/7/25	Mon 7/7/25
17	Pave Binder Asphalt	American	1 day	Tue 7/8/25	Tue 7/8/25
18	Adjustments (3 MHs)	Haas	1 day	Wed 7/9/25	Wed 7/9/25
19	Pave Surface Asphalt	American	1 day	Fri 7/11/25	Fri 7/11/25
20	Shouldering	Haas	1 day	Tue 7/22/25	Tue 7/22/25
21	**Oakdale Ln & Wedgewood**		**39 days**	**Thu 5/29/25**	**Wed 7/23/25**
22	Pulverize/Knockdown/Compact	Haas	1 day	Thu 5/29/25	Thu 5/29/25
23	Grade & Balance Road	Haas	2 days	Mon 6/2/25	Tue 6/3/25
24	Install Cross Drains (7EA)	Haas	2 days	Mon 6/9/25	Tue 6/10/25
25	Fine Grade/Sawcut	Haas	1 day	Tue 7/8/25	Tue 7/8/25
26	Pave Binder Asphalt	American	1 day	Wed 7/9/25	Wed 7/9/25
27	Adjustments (2WVs- 7 MHs)	Haas	1 day	Thu 7/10/25	Thu 7/10/25
28	Pave Surface Asphalt	American	2 days	Mon 7/14/25	Tue 7/15/25
29	Shouldering	Haas	1 day	Wed 7/23/25	Wed 7/23/25
30	**Sedona CT**		**39 days**	**Thu 5/29/25**	**Wed 7/23/25**
31	Pulverize/Knockdown/Compact	Haas	1 day	Thu 5/29/25	Thu 5/29/25
32	Grade & Balance Road	Haas	1 day	Tue 6/3/25	Tue 6/3/25
33	Install Cross Drains (7EA)	Haas	1 day	Wed 6/11/25	Wed 6/11/25
34	Fine Grade/Sawcut	Haas	1 day	Wed 7/9/25	Wed 7/9/25
35	Pave Binder Asphalt	American	1 day	Wed 7/9/25	Wed 7/9/25
36	Adjustments (1 WVs- 4 MHs)	Haas	1 day	Thu 7/10/25	Thu 7/10/25
37	Pave Surface Asphalt	American	1 day	Mon 7/14/25	Mon 7/14/25
38	Shouldering	Haas	1 day	Wed 7/23/25	Wed 7/23/25
39	**Kronenwetter Drive 90+22 - 201+45**		**69 days**	**Mon 6/2/25**	**Mon 9/8/25**
40	Mobilization/Traffic & Erosion Control/Staking	Haas	1 day	Mon 6/2/25	Mon 6/2/25
41	Pulverize/Knockdown/Compact	Haas	6 days	Mon 6/2/25	Mon 6/9/25
42	Base Course	Haas	9 days	Tue 6/10/25	Fri 6/20/25
43	Fine Grade/Sawcut	Haas	3 days	Mon 6/23/25	Wed 6/25/25
44	Pave Binder Asphalt	American	2 days	Thu 6/26/25	Fri 6/27/25
45	Pave Surface Asphalt	American	2 days	Wed 8/27/25	Thu 8/28/25
46	Shouldering	Haas	3 days	Thu 9/4/25	Mon 9/8/25
47					
53	**Indianhead Drive/Kronenwetter Drive 0+30 - 36+09**		**43 days**	**Mon 6/23/25**	**Thu 8/21/25**
54	Mobilization/Traffic & Erosion Control/Staking	Haas,Rent A Flash,Ridge	1 day	Mon 6/23/25	Mon 6/23/25
55	Pulverize (1200SY)	Haas	2 days	Mon 6/23/25	Tue 6/24/25
56	Remove Pulverized Salvaged Base Course	Haas	4 days	Tue 6/24/25	Fri 6/27/25
57	Common Excavation	Haas	15 days	Mon 6/30/25	Mon 7/21/25
58	Fabric & Breaker Run	Haas	15 days	Mon 7/7/25	Fri 7/25/25
59	Base Course	Haas	10 days	Mon 7/14/25	Fri 7/25/25
60	Concrete Bridge Approaches	Pember	3 days	Mon 7/28/25	Wed 7/30/25
61	Fine Grade/Sawcut	Haas	3 days	Wed 8/6/25	Fri 8/8/25
63	Pave Binder Asphalt	American	2 days	Mon 8/11/25	Tue 8/12/25
64	Adjustments (13 MHs - 11 WVs)	Haas	3 days	Wed 8/13/25	Fri 8/15/25
62	Pave Surface Asphalt	American	2 days	Mon 8/18/25	Tue 8/19/25
65	Shouldering	Haas	2 days	Wed 8/20/25	Thu 8/21/25
48					
49	**Kronenwetter Drive 38+61-62+36 & 64+23-90+22**		**17 days**	**Tue 8/19/25**	**Thu 9/11/25**
50	1.5" Milling	All States	4 days	Tue 8/19/25	Fri 8/22/25
51	1.5" Asphalt	American	2 days	Wed 8/27/25	Thu 8/28/25
52	Shouldering	Haas	3 days	Tue 9/9/25	Thu 9/11/25
66	**Entire Job**		**1 day**	**Fri 9/12/25**	**Fri 9/12/25**
67	Pavement Marking	Brickline	1 day	Fri 9/12/25	Fri 9/12/25

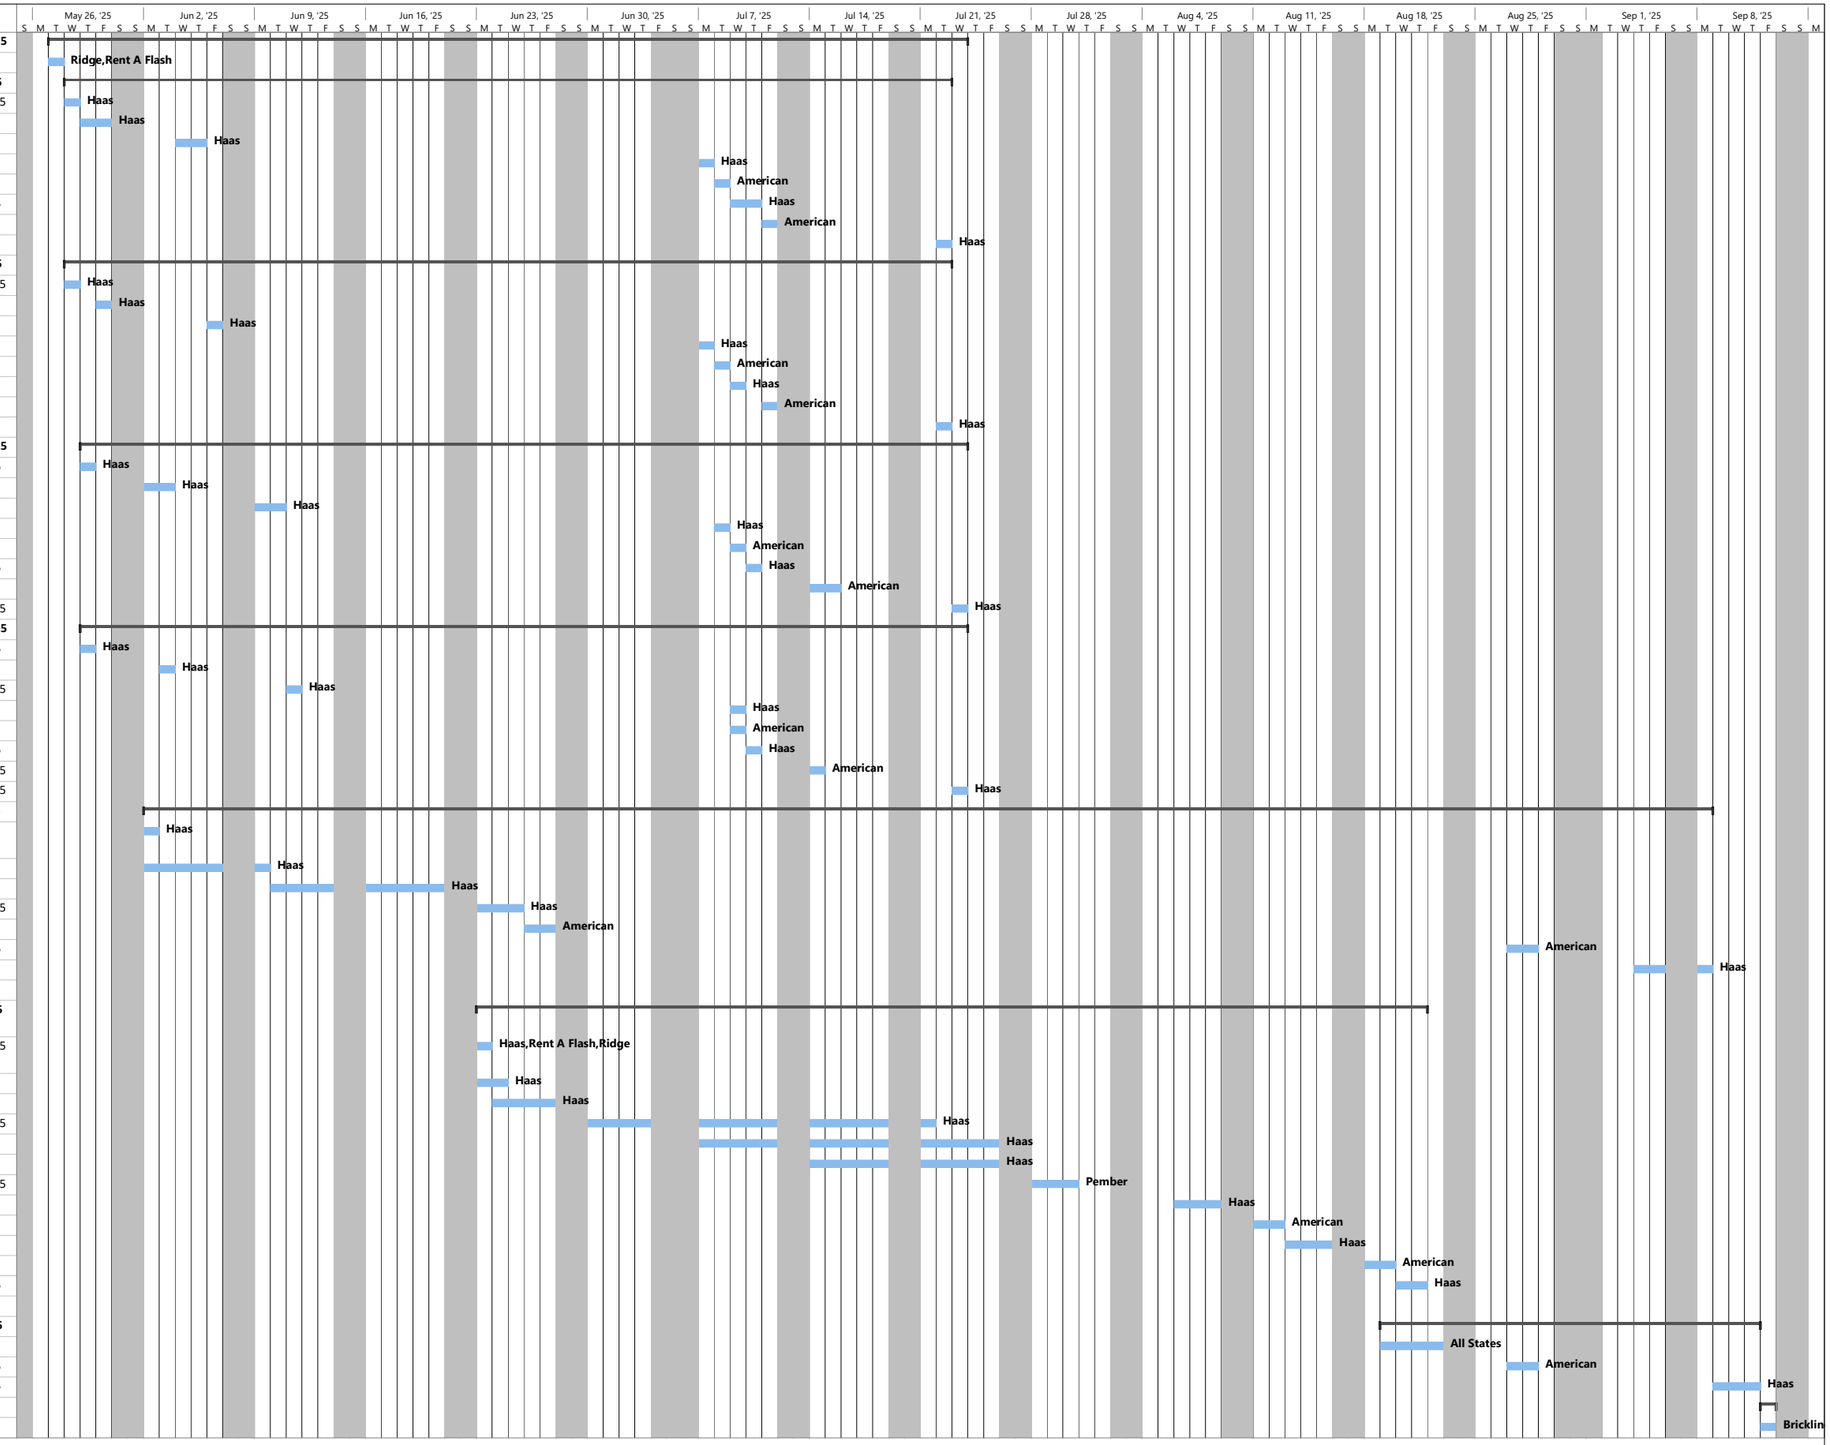

Project: Kronenwetter 2025 Roa
Date: Wed 5/21/25

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
