PROJECT TITLE	Town Of RObbins 2023 Water System Improvements	COMPANY NAME	ELJ, Inc.
PROJECT MANAGER	Aaron Maready & Trent Jones	DATE	12/22/25
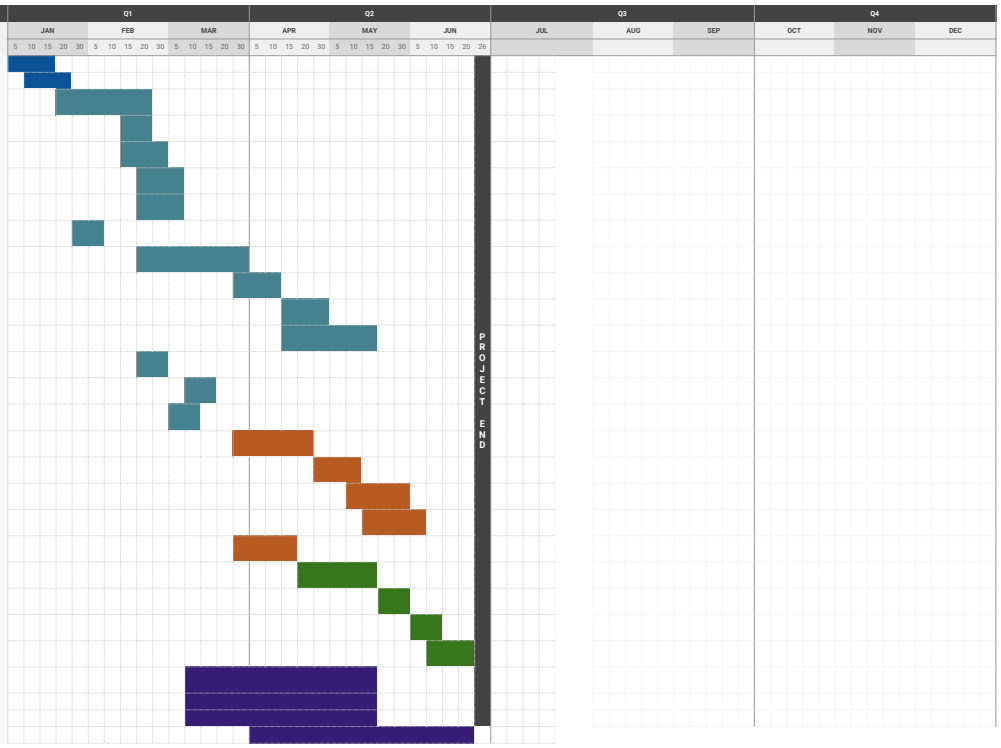
PHASE	DETAILS		
1	Mobilization & Recieve Materials	Start: 1/5/26	Finish: 1/9/26
	Locate & Pothole utilities	Start: 1/12/26	Finish: 1/23/26
2	Install Waterline from station 0+00 to 52+67.96 S. Middleton	Start: 1/19/26	Finish: 2/20/26
	Install directional drill at station +/- 16+00	Start: 2/16/26	Finish: 2/20/26
	Testing station 0+00 to 52+67.86 S Middleton	Start: 2/16/26	Finish: 2/24/26
	Service Connections 0+00 to 52+67. 96 S Middleton	Start: 2/23/26	Finish: 3/6/26
	Seed/Straw/Fertilize 0+00 to 52+67. 96 S Middleton	Start: 2/23/26	Finish: 3/6/26
	Install bore & jack at station +/- 48+00 Railroad	Start: 1/30/26	Finish: 2/6/26
	Install Waterline from station 0+00 to 32+48.92 E. Hemp	Start: 2/23/26	Finish: 3/27/26
	Testing Station 0+00 to 32+48.92 E Hemp	Start: 3/27/26	Finish: 4/10/26
	Service Connections 0+00 to 32+48. 92 E Hemp	Start: 4/13/26	Finish: 4/30/26
	Seed/Straw/Fertilize 0+00 to 32+48. 92 E Hemp	Start:4/13/26	Finish: 5/15/26
	Install bore & Jack at station 0+00 ross street	Start: 2/23/26	Finish: 2/27/26
	Install bore & Jack at currie baptist station 22+01	Start: 3/9/26	Finish: 3/13/26
	Install bore & Jack at S. Emma ln 26+01	Start: 3/2/26	Finish: 3/6/26
3	Install Waterline from 0+00 to 15+46. 68 W. Magnolia	Start: 3/30/26	Finish: 4/24/26
	Testing Station 0+00 to 15+46.68 W Magnolia	Start: 4/27/26	Finish: 5/8/26
	Service Connections 0+00 to 15+46. 68 W Magnolia	Start: 5/11/26	Finish: 5/29/26
	Seed/Straw/Fertilize 0+00 to 15+46. 68 W Magnolia	Start: 5/18/26	Finish: 6/5/26
	Install Bore & Jack at NW Broad station 15+00	Start: 3/30/26	Finish: 4/13/26
4	Install Waterline 0+00 to 4+25 E Elm Street	Start: 4/26/26	Finish: 5/15/26
	Testing Station 0+00 to 4+25 E Elm Street	Start: 5/18/26	Finish: 5/29/26
	Service Connections 0+00 to 4+25 E Elm Street	Start: 6/1/26	Finish: 6/12/26
	Seed/Straw/Fertilize 0+00 to 4+25 E Elm Street	Start: 6/8/26	Finish: 6/19/26
5	Removal & Replacement of Firehydrants on existing Lines	Start: 3/9/26	Finish: 5/15/26
	Install Valves N Moore every 3,000'	Start: 3/9/26	Finish: 5/15/26
	Install Fire Hydrants on Existing Lines	Start: 3/9/26	Finish: 5/15/26
	Meter Install & Network	Start: 4/6/26	Finish: 6/26/26
