CITY OF SONORA
SNELL ROAD RECONSTRUCTION PROJECT

ID	Task Name	Duration	Start	Finish	Predecessors	Successors
1	**Notice to Proceed**	0 days	Tue 4/16/24	Tue 4/16/24		5,3,4FS+5 days
2	**Project Management**	**300 days**	**Tue 4/16/24**	**Mon 6/9/25**		
3	Project Management	60 wks	Tue 4/16/24	Mon 6/9/25	1	
4	Kick Off Meeting	0 days	Mon 4/22/24	Mon 4/22/24	1FS+5 days	7,8,12,28,15,19
5	PDT Meetings	60 wks	Tue 4/16/24	Mon 6/9/25	1	
6	**Surveying/Mapping**	**31 days**	**Tue 4/23/24**	**Tue 6/4/24**		
7	Research Background Information	3 days	Tue 4/23/24	Thu 4/25/24	4	
8	Site Investigation	1 day	Tue 4/23/24	Tue 4/23/24	4	9
9	Topographic Survey and Mapping	25 days	Wed 4/24/24	Tue 5/28/24	8	31,10FF
10	Map Existing R/W	15 days	Wed 5/8/24	Tue 5/28/24	9FF	13
11	Existing Utility Mapping	31 days	Tue 4/23/24	Tue 6/4/24		
12	Utility Verification Letter	1 wk	Tue 4/23/24	Mon 4/29/24	4	13
13	Map Existing Utilities	1 wk	Wed 5/29/24	Tue 6/4/24	12,10	
14	**Field Investigation/Geotechnical Research**	**33 days**	**Tue 4/23/24**	**Thu 6/6/24**		
15	Research Background Information	3 days	Tue 4/23/24	Thu 4/25/24	4	16
16	Geotechnical Field Investigation	20 days	Fri 4/26/24	Thu 5/23/24	15	17
17	Pavement Design Memo	10 days	**Fri 5/24/24**	Thu 6/6/24	16	31FF
18	**Environmental Analysis**	**100 days**	**Tue 4/23/24**	**Mon 9/9/24**		
19	Project Description	10 days	Tue 4/23/24	Mon 5/6/24	4	20,21
20	Record Searches (biology, cultural, hazards)	8 wks	Tue 5/7/24	Mon 7/1/24	19	21
21	Draft CEQA CE	15 days	Tue 7/2/24	Mon 7/22/24	19,20	22
22	City Review CEQA CE	20 days	Tue 7/23/24	Mon 8/19/24	21	23
23	Revise CEQA CE	5 days	Tue 8/20/24	Mon 8/26/24	22	24
24	City Review and Approve CEQA CE	5 days	Tue 8/27/24	Mon 9/2/24	23	25
25	City Files CE with County Clerk and SCH	5 days	Tue 9/3/24	Mon 9/9/24	24	
26	**Preliminary Engineering**	**66 days**	**Tue 4/23/24**	**Tue 7/23/24**		
27	30% Plans and Estimate	66 days	Tue 4/23/24	Tue 7/23/24		
28	Roadway Design	2 wks	Tue 4/23/24	Mon 5/6/24	4	29
29	Drainage Design	1 wk	Tue 5/7/24	Mon 5/13/24	28	30,31
30	30% Cross-Sections	1 wk	Tue 5/14/24	Mon 5/20/24	29	31
31	Prepare 30% Plans	20 days	Wed 5/29/24	Tue 6/25/24	9,30,29,17FF	32FF,33SS
32	Prepare 30% Estimate	5 days	Wed 6/19/24	Tue 6/25/24	31FF	33SS
33	QA/QC 30% and Make Revisions	5 days	Wed 6/19/24	Tue 6/25/24	31SS,32SS	34
34	***Submit 30% PS&E***	***0 days***	***Tue 6/25/24***	***Tue 6/25/24***	33	35
35	***City Review 30% Plans and Estimate***	***20 days***	***Wed 6/26/24***	***Tue 7/23/24***	34	37
36	**Final Design**	**84 days**	**Wed 7/24/24**	**Mon 11/18/24**		
37	30% Constructability Review Meeting	1 day	Wed 7/24/24	Wed 7/24/24	35	38
38	Revision Roadway Design	2 wks	Thu 7/25/24	Wed 8/7/24	37	40
39	60% Plans, Specifications, and Estimate	37 days	Thu 8/8/24	Fri 9/27/24		
40	Draft Response to Comments	2 days	Thu 8/8/24	Fri 8/9/24	38	41
41	60% Plans	20 days	Mon 8/12/24	Fri 9/6/24	40	42FF,43FF,45FF
42	60% Specifications	1 wk	Mon 9/2/24	Fri 9/6/24	41FF	45FF
43	60% Estimate	1 wk	Mon 9/2/24	Fri 9/6/24	41FF	
44	60% Update Cross-Sections	2 wks	Mon 8/26/24	Fri 9/6/24	41FF	45FF
45	QA/QC 60% Plans and Incorporate Revisions	5 days	Mon 9/2/24	Fri 9/6/24	41FF,42FF,44FF	46
46	***Submit 60% PS&E***	0 wks	Fri 9/6/24	Fri 9/6/24	45	47
47	***City Review 60% Plans, Specs, and Estimate***	3 wks	Mon 9/9/24	Fri 9/27/24	46	49
48	90% Plans, Specifications, and Estimate	31 days	Mon 9/30/24	Mon 11/11/24		
49	60% Constructability Review Meeting	1 day	Mon 9/30/24	Mon 9/30/24	47	50,51
50	Draft Response to Comments	2 days	Tue 10/1/24	Wed 10/2/24	49	
51	90% Plans	15 days	Tue 10/1/24	Mon 10/21/24	49	55FF,52FF,53FF
52	90% Specifications	1 wk	Tue 10/15/24	Mon 10/21/24	51FF	
53	90% Estimate	1 wk	Tue 10/15/24	Mon 10/21/24	51FF	
54	90% Cross-Sections	1 wk	Tue 10/15/24	Mon 10/21/24	51FF	
55	QA/QC 90% Plans and Incorporate Revisions	1 wk	Tue 10/15/24	Mon 10/21/24	51FF	56
56	***Submit 90% PS&E***	0 wks	Mon 10/21/24	Mon 10/21/24	55	57
57	***City Review 90% PS&E***	3 wks	Tue 10/22/24	Mon 11/11/24	56	59,60,61
58	100% Plans, Specifications, and Estimate (Final)	5 days	Tue 11/12/24	Mon 11/18/24		
59	90% Constructability Review Meeting	1 day	Tue 11/12/24	Tue 11/12/24	57	
60	Draft Response to Comments	1 day	Tue 11/12/24	Tue 11/12/24	57	
61	100% Plans	5 days	Tue 11/12/24	Mon 11/18/24	57	62FF,63FF,64FF
62	100% Specifications	2 days	Fri 11/15/24	Mon 11/18/24	61FF	64FF
63	100% Estimate	2 days	Fri 11/15/24	Mon 11/18/24	61FF	64FF
64	QA/QC 100% Plans and Incorporate Revisions	2 days	Fri 11/15/24	Mon 11/18/24	61FF,62FF,63FF	65
65	***Submit 100% PS&E (Final)***	0 wks	Mon 11/18/24	Mon 11/18/24	64	68,67,70
66	**Right of Way**	**20 days**	**Tue 11/19/24**	**Mon 12/16/24**		
67	Prepare and Submit R/W Certification to Caltrans	5 days	Tue 11/19/24	Mon 11/25/24	65	68
68	Caltrans Review and Approves R/W Certification	15 days	Tue 11/26/24	Mon 12/16/24	67,65	70
69	**Construction Support**	**146 days**	**Tue 12/17/24**	**Tue 7/8/25**		
70	City Council Approval to Advertise	10 days	Tue 12/17/24	Mon 12/30/24	65,68	71
71	Advertising Period	30 days	Tue 12/31/24	Mon 2/10/25	70	72SF+10 days,7
72	Pre-Bid Meeting	1 day	Mon 1/13/25	Mon 1/13/25	71SF+10 days	
73	Bid Opening	1 day	Tue 2/11/25	Tue 2/11/25	71	74
74	Award Construction Contract	30 days	Wed 2/12/25	Tue 3/25/25	73	75
75	Begin Construction	0 days	Tue 3/25/25	Tue 3/25/25	74	76
76	Construction Support	60 days	Wed 3/26/25	Tue 6/17/25	75	77
77	Prepare Record Drawings	15 days	Wed 6/18/25	Tue 7/8/25	76	

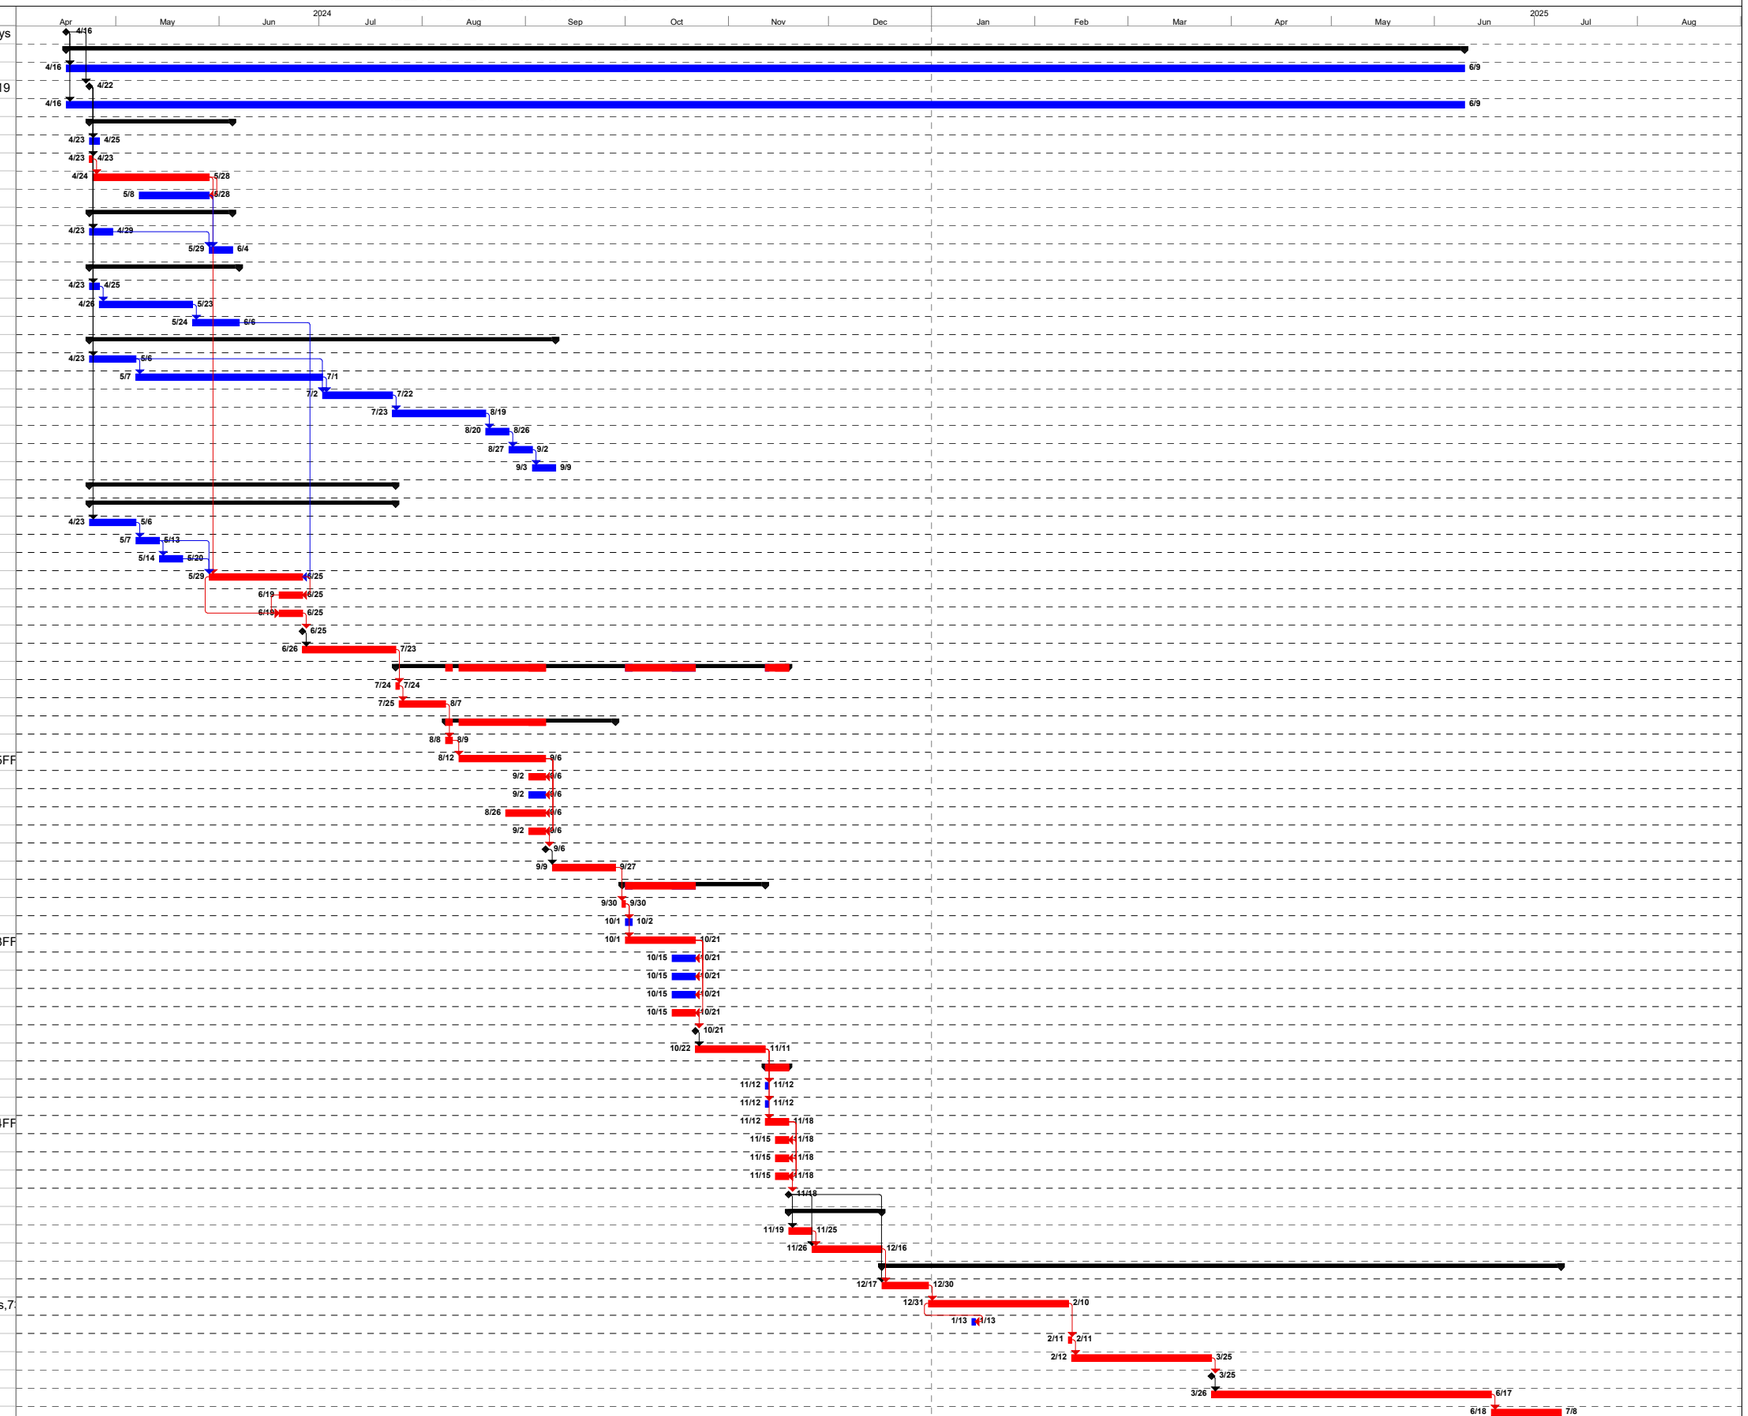

Task | Critical Task | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Progress | Deadline

Fri 3/29/24
