2024 SPRING LAKE PARK CITY HALL RENOVATION / EXPANSION

Construction Results Corporation
Trusted Commercial & Industrial General Contractor

PROJECT MANAGER:
JASON HARALDSON 612-919-0234
SUPT
GARY SWIFT
612-282-5658

ID	Facility	Task Name	Duration	Start	Finish	Resource Names
1		**MILESTONES**				
2		Contract Executed	1 day	Thu 2/15/24	Thu 2/15/24	
3		Building Permit Issued	1 day	Wed 3/20/24	Wed 3/20/24	
4		Site Work Complete	1 day	Thu 6/6/24	Thu 6/6/24	
5		Mechanical / Electrical Rough In Complete	1 day	Fri 7/26/24	Fri 7/26/24	
6		Drywall Complete	1 day	Wed 8/11/24	Wed 8/11/24	
7		Test & Balance Complete	1 day	Mon 8/5/24	Mon 8/5/24	
8		Owner Occupancy	1 day	Mon 9/30/24	Mon 9/30/24	
9		**PRE CONSTRUCTION**				
10		Permit Review - Permit Issued	14 days	Fri 12/22/23	Wed 1/10/24	SLP Inspections
11		Contracts	14 days	Tue 12/12/24	Thu 2/15/24	
12		Pre Construction Meeting	1 day	Thu 2/15/24	Thu 2/15/24	Stormo
13		Shop Drawings / Submittals	50 days	Mon 1/8/24	Fri 3/15/24	CRC
14		Material Procurement	225 days	Mon 2/19/24	Fri 12/6/24	CRC
15		**SITE WORK**				
16		Layout / Survey	1 day	Tue 3/12/24	Tue 3/12/24	Gettman
17		Erosion Control / Site Demolition	6 days	Fri 2/16/24	Fri 2/23/24	Kenaltc X
18		Sub cut / Place Aggregate Base for Concrete	2 days	Thu 5/30/24	Fri 5/31/24	Kenaltc X
19		Form Stoops	2 days	Mon 4/22/24	Tue 4/23/24	CRC
20		Place, Finish Stoops / Strip Forms	2 days	Wed 4/24/24	Thu 4/25/24	CRC
21		Backfill Foundations	1 day	Fri 4/5/24	Fri 4/5/24	Kenaltc X
22		Curb & Gutter	5 days	Wed 5/29/24	Tue 6/4/24	CRC
23		Concrete Paving / Strip Forms	6 days	Wed 6/5/24	Fri 6/14/24	CRC
24		Exterior Bollards	2 days	Thu 4/18/24	Fri 4/19/24	Lonco
25		Sub cut / Place Base for Paving	2 days	Thu 6/13/24	Fri 6/14/24	Kenaltc X
26		Base Coat Asphalt Paving	1 day	Wed 6/5/24	Wed 6/5/24	ARC
27		Wear Coat Asphalt Paving	1 day	Thu 6/6/24	Thu 6/6/24	ARC
28		Asphalt Striping	1 day	Fri 6/7/24	Fri 6/7/24	ARC
29		Final Grading	1 day	Mon 6/17/24	Mon 6/17/24	Kenaltc X
30		Landscape Restoration	2 days	Tue 6/4/24	Wed 6/5/24	CRC
31		**CONSTRUCTION PHASE #1**	**115 days**	**Mon 2/26/24**	**Fri 8/2/24**	
32		Excavation New Foundations	5 days	Mon 2/26/24	Wed 2/28/24	Kenaltc X
33		Form Foundations	3 days	Mon 3/11/24	Wed 3/13/24	CRC
34		Foundation Inspection	1 day	Tue 3/12/24	Tue 3/12/24	SLP
35		Foundation Concrete	5 days	Thu 3/14/24	Mon 3/18/24	CRC
36		Masonry	30 days	Tue 3/19/24	Mon 4/29/24	Foley
37		Brainerainer Dampproofing	3 days	Tue 4/2/24	Thu 4/4/24	Runway
38		Structural Steel	5 days	Tue 4/23/24	Mon 4/29/24	Lonco
39		Roofing / Sheet Metal Flashing	10 days	Thu 5/2/24	Wed 5/15/24	Thurnes
40		Place & Finish Interior S.O.G.	3 days	Thu 5/2/24	Mon 5/6/24	Kellsher
41		Pre Cast Roof Planks	2 days	Tue 4/30/24	Wed 5/1/24	Terracon
42		Interior Framing - Set Door Frames	4 days	Tue 5/7/24	Fri 5/10/24	RTL Construction
43		Exterior Framing - Sheathing / Vapor Barrier	8 days	Thu 5/2/24	Mon 5/13/24	RTL Construction
44		Aluminum Composite Wall Panels	10 days	Wed 5/15/24	Tue 5/28/24	P.B.S
45		Install Exterior Windows	5 days	Wed 5/15/24	Tue 5/21/24	Mimar
46		In wall electrical rough in	5 days	Fri 5/10/24	Thu 5/16/24	Retrofit
47		Inspections	1 day	Thu 5/16/24	Thu 5/16/24	CRC
48		Above Ceiling Mechanical Rough In	6 days	Thu 5/16/24	Thu 5/23/24	Precise
49		Above Ceiling Electrical Rough In	6 days	Thu 5/16/24	Tue 5/21/24	Retrofit
50		Fire Protection Rough In	5 days	Thu 5/2/24	Mon 5/6/24	Summit
51		Drywall	5 days	Fri 5/17/24	Tue 5/21/24	RTL Construction
52		Mechanical Insulation	3 days	Fri 5/24/24	Tue 5/28/24	Precise
53		Aluminum Storefront / Glazing / Hardware	6 days	Mon 6/3/24	Mon 6/10/24	SPWD
54		Drywall Tape & Finish	6 days	Wed 5/22/24	Mon 6/3/24	RTL Construction
55		Prep / Prime First Coat Paint	2 days	Thu 5/30/24	Fri 5/31/24	Brush Masters
56		Floor Prep	2 days	Fri 5/31/24	Fri 6/31/24	
57		Install ACT Grid	3 days	Fri 5/31/24	Tue 6/4/24	Minnesota Acoustics
58		Ceramic Tile Finishes	4 days	Mon 6/3/24	Thu 6/6/24	ATB
59		Lighting Install	3 days	Wed 6/5/24	Fri 6/7/24	Retrofit
60		Set Sprinkler Heads	2 days	Wed 6/5/24	Thu 6/6/24	Summit
61		Install ACT	3 days	Mon 6/10/24	Wed 6/12/24	Minnesota Acoustics
62		Final Paint	3 days	Fri 6/7/24	Mon 6/10/24	Brush Masters
63		Metal Stairs - Handrail	4 days	Mon 5/20/24	Thu 5/23/24	Lonco
64		Specialties / Accessories	3 days	Tue 5/28/24	Mon 5/30/24	Centennial
65		Doors / Hardware	3 days	Thu 6/13/24	Thu 6/13/24	CRC
66		Specialties / Entrance Mats	2 days	Mon 6/3/24	Tue 6/4/24	CRC
67		Electrical Finishes	5 days	Fri 6/7/24	Thu 6/13/24	Retrofit
68		Casework / Countertops	3 day	Tue 6/11/24	Tue 6/11/24	CRC
69		Mechanical Systems Start Up	3 days	Wed 7/31/24	Wed 7/31/24	Precise
70		Test & Balance	2 days	Thu 8/1/24	Fri 8/2/24	
71		Final Clean	1 day	Wed 6/12/24	Wed 6/12/24	CRC
72		Final Inspections	1 day	Mon 4/15/24	Mon 4/15/24	SLP Inspections
73		Owner Furniture Install	4 days	Tue 8/1/24	Fri 8/4/24	SLP
74		**CONSTRUCTION PHASE #2**	**122 days**	**Mon 2/12/24**	**Tue 7/30/24**	
75		Mobilize / Dust Protection	1 day	Tue 2/13/24	Tue 2/13/24	CRC
76		Demolition	20 days	Fri 2/16/24	Thu 3/14/24	CRC
77		Mechanical / Electrical Demo	7 days	Fri 2/16/24	Mon 2/26/24	Precise / Retrofit
78		Saw Cut & Remove SOG	12 days	Wed 3/6/24	Thu 3/21/24	CRC
79		Excavate Interior Foundations	3 days	Thu 3/14/24	Mon 3/18/24	
80		Form Foundations	2 days	Tue 3/19/24	Wed 3/20/24	CRC
81		Foundation Inspection	1 day	Fri 3/22/24	Fri 3/22/24	CRC
82		Foundation Concrete	5 days	Mon 3/25/24	Wed 3/27/24	CRC
83		Masonry	8 days	Wed 4/10/24	Mon 4/22/24	Foley
84		Underground Plumbing	3 days	Tue 4/23/24	Thu 4/25/24	Precise
85		Underground Plumbing Inspections	1 day	Tue 4/23/24	Tue 4/23/24	Precise
86		Place & Finish Interior SOG	4 days	Fri 4/26/24	Wed 5/1/24	Kellsher
87		Pre Cast Planks	1 day	Mon 4/15/24	Mon 4/15/24	Terracon
88		Place & Finish Pre Cast Topping	2 days	Thu 5/2/24	Fri 5/3/24	Kellsher
89		Sealed Concrete Floor Finishes	6 days	Thu 5/30/24	Thu 6/6/24	Mavo
90		Interior Wall Framing / Door Frames	4 days	Thu 5/2/24	Tue 5/7/24	RTL Construction
91		Roofing Sheet Metal Flashings	10 days	Thu 4/9/24	Wed 4/11/24	Thurnes
92		Install Exterior Wall Louver	3 days	Thu 4/25/24	Mon 4/29/24	CRC
93		In Wall Electrical Rough In	5 days	Wed 5/8/24	Tue 5/14/24	Retrofit
94		In Wall Plumbing Rough In	5 days	Wed 5/8/24	Tue 5/14/24	Precise
95		Inspections	1 day	Tue 5/14/24	Tue 5/14/24	SLP Inspections
96		Above Ceiling Mechanical Rough In	6 days	Wed 5/8/24	Fri 5/17/24	Precise
97		Above Ceiling Electrical Rough In	6 days	Wed 5/8/24	Wed 5/15/24	Retrofit
98		Fire Protection Rough In	4 days	Wed 5/8/24	Mon 5/13/24	Summit
99		Drywall	5 days	Wed 5/15/24	Fri 5/17/24	RTL Construction
100		Mechanical Insulation	2 days	Mon 5/20/24	Tue 5/21/24	Precise
101		Drywall Tape & Finish	4 days	Mon 5/20/24	Wed 5/29/24	RTL Construction
102		Prep / Prime First Coat Paint	2 days	Thu 5/30/24	Fri 5/31/24	Brush Masters
103		Install ACT Grid	3 days	Mon 6/3/24	Wed 6/5/24	Minnesota Acoustics
104		Ceramic Tile Finishes	4 days	Mon 5/20/24	Thu 5/23/24	ATB
105		Ceramic Tile Finishes	3 days	Mon 5/20/24	Mon 6/10/24	ATB
106		Lighting Install	3 days	Thu 6/6/24	Tue 6/11/24	Retrofit
107		Set Sprinkler Heads	3 days	Thu 6/6/24	Mon 6/10/24	Summit
108		Install ACT	4 days	Wed 6/12/24	Mon 6/17/24	Minnesota Acoustics
109		Final Paint	4 days	Wed 6/12/24	Mon 6/17/24	Brush Masters
110		Doors / Hardware	3 days	Tue 6/18/24	Thu 6/20/24	CRC
111		Specialties / Accessories	3 days	Fri 6/7/24	Tue 6/11/24	CRC
112		Metal Stairs - Handrail	4 days	Mon 5/6/24	Thu 5/9/24	Lonco
113		Install Overhead Doors	4 days	Mon 4/8/24	Fri 4/12/24	Mimar
114		Electrical Finishes	7 days	Mon 6/17/24	Tue 6/25/24	Retrofit
115		Plumbing Finishes	7 days	Thu 6/6/24	Fri 6/14/24	Precise
116		Casework / Countertops	3 days	Mon 6/17/24	Wed 6/19/24	CRC
117		Final Clean	1 day	Wed 6/12/24	Wed 6/12/24	CRC
118		Final Paint	4 days	Wed 6/12/24	Mon 6/17/24	Brush Masters
119		Doors / Hardware	3 days	Tue 6/18/24	Thu 6/20/24	CRC
120		Specialties / Accessories	3 days	Fri 6/7/24	Tue 6/11/24	CRC
121		Metal Stairs - Handrail	4 days	Mon 5/6/24	Thu 5/9/24	Lonco
122		Install Overhead Doors	4 days	Mon 4/8/24	Fri 4/12/24	Mimar
123		Electrical Finishes	7 days	Mon 6/17/24	Tue 6/25/24	Retrofit
124		Plumbing Finishes	7 days	Thu 6/6/24	Fri 6/14/24	Precise
125		Casework / Countertops	3 days	Mon 6/17/24	Wed 6/19/24	CRC
126		Microstone Finishes	6 days	Mon 6/3/24	Mon 6/10/24	CRC
127		Final Clean	1 day	Fri 8/2/24	Fri 8/2/24	CRC
128		Test & Balance	3 days	Mon 12/18/23	Mon 12/18/23	
129		Final Inspections	1 day	Fri 8/2/24	Fri 8/2/24	SLP
130		Owner Furniture Install	4 days	Tue 8/6/24	Thu 8/8/24	SLP
131		**CONSTRUCTION PHASE #3**	**60 days**	**Tue 7/2/24**	**Mon 9/30/24**	
132		Mobilize / Dust Protection	1 day	Thu 8/1/24	Thu 8/1/24	CRC
133		Demolition	5 days	Fri 8/2/24	Thu 8/8/24	CRC
134		Mechanical / Electrical Demo	3 days	Mon 8/12/24	Fri 8/15/24	Retrofit
135		Saw Cut & Remove SOG	5 days	Tue 8/6/24	Thu 8/8/24	CRC
136		Masonry	3 days	Tue 6/25/24	Mon 7/1/24	Foley
137		Underground Plumbing	4 days	Fri 6/21/24	Wed 6/26/24	Precise
138		Underground Plumbing Inspection	1 day	Thu 6/27/24	Thu 6/27/24	Precise
139		Place & Finish Interior SOG	2 days	Fri 7/5/24	Mon 7/8/24	Kellsher
140		Frame Exterior Infill Framing / Door Frames	3 days	Tue 7/2/24	Wed 7/3/24	RTL Construction
141		Roofing - Sheet Metal Flashings	5 days	Mon 5/6/24	Mon 5/13/24	Thurnes
142		Install Exterior Wall Louver	2 days	Wed 5/1/24	Thu 5/2/24	CRC
143		In Wall Electrical Rough In	2 days	Thu 7/4/24	Fri 7/5/24	Retrofit
144		In Wall Plumbing Rough In	3 days	Wed 7/3/24	Fri 7/5/24	Precise
145		Inspections	1 day	Mon 7/8/24	Mon 7/8/24	SLP Inspections
146		Above Ceiling Mechanical Rough In	4 days	Tue 7/2/24	Fri 7/5/24	Precise
147		Above Ceiling Electrical Rough In	3 days	Wed 7/3/24	Fri 7/5/24	Retrofit
148		Fire Protection Rough In	2 days	Thu 7/4/24	Fri 7/5/24	Summit
149		Drywall	3 days	Mon 7/8/24	Wed 7/10/24	RTL Construction
150		Mechanical Insulation	2 days	Tue 7/9/24	Mon 7/8/24	Precise
151		Aluminum Storefront / Glazing / Hardware	5 days	Mon 5/27/24	Wed 6/26/24	SPWD
152		Drywall Tape & Finish	4 days	Wed 7/10/24	Mon 7/15/24	RTL Construction
153		Sealed Concrete Floor Finishes	3 days	Thu 7/18/24	Mon 7/22/24	Mavo
154		Prep / Prime First Coat Paint	2 days	Tue 7/16/24	Wed 7/17/24	Brush Masters
155		Floor Prep	2 days	Tue 7/16/24	Wed 7/17/24	
156		Install ACT Grid	2 days	Thu 7/18/24	Fri 7/19/24	Minnesota Acoustics
157		Concrete Floor Coating Finishes	4 days	Tue 7/16/24	Fri 7/19/24	QC
158		Ceramic Tile Finishes	10 days	Thu 7/11/24	Wed 7/24/24	ATB
159		Lighting Install	3 days	Mon 7/22/24	Wed 7/24/24	Retrofit
160		Set Sprinkler Heads	4 days	Mon 7/22/24	Thu 7/25/24	Summit
161		Install ACT	3 days	Fri 7/26/24	Tue 7/30/24	Minnesota Acoustics
162		Final Paint	2 days	Fri 7/26/24	Mon 7/29/24	Brush Masters
163		Carpet Flooring	3 days	Tue 7/30/24	Thu 8/1/24	Centennial
164		Doors / Hardware	3 days	Tue 7/30/24	Thu 8/1/24	CRC
165		Specialties / Accessories	3 days	Thu 7/25/24	Mon 7/29/24	CRC
166		Electrical Finishes	3 days	Tue 7/30/24	Thu 8/1/24	Retrofit
167		Plumbing Finishes	6 days	Thu 7/25/24	Thu 8/1/24	Precise
168		Casework / Countertops	3 days	Tue 7/30/24	Thu 8/1/24	CRC
169		Personnel Lockers Install	3 days	Tue 7/30/24	Thu 8/1/24	HD Group
170		Mechanical Systems Start Up	2 days	Wed 7/31/24	Thu 8/1/24	Precise
171		Test & Balance	2 days	Fri 8/2/24	Mon 8/5/24	
172		Final Clean	2 days	Wed 6/12/24	Thu 6/13/24	CRC
173		Final Inspections	1 day	Fri 8/2/24	Fri 8/2/24	SLP Inspections
174		Owner Furniture Install	3 days	Mon 6/17/24	Wed 6/19/24	SLP
175		**Construction Phase #4**	**177 days**	**Mon 12/18/23**	**Tue 8/20/24**	
176		Mobilize / Dust Protection	1 day	Tue 6/18/24	Tue 6/18/24	CRC
177		Demolition	3 days	Wed 6/19/24	Fri 6/21/24	CRC
178		Mechanical / Electrical Demo	5 days	Wed 6/19/24	Tue 6/25/24	Precise / Retrofit
179		Masonry	3 days	Tue 6/25/24	Mon 7/1/24	Foley
180		Interior Wall Framing / Door Frames	2 days	Thu 6/27/24	Fri 6/28/24	RTL Construction
181		Roofing Sheet Metal Flashings	6 days	Tue 5/14/24	Tue 5/21/24	Thurnes
182		In Wall Electrical Rough In	4 days	Mon 7/1/24	Thu 7/4/24	Retrofit
183		In Wall Plumbing Rough In	2 days	Mon 7/1/24	Tue 7/2/24	Precise
184		Inspections	1 day	Fri 7/5/24	Fri 7/5/24	SLP
185		Above Ceiling Mechanical Rough In	6 days	Mon 7/8/24	Mon 7/15/24	Precise
186		Above Ceiling Electrical Rough In	5 days	Mon 7/8/24	Mon 7/10/24	Retrofit
187		Fire Protection Rough In	4 days	Mon 7/8/24	Thu 7/11/24	Summit
188		Drywall	5 days	Tue 7/16/24	Mon 7/22/24	RTL Construction
189		Mechanical Insulation	2 days	Tue 7/16/24	Wed 7/17/24	Precise
190		Drywall Tape & Finish	6 days	Mon 7/15/24	Mon 7/22/24	RTL Construction
191		Prep / Prime First Coat Paint	4 days	Tue 7/23/24	Fri 7/26/24	Brush Masters
192		Install ACT Grid	2 days	Mon 7/29/24	Tue 7/30/24	Minnesota Acoustics
193		Ceramic Tile Finishes	4 days	Mon 7/29/24	Thu 8/1/24	ATB
194		Lighting Install	3 days	Wed 7/31/24	Tue 8/6/24	Retrofit
195		Set Sprinkler Heads	3 days	Wed 7/31/24	Fri 8/2/24	Summit
196		Install ACT	3 days	Wed 8/7/24	Fri 8/9/24	Minnesota Acoustics
197		Final Paint	3 days	Wed 8/7/24	Fri 8/9/24	Brush Masters
198		Carpet Flooring	3 days	Mon 8/12/24	Wed 8/14/24	Centennial
199		Doors / Hardware	3 days	Thu 8/15/24	Tue 8/20/24	CRC
200		Install Operable Partition	3 days	Mon 7/29/24	Wed 7/31/24	Acoustics Associates
201		Electrical Finishes	4 days	Mon 8/12/24	Thu 8/15/24	Retrofit
202		Plumbing Finishes	3 days	Wed 7/31/24	Thu 8/1/24	Precise
203		Casework / Countertops	2 days	Mon 7/29/24	Tue 7/30/24	CRC
204		Final Clean	1 day	Fri 8/2/24	Fri 8/2/24	CRC
205		Test & Balance	3 days	Mon 12/18/23	Mon 12/18/23	
206		Final Inspections	1 day	Fri 8/9/24	Fri 8/9/24	SLP
207		Owner Furniture Install	3 days	Tue 8/13/24	Thu 8/15/24	SLP
208		**CONSTRUCTION PHASE #5**	**60 days**	**Tue 7/2/24**	**Mon 9/30/24**	
209		Mobilize / Dust Protection	1 day	Thu 8/1/24	Thu 8/1/24	CRC
210		Demolition	5 days	Fri 8/2/24	Thu 8/8/24	CRC
211		Mechanical / Electrical Demo	3 days	Fri 8/2/24	Tue 8/6/24	Precise / Retrofit
212		Saw Cut & Remove SOG	5 days	Tue 8/6/24	Thu 8/8/24	CRC

2024 SPRING LAKE PARK CITY HALL RENOVATION / EXPANSION

Construction Results Corporation
Trusted Commercial & Industrial General Contractor

PROJECT MANAGER:
JASON HARALDSON 612-919-0234
SUPT
GARY SWIFT
612-282-5658

ID	Task ID	Task Name	Duration	Start	Finish	Resource Names
107		Cap Underground Plumbing	1 day	Fri 8/9/24	Fri 8/9/24	Precise
108		Place & Finish Interior SOG	2 days	Mon 8/12/24	Tue 8/13/24	Kelliher
109		Masonry	5 days	Tue 7/2/24	Wed 7/10/24	Foley
110		Interior Wall Framing / Door Frames	5 days	Wed 8/14/24	Tue 8/20/24	RTL Construction
111		Above Ceiling Electrical Rough In	4 days	Wed 8/21/24	Mon 8/26/24	Ratcliffe
112		Inspections	1 day	Fri 8/23/24	Fri 8/23/24	SLP Inspections
113		Above Ceiling Mechanical Rough In	4 days	Wed 8/21/24	Mon 8/26/24	Precise
114		Above Ceiling Electrical Rough In	4 days	Wed 8/21/24	Mon 8/26/24	Ratcliffe
115		Fire Protection Rough In	3 days	Wed 8/21/24	Fri 8/23/24	Summit
116		Drywall	4 days	Mon 8/26/24	Thu 8/29/24	RTL Construction
117		Mechanical Insulation	2 days	Tue 8/27/24	Wed 8/28/24	Precise
118		Aluminum Storefront / Glazing / Hardware	5 days	Thu 7/11/24	Wed 7/17/24	MWG
119		Drywall Tape & Finish	8 days	Fri 8/30/24	Tue 9/10/24	RTL Construction
120		Prep / Prime Coat Coat Paint	2 days	Wed 9/11/24	Thu 9/12/24	Brush Masters
121		Install Acoustic Ceiling	1 day	Fri 9/13/24	Fri 9/13/24	Minnesota Acoustics
122		Ceramic Tile Finishes	4 days	Wed 9/11/24	Mon 9/16/24	ATB
123		Lighting Install	5 days	Mon 9/16/24	Fri 9/20/24	Ratcliffe
124		Set Sprinkler Heads	3 days	Tue 9/17/24	Thu 9/19/24	Summit
125		Install ACT	3 days	Tue 9/17/24	Thu 9/19/24	Minnesota Acoustics
126		Final Paint	3 days	Fri 9/13/24	Tue 9/17/24	Brush Masters
127		Carpet Flooring	5 days	Mon 9/16/24	Fri 9/20/24	Continental
128		Doors / Hardware	4 days	Mon 9/23/24	Thu 9/26/24	CRC
129		Finish Carpentry	5 days	Fri 9/13/24	Thu 9/19/24	CRC
130		Electrical Finishes	5 days	Wed 9/18/24	Tue 9/24/24	Ratcliffe
131		Mechanical Finishes	5 days	Wed 9/18/24	Tue 9/24/24	Precise
132		Mechanical Systems Start Up	1 day	Wed 7/31/24	Wed 7/31/24	Precise
133		Test & Balance	2 days	Thu 8/1/24	Fri 8/2/24	
134		Final Clean	2 days	Fri 9/20/24	Mon 9/23/24	CRC
135		Final Inspections	1 day	Wed 9/25/24	Wed 9/25/24	SLP Inspections
136		Owner Furniture Install	5 days	Tue 9/24/24	Mon 9/30/24	SLP
137		**PROJECT CLOSEOUT**				
138		O&M Closeout Documents	15 days	Mon 7/29/24	Fri 8/16/24	CRC
139		Punch List	10 days	Wed 7/24/24	Tue 8/6/24	Stantec
140		Substantial Completion	1 day	Tue 8/6/24	Tue 8/6/24	SLP
141		Certificate of Occupancy	1 day	Wed 8/7/24	Wed 8/7/24	SLP Inspections
142						



2024 SPRING LAKE PARK CITY HALL RENOVATION / EXPANSION

Construction Results Corporation

Trusted Commercial & Industrial General Contractor

PROJECT MANAGER:
JASON HARALDSON 612-919-0234
SUPT
GARY SWIFT
612-282-5658

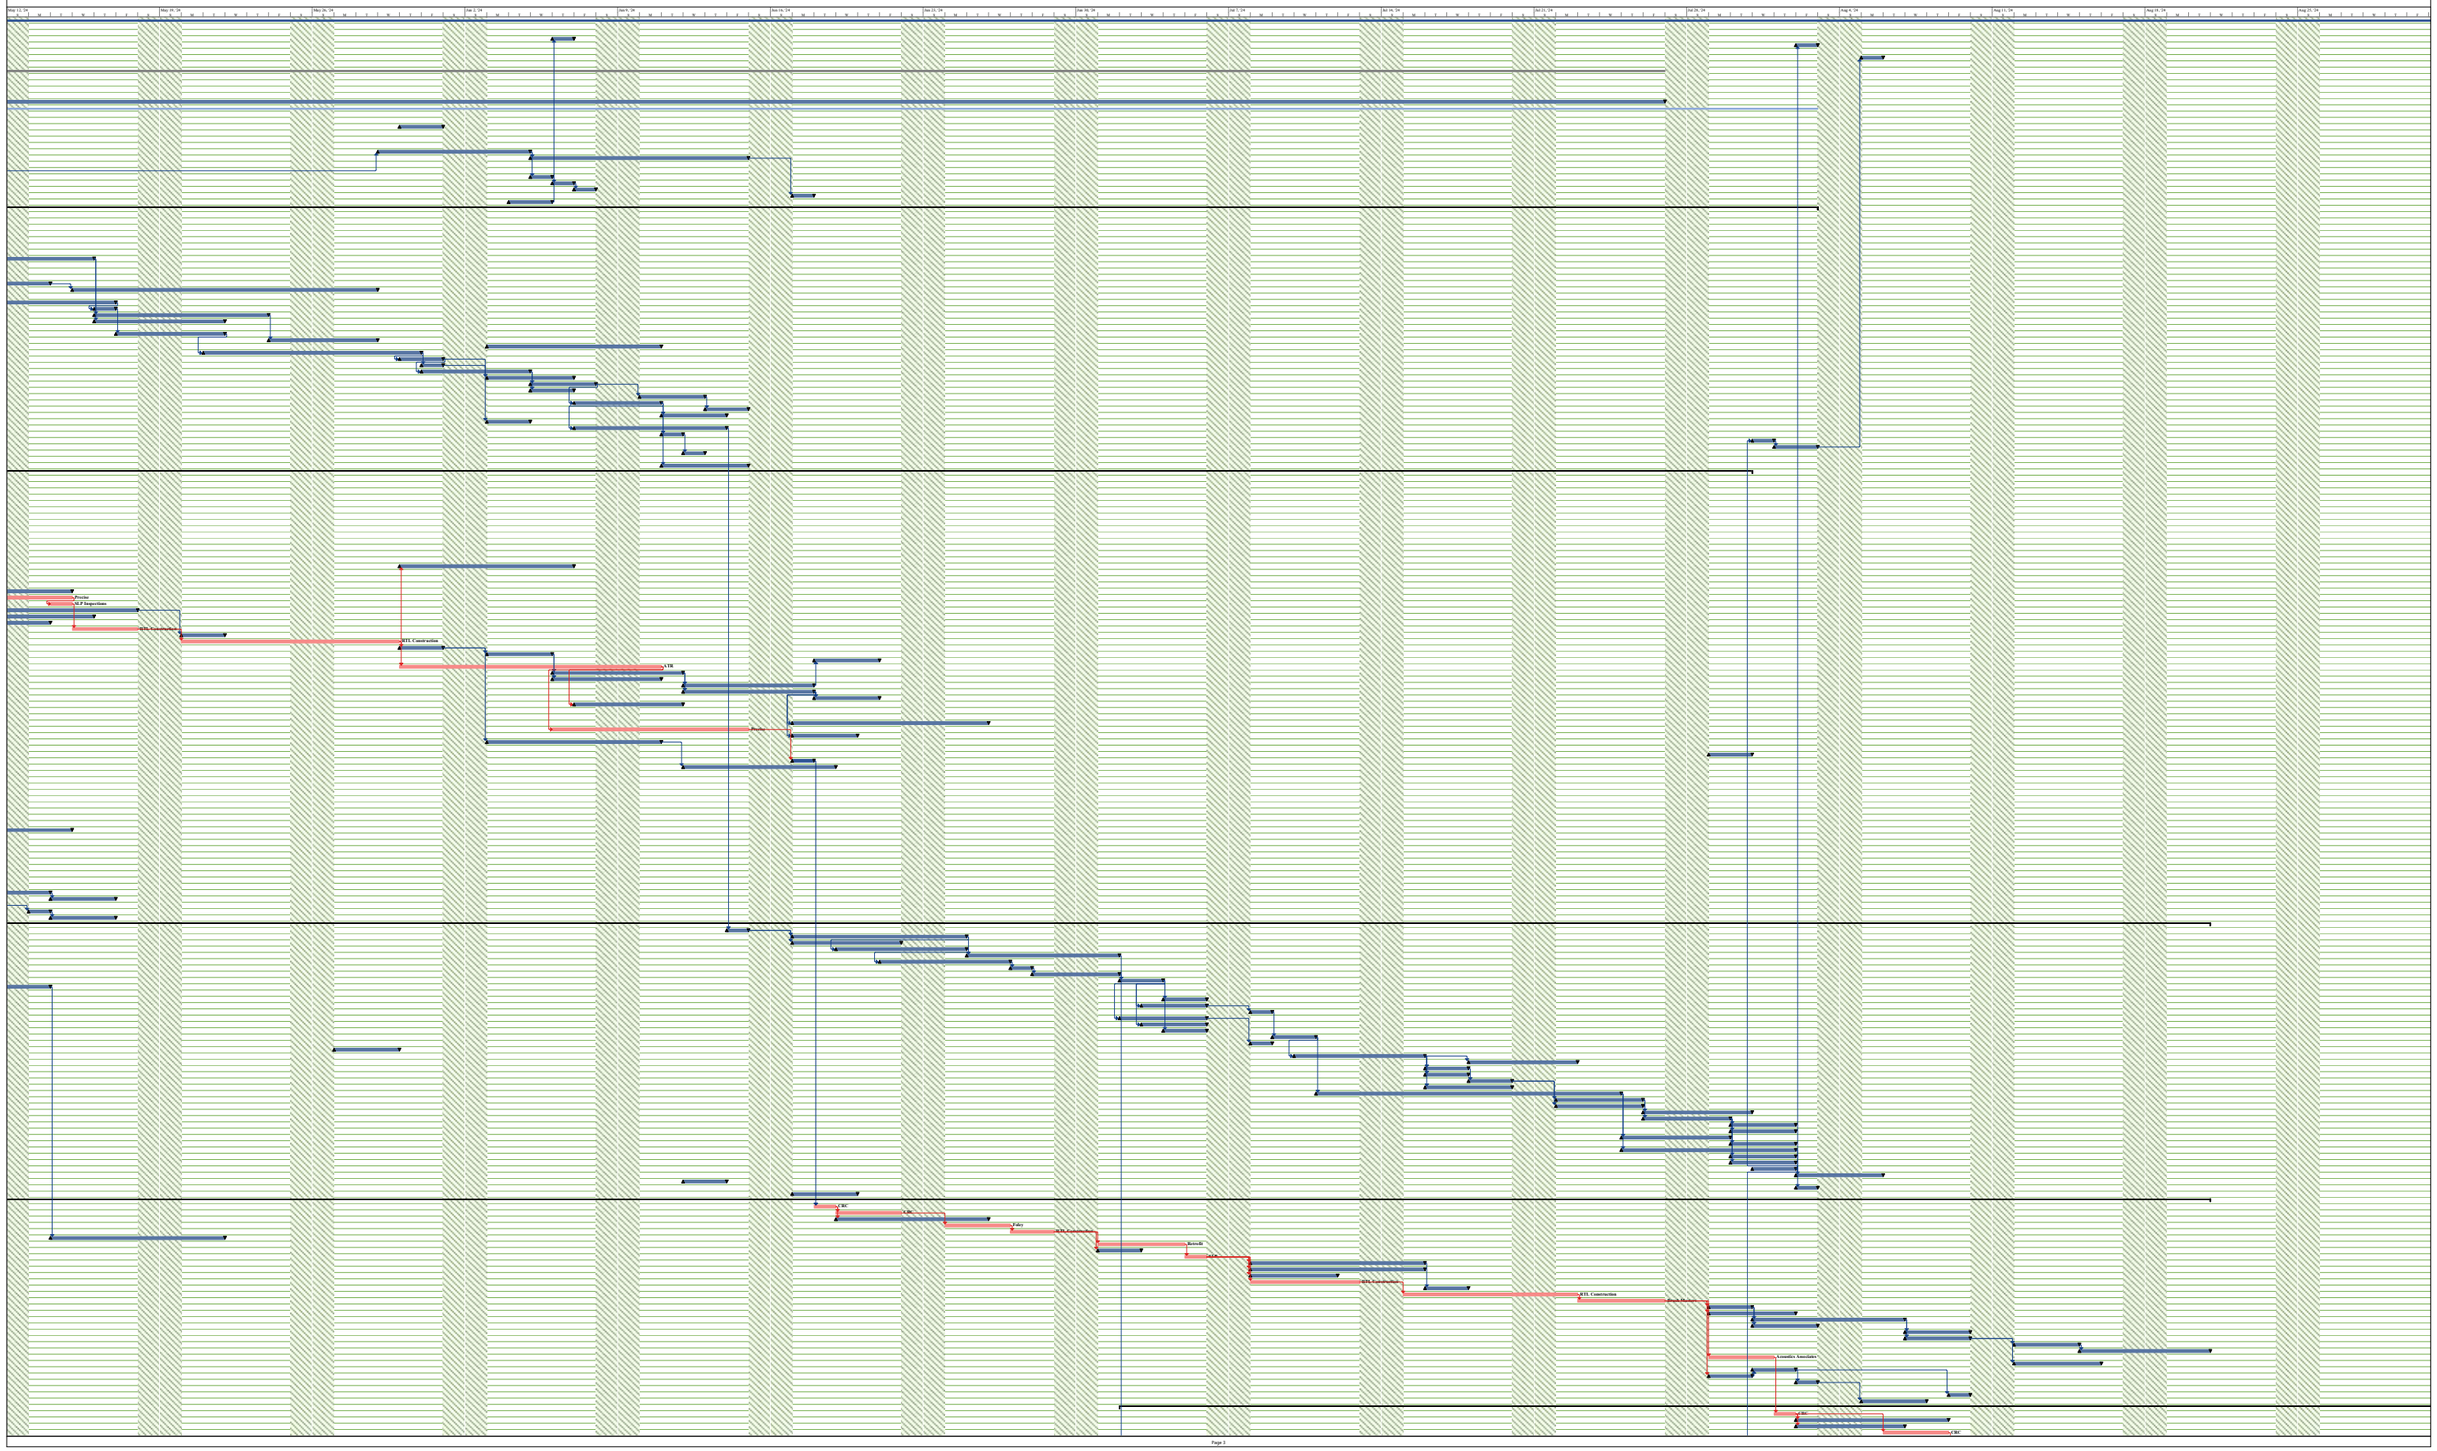

2024 SPRING LAKE PARK CITY HALL RENOVATION / EXPANSION

Construction Results Corporation

Trusted Commercial & Industrial General Contractor
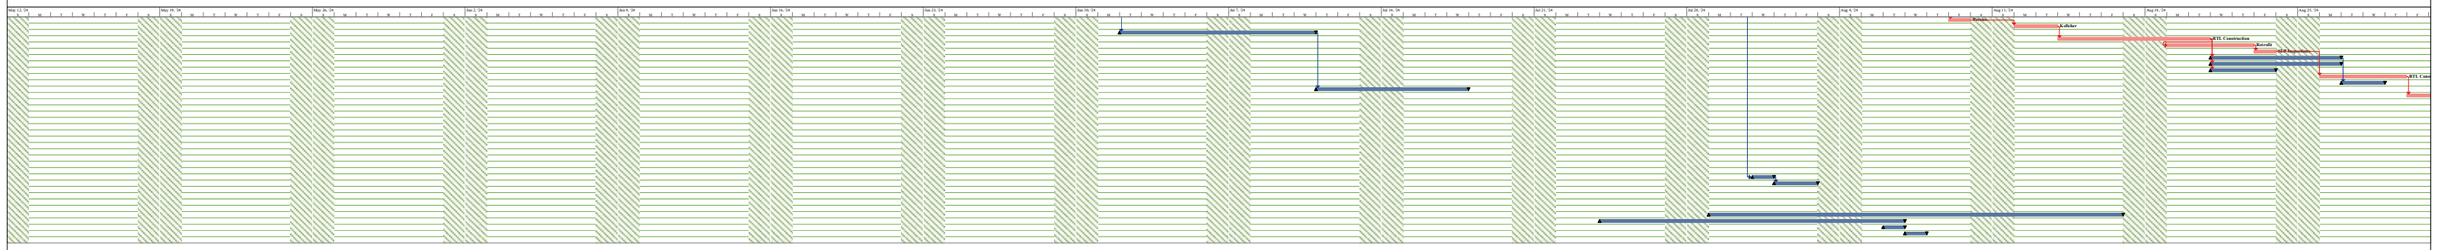
PROJECT MANAGER:
JASON HARALDSON 612-919-0234
SUPT
GARY SWIFT
612-282-5658
