Line	Name	Responsibility	Duration	Predecessors	Successors	Start	Finish
	MAJOR MILESTONES						
2	SISD Stadium Interview				3 2d	1/17/2023	1/17/2023
3	Notice to Proceed			2 2d	ns	1/19/2023	1/19/2023
4	Mobilizing			20 25d		11/15/2023	11/15/2023
5	Substantial Completion			50		3/14/2025	3/14/2025
6	Final Completion			51		4/17/2025	4/17/2025
	DESIGN AND ENGINEERING						
	SCHEMATIC DESIGN						
	DESIGN DEVELOPMENT						
10	Design Development (DD)		90d	ns	11, 19 -20d, 26 -17d	4/20/2023	8/28/2023
11	SISD Approval (DD)		5d	10	13, 18, 20 5d	8/29/2023	9/5/2023
	CONTRACT DOCUMENTS						
13	Design Development (CD)		55d	11	14	9/6/2023	11/21/2023
14	SISD Approval (CD)		5d	13	23, 29 -1d	11/22/2023	11/30/2023
	PRECONSTRUCTION						
	SD BUDGETING						
	DD BUDGETING						
18	Design Builder Budgeting		15d	11		9/6/2023	9/26/2023
19	GMP#01 Bleacher/Turf Early Bid Package		20d	10 -20d	45	8/1/2023	8/28/2023
20	GMP#02 Site Package Early Bid Package		20d	11 5d	4 25d, 21	9/13/2023	10/10/2023
21	SISD Approval		5d	20	34	10/11/2023	10/17/2023
	GMP DEVELOPMENT						
23	GMP#03 Building Package		20d	14	24	12/1/2023	12/29/2023
24	SISD Approval		10d	23	39	1/2/2024	1/15/2024
	PERMITTING AND APPROVALS						
26	Early Site Package Issued to AHJ for Permit			10 -17d	27	8/4/2023	8/4/2023
27	Early Site Package AHJ Review Comments		20d	26	28	8/4/2023	8/31/2023
28	Early Site Package Permit Issued		20d	27	34	9/1/2023	9/29/2023
29	Building Issued to AHJ for Permit			14 -1d	30	11/30/2023	11/30/2023
30	Building AHJ Review Comments		20d	29	31	11/30/2023	12/28/2023
31	Building Permit Issued		10d	30	39	12/29/2023	1/12/2024

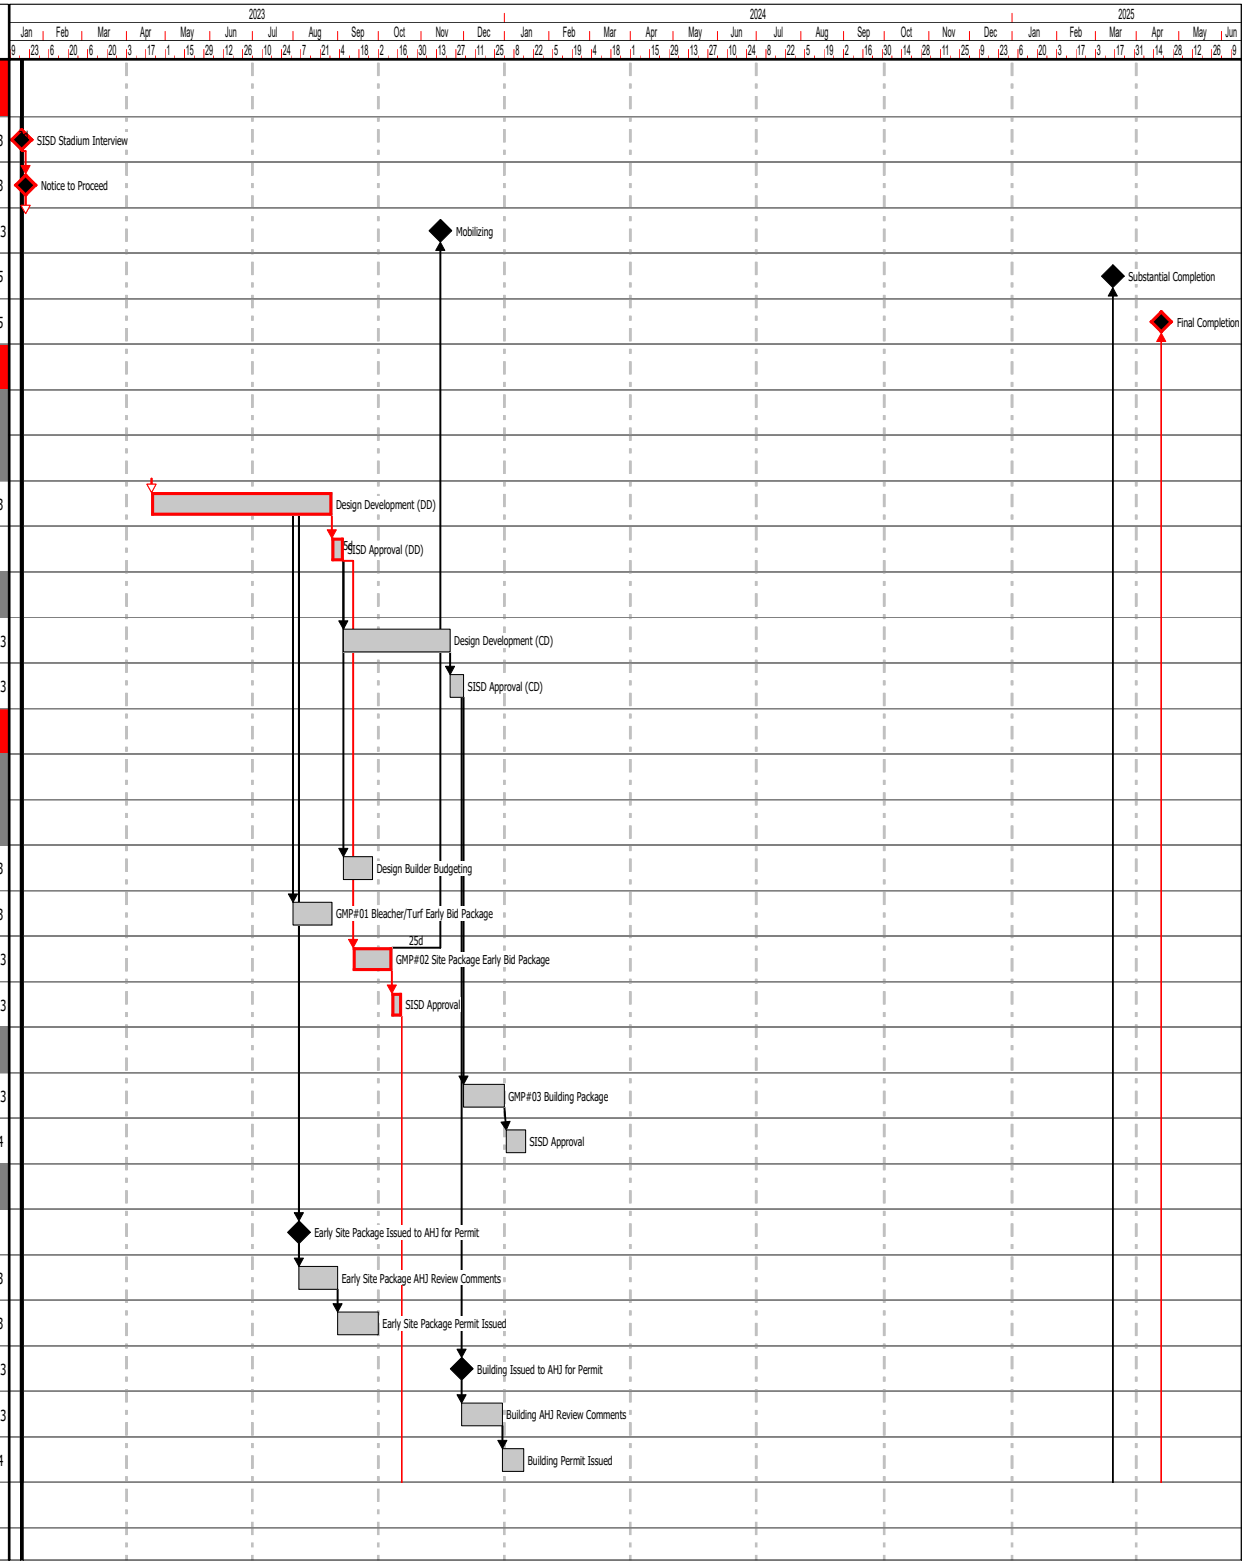

Line	Name	Responsibility	Duration	Predecessors	Successors	Start	Finish
	CONSTRUCTION						
	SITE WORK						
34	Earthwork		70d	21, 28	35 SS 20d, 39	10/18/2023	1/29/2024
35	Site Utilities		75d	34 SS 20d	36 SS 35d, 37	11/15/2023	3/4/2024
36	Paving		65d	35 SS 35d	37	1/9/2024	4/8/2024
37	Site Work Finishes		70d	35, 36, 41 SS 15d		7/3/2024	10/11/2024
	BUILDINGS						
39	Foundations		100d	24, 34, 31	40 SS 50d	1/30/2024	6/18/2024
40	Structure		90d	39 SS 50d	41 SS 45d	4/9/2024	8/15/2024
41	Exterior Facades		120d	40 SS 45d	42 SS 45d, 44, 45 SS 80d, 37 SS 15d	6/12/2024	12/3/2024
42	Interior Finishes		120d	41 SS 45d	49	8/16/2024	2/6/2025
	SITE FINISHES						
44	Scoreboard		60d	41		12/4/2024	2/27/2025
45	Bleachers		75d	19, 41 SS 80d	46 SS 50d	10/7/2024	1/23/2025
46	Turf		55d	45 SS 50d	49	12/18/2024	3/6/2025
	CLOSEOUT						
	PUNCHLIST						
49	Final Inspections		5d	42, 46	50	3/7/2025	3/13/2025
50	Certificate of Occupancy			49	5, 51	3/14/2025	3/14/2025
51	Punchlists		25d	50	6	3/14/2025	4/17/2025

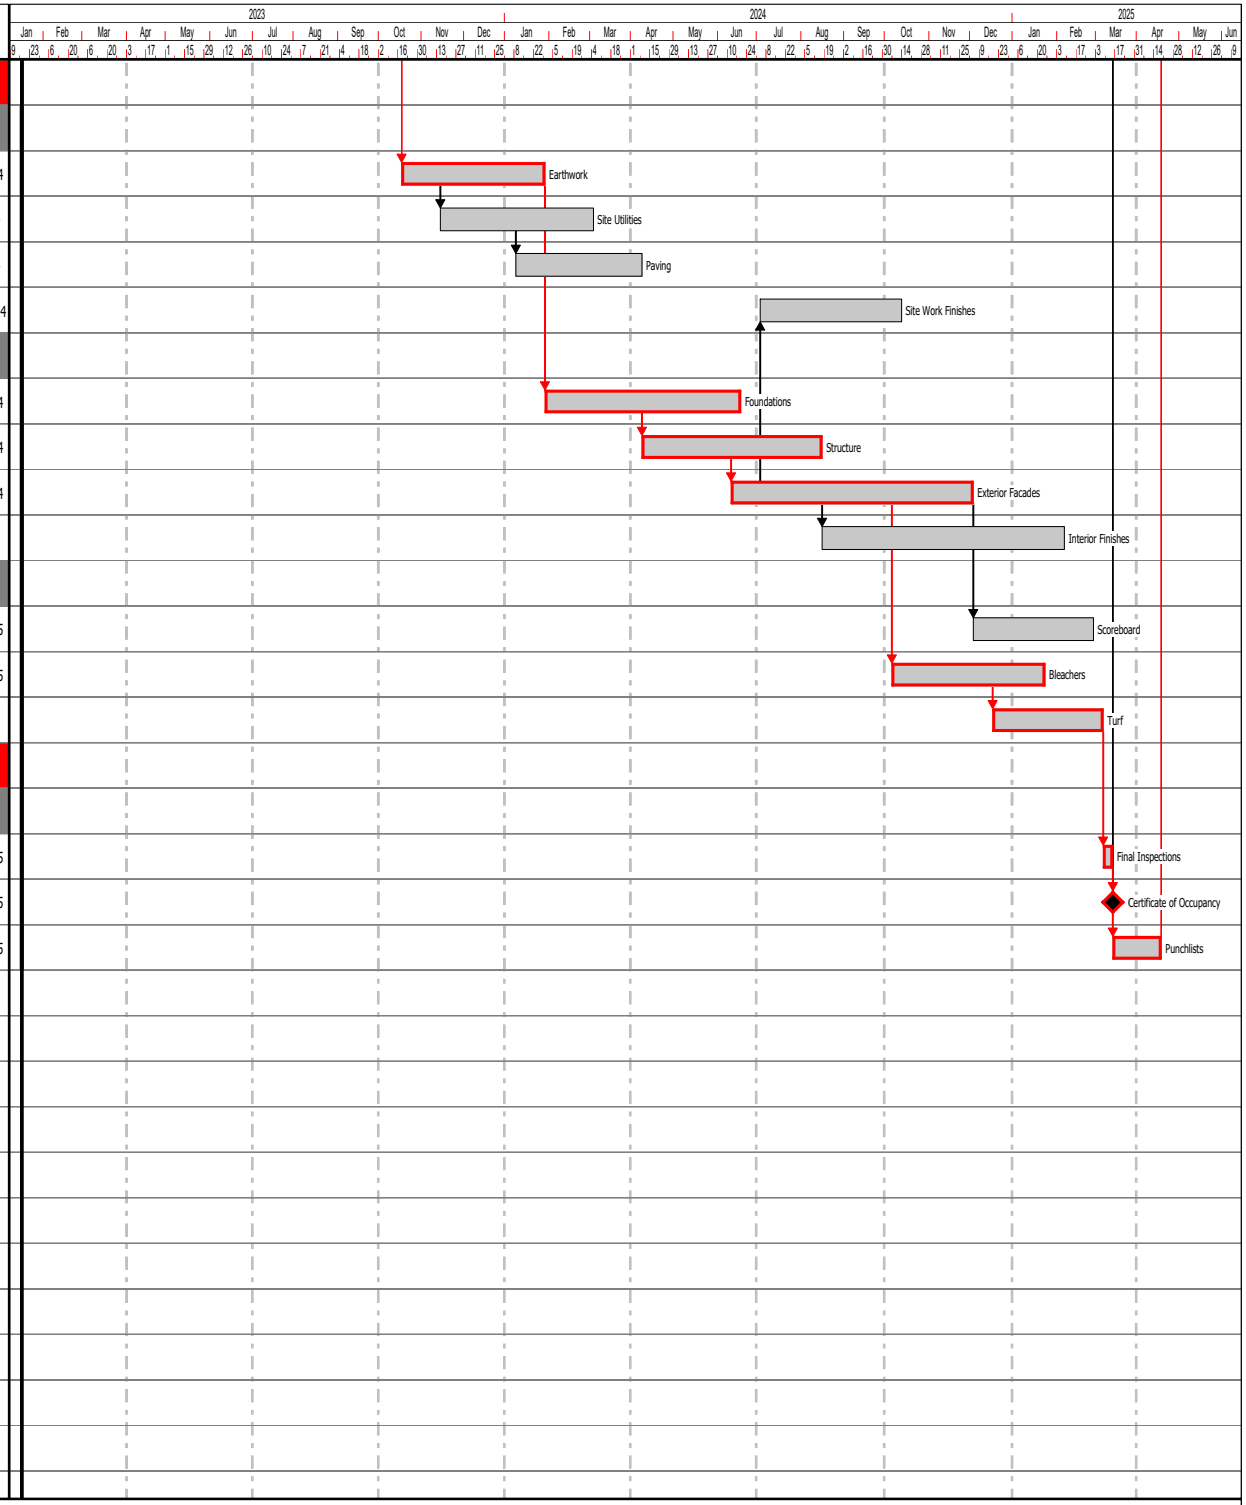

Milestone Appearances

◇ Diamond
