ID	Task Name	Duration	Start	Finish	Predecessors	% Complete	Flag1	Resource Names
6	CO#1	250 edays	Fri 10/3/25	Wed 6/10/26	5	19%	No	
84	**Change Order**	**200 days**	**Mon 3/3/25**	**Mon 12/8/25**		**97%**	**No**	
90	**Headworks**	**200 days**	**Mon 3/3/25**	**Mon 12/8/25**		**93%**	**No**	
93	Delivery	30 ewks	Mon 5/12/25	Mon 12/8/25	92	91%	No	
102	**Work Phase**	**555 days?**	**Mon 3/18/24**	**Fri 5/1/26**		**74%**	**No**	
181	**Yard Piping**	**328 days**	**Tue 9/10/24**	**Thu 12/11/25**		**89%**	**No**	
198	**Post CO**	**10 days**	**Fri 11/28/25**	**Thu 12/11/25**		**0%**	**No**	
199	Install 4" Disk Filter Drain (130 LF)	3 days	Fri 11/28/25	Tue 12/2/25	220	0%	No	
200	Install Plant Water Lines (800 LF)	2 days	Wed 12/3/25	Thu 12/4/25	199	0%	No	
201	Install 3" Digestor Drain HDPE (130 LF)	3 days	Fri 12/5/25	Tue 12/9/25	200	0%	No	
202	Install 3/4" Chem Feed Lines	2 days	Wed 12/10/25	Thu 12/11/25	201	0%	No	
206	**Equipment & Fab Pipe**	**344 days**	**Mon 11/11/24**	**Thu 3/5/26**		**49%**	**No**	
207	**SBR**	**344 days**	**Mon 11/11/24**	**Thu 3/5/26**		**62%**	**No**	
221	Install Decanters (x3)	10 days	Fri 11/28/25	Thu 12/11/25	220	0%	No	
222	Install Chlorine Contact Weir	2 days	Fri 12/12/25	Mon 12/15/25	118,56,220,221	0%	No	
223	Install DO Probes	2 days	Fri 11/28/25	Mon 12/1/25	220	0%	No	
224	Install Diffusers (x4 basins)	20 days	Fri 1/30/26	Thu 2/26/26	269FS-30 days	0%	No	
225	Install 12" Chlorinated Effluent (50 LF)	5 days	Fri 2/27/26	Thu 3/5/26	224	0%	No	
226	Electrical	20 days	Tue 12/2/25	Mon 12/29/25	223	0%	Yes	Electrician
235	**Chemical Feed**	**93 days**	**Tue 9/16/25**	**Thu 1/22/26**		**13%**	**No**	
237	Install Chlorine Feed Interior Pipe	2 days	Mon 1/5/26	Tue 1/6/26	249	0%	No	
238	Install Alum Feed Interior Pipe	2 days	Wed 1/7/26	Thu 1/8/26	237	0%	No	
239	Electrical	10 days	Fri 1/9/26	Thu 1/22/26	238	0%	Yes	Electrician
240	**Disk Filter & Pumps**	**44 days**	**Thu 10/16/25**	**Tue 12/16/25**		**57%**	**No**	
243	Install Filter	2 days	Thu 11/20/25	Fri 11/21/25	242	0%	No	
244	Install Pumps	2 days	Mon 11/24/25	Tue 11/25/25	243	0%	No	
245	Electrical	15 days	Wed 11/26/25	Tue 12/16/25	244	0%	Yes	Electrician
246	**Headworks/Grit Removal**	**50 days**	**Mon 12/8/25**	**Fri 2/13/26**		**0%**	**No**	
247	Install Grit Fine Screen System	7 days	Mon 12/8/25	Tue 12/16/25	90	0%	No	
248	Install Grit Removal System	10 days	Wed 12/17/25	Tue 12/30/25	247	0%	No	
249	Install Grit Classifier/Discharge Screw	3 days	Wed 12/31/25	Fri 1/2/26	248	0%	No	
250	Install Catwalk Framing & Grating	10 days	Mon 1/5/26	Fri 1/16/26	249,56	0%	No	
251	Install Catwalk Handrail	5 days	Mon 1/19/26	Fri 1/23/26	250	0%	No	
252	Install Fab to Screen Tank	3 days	Mon 1/26/26	Wed 1/28/26	251	0%	No	
253	Install Grit Screen Bypass Fab Pipe	2 days	Thu 1/29/26	Fri 1/30/26	252	0%	No	
254	Install Grit Removal Effluent Pipe	5 days	Mon 2/2/26	Fri 2/6/26	253	0%	No	
255	Install 4" Disk Filter Drain Fab	3 days	Mon 2/9/26	Wed 2/11/26	254	0%	No	
256	Install 3" Screw Press Drain Fab	3 days	Mon 2/9/26	Wed 2/11/26	254	0%	No	

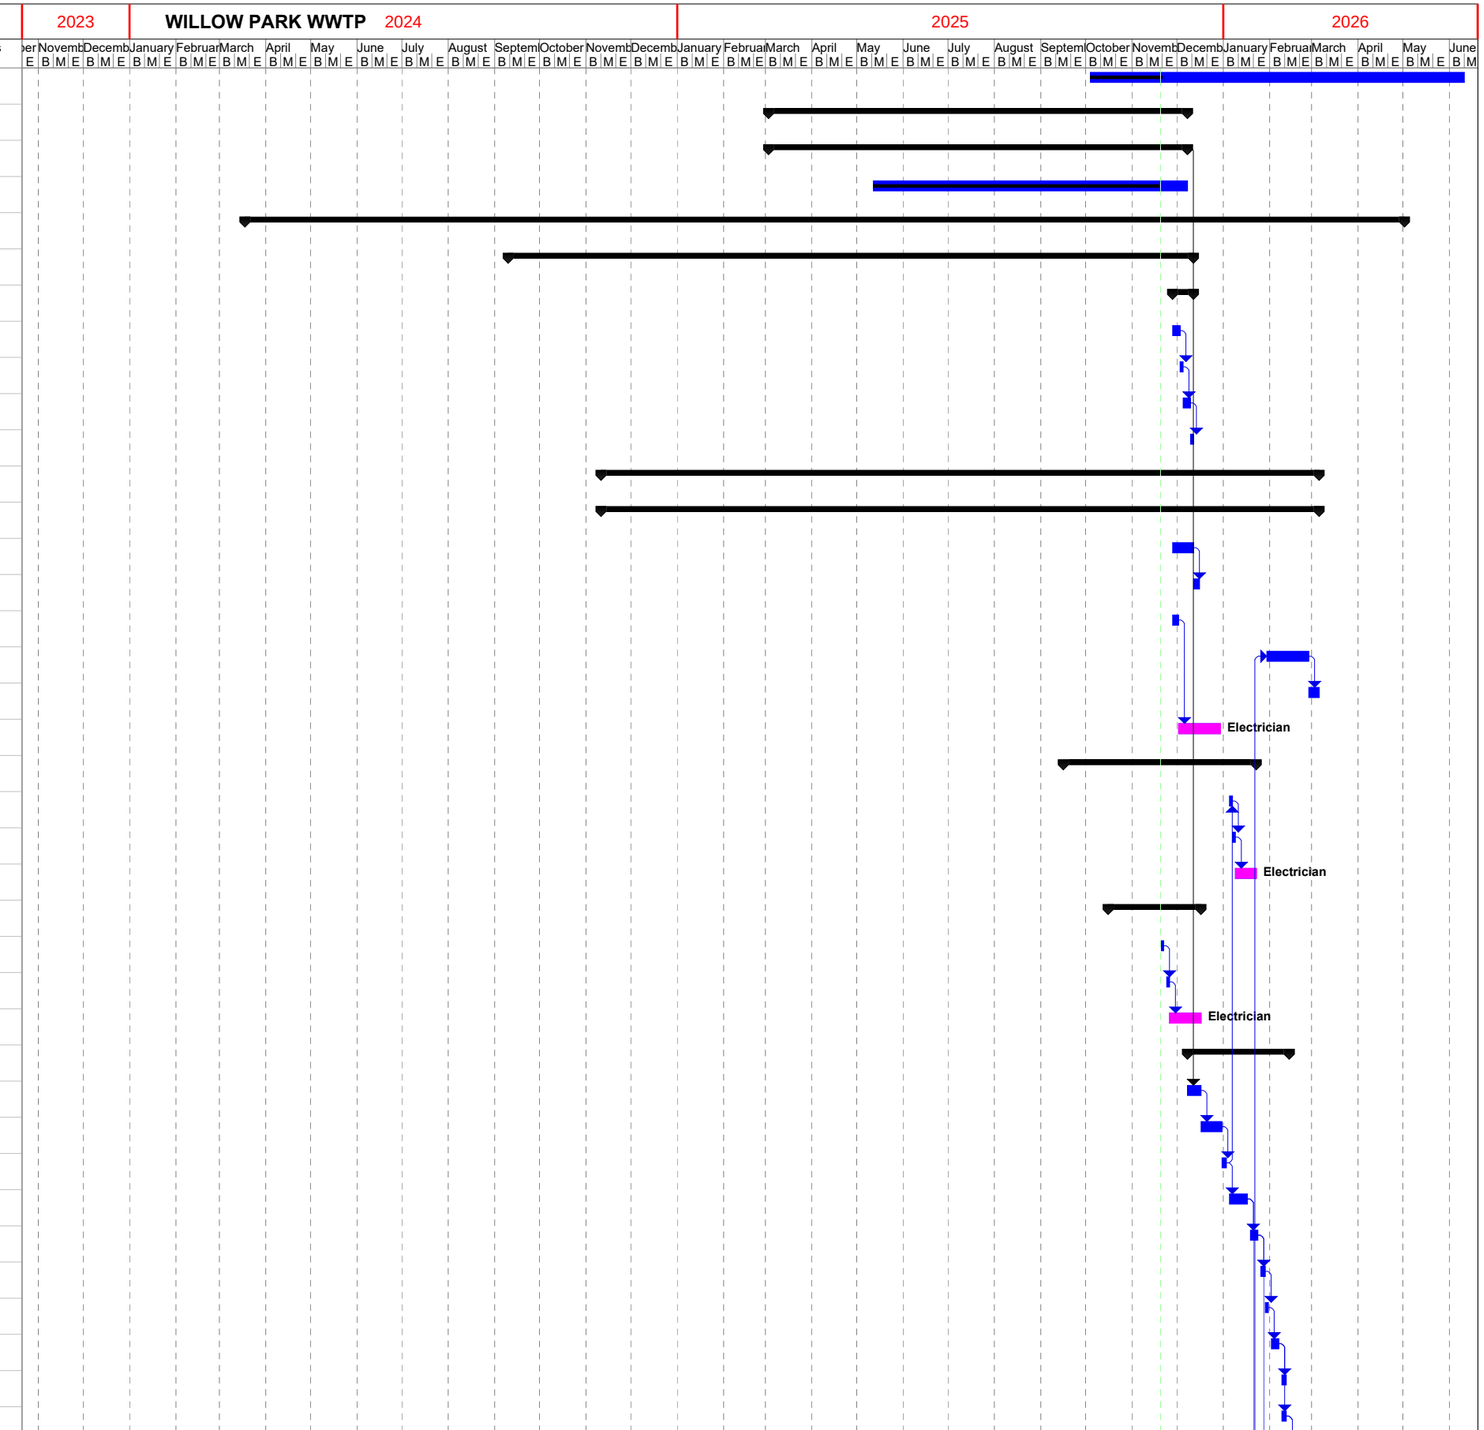
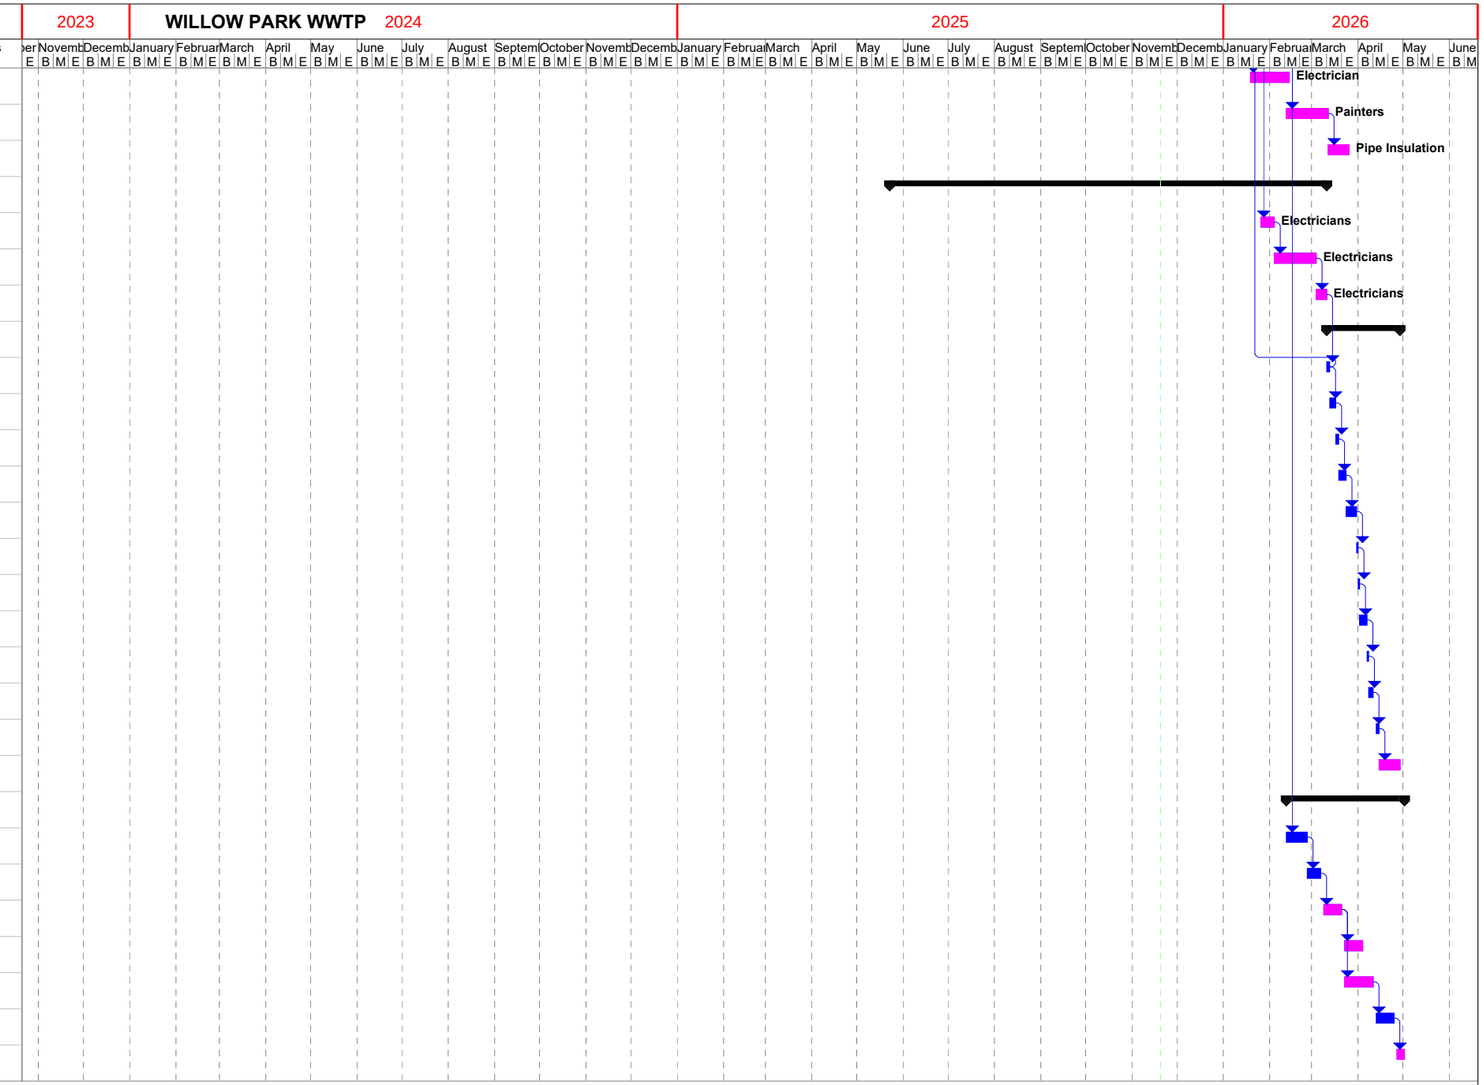
ID	Task Name	Duration	Start	Finish	Predecessors	% Complete	Flag1	Resource Names
257	Electrical	20 days	Mon 1/19/26	Fri 2/13/26	250	0%	Yes	Electrician
258	Paint Fab Piping	20 days	Thu 2/12/26	Wed 3/11/26	256	0%	Yes	Painters
259	Insulate Exposed Piping	10 days	Thu 3/12/26	Wed 3/25/26	258	0%	Yes	Pipe Insulation
260	**Electrical**	**208 days**	**Fri 5/23/25**	**Tue 3/10/26**		**58%**	**No**	
265	Install Instrumentation	7 days	Mon 1/26/26	Tue 2/3/26	251	0%	Yes	Electricians
266	Install SCADA Equipment	20 days	Wed 2/4/26	Tue 3/3/26	265	0%	Yes	Electricians
267	Terminations/Testing	5 days	Wed 3/4/26	Tue 3/10/26	266	0%	Yes	Electricians
268	**Start-Up & Testing**	**35 days**	**Wed 3/11/26**	**Tue 4/28/26**		**0%**	**No**	
269	Fill Basins for Diffuser Testing	2 days	Wed 3/11/26	Thu 3/12/26	267	0%	No	
270	Start-Up Blowers	2 days	Fri 3/13/26	Mon 3/16/26	269	0%	No	
271	Leak Test Diffusers	2 days	Tue 3/17/26	Wed 3/18/26	270	0%	No	
272	Start-Up Grit Removal System	3 days	Thu 3/19/26	Mon 3/23/26	271	0%	No	
273	Install/Start-Up Mixers	5 days	Tue 3/24/26	Mon 3/30/26	272	0%	No	
274	Start-Up Effluent Pumps	1 day	Tue 3/31/26	Tue 3/31/26	273	0%	No	
275	Start-Up Vertical Turbine Pump	1 day	Wed 4/1/26	Wed 4/1/26	274	0%	No	
276	Start-Up Disk Filter & BW Pumps	3 days	Thu 4/2/26	Mon 4/6/26	275	0%	No	
277	Start-Up Progressive Cavity Pump	1 day	Tue 4/7/26	Tue 4/7/26	276	0%	No	
278	Start-Up Sludge Dewatering & Conveyor	3 days	Wed 4/8/26	Fri 4/10/26	277	0%	No	
279	Start-Up Chlorine & Alum Feed	2 days	Mon 4/13/26	Tue 4/14/26	278	0%	No	
280	Final SCADA/Instrumentation Testing	10 days	Wed 4/15/26	Tue 4/28/26	279	0%	Yes	
281	**Sitework**	**57 days**	**Thu 2/12/26**	**Fri 5/1/26**		**0%**	**No**	
282	Finish Grade Site	10 days	Thu 2/12/26	Wed 2/25/26	256	0%	No	
283	Install Concrete Around Lift Station	7 days	Thu 2/26/26	Fri 3/6/26	282	0%	No	
284	Install Crushed Stone Base	10 days	Mon 3/9/26	Fri 3/20/26	283	0%	Yes	
285	Install Crushed Stone Roads	10 days	Mon 3/23/26	Fri 4/3/26	284	0%	Yes	
286	Install Chain Link Fencing & Gates	15 days	Mon 3/23/26	Fri 4/10/26	284	0%	Yes	
287	Finish Grade Exterior Fencing (topsoil)	10 days	Mon 4/13/26	Fri 4/24/26	286	0%	No	
288	Hydromulch/Seed	5 days	Mon 4/27/26	Fri 5/1/26	287	0%	Yes
