



CONTRACT FOR SERVICES AMENDMENT NO. ELEVEN

ADDITIONAL SERVICES AUTHORIZATION

The following modifications to the contract ("Contract") for Wilkinson Garden Area Roadway Drainage Improvements 20090089.00.AG dated March 23, 2009 between The City of Augusta (OWNER) and W.K. Dickson & Co., LLC *an Ardurra Company* (CONSULTANT) are authorized.

1. SCOPE OF SERVICES.

CONSULTANT issued drawings for bid on June 30th, 2025. OWNER initiated utility coordination with the following utilities via Procore on July 14th, 2025:

- Augusta Utilities
- Comcast
- Unity Fiber, LLC
- DC Blox Fiber
- Southern Company
- Crown Castle
- WOW
- AGL/SEC
- SEGRA
- Jefferson Electric Cooperative
- AT&T
- Century Link/Lumen & Level 3

OWNER has provided marked-up drawings from Comcast and AUD. AT&T has indicated that they will be relocating most, if not all, facilities in conflict, but no drawings or location information have been provided as of September 24, 2025. Georgia Power has not provided any documentation, but email correspondence has indicated that they are working on relocation plans.

OWNER provided GIS locations for sanitary sewer and water which were included in the original design plans. It was noted in previous design correspondence that some of those facilities would require relocation or the design would require revision to accommodate the existing locations.


CONSULTANT proposes to coordinate with utility providers listed above to secure feedback on utilities in the immediate area of proposed improvements. CONSULTANT will allow four (4) weeks from initial contact for utility providers to respond. CONSULTANT will then compile a red line document to present to OWNER for review. If new information is received after the review period, additional services may be required to produce final document for review.

CONSULTANT proposes assessment of existing Augusta Utilities Department (AUD) owned sanitary sewer along Calvary Drive, Barnes Road and Kratha Drive. Based on current design, relocation of this sewer will be required. To complete this, CONSULTANT has engaged a SUBCONSULTANT to provide survey and underground utility locate services. CONSULTANT assumes the sewer re-routes will remain in the existing public R/W. Additional survey outside of the R/W will be additional services. No additional easements are assumed as a part of this scope.

An additional set of utility plans will be added to the Issued for Bid set, dated June 30, 2025. Roadway profiles of the affected areas will be revised to show proposed sanitary sewer adjustments. All changes to drawings will be clouded with revision date added to border and cover. See Exhibit 1 below for areas of survey and design. Additional survey or design outside of the areas highlighted the map will require additional services.

CONSULTANT proposes one (1) review meeting with OWNER to identify conflicts with existing utilities and review sanitary sewer redesign. It is assumed that the redesign of utilities not owned by the City of Augusta and/or AUD will be handled by the utility provider. CONSULTANT will also participate in 10 bi-weekly update meetings as requested by OWNER.

Exhibit 1 Project Area

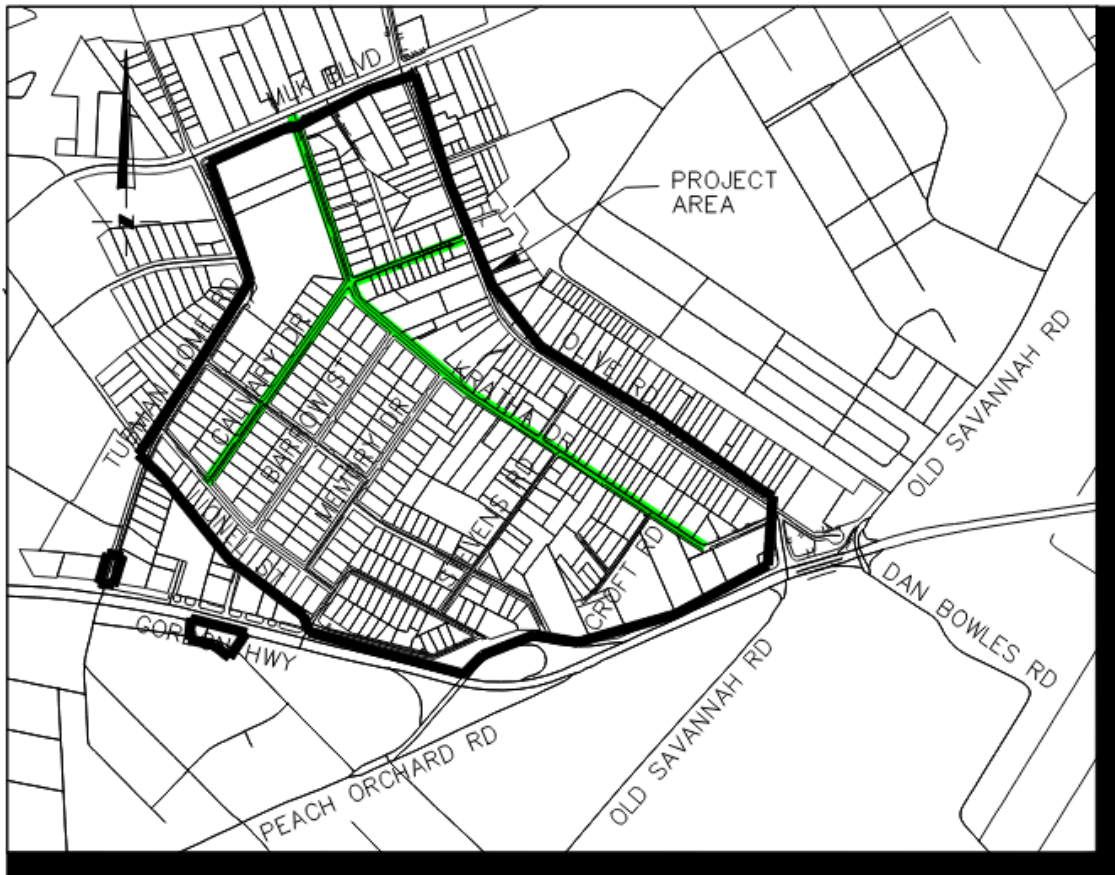

2. TIME OF PERFORMANCE. CONSULTANT's time of performance for the above additional services shall be 11 weeks from execution of this amendment.
3. COMPENSATION. The total Contract lump sum is increased from \$940,400.00 to \$997,940.00.

All other terms of the Contract remain unchanged.

OWNER:

CITY OF AUGUSTA

By: _____

Name: _____

Title: _____

Date: _____

CONSULTANT:

W.K. DICKSON & CO., LLC
an Ardurra Company

By: 

Name: Lisa Wells

Title: Practice Director

Date: 10/7/2025
