

Waterline Replacement & Upsizing (Taco Casa) Project #WA2506 *CHANGE ORDER*

PRESENTED TO THE CITY COUNCIL

JANUARY 5, 2026

SUMMARY

The Waterline Replacement & Upsizing (Taco Casa) Project addresses capacity and reliability issues with the existing 2” dead-end water line by upsizing, looping, and rehabilitating the line.

The project was advertised on July 11 and July 18, 2025, with proposals accepted through Bonfire from July 11 to July 31, 2025. The advertisement was sent to 748 vendors utilizing three commodity codes, and four submissions were received. The item did not meet the threshold for Council approval and was therefore authorized administratively. However, the formal solicitation process was utilized.

BACKGROUND

The Waterline Replacement & Upsizing (Taco Casa) Project addresses capacity and reliability issues with the existing 2-inch dead-end water line, which was undersized and not part of a looped system.

The project replaced the old line with a new 8-inch PVC main and extended it to connect with another dead-end line to the northeast, creating a looped network that improves reliability, water circulation, and overall capacity.

Construction is complete, the new line is active, and the contractor is finishing final cleanup. The upgraded line will provide improved service and long-term system reliability for the area.




CONSTRUCTION CHANGE ORDER

- The additional construction within this change order consists of installing a 5/8" service connection, 25 square yards of pavement replacement, and one 8" gate valve for the completion of the Waterline Replacement and Upsizing (Taco Casa) Project.
 - Amendment Amount: \$13,667.60
 - Total Contract amount: \$106,892.60
-
- Amendment within budgeted funds (\$142,220 Construction Budget)
 - Change order necessary due to rehabilitation scope change – these items were not included within the original schedule of values for the Project

TIMELINE

- Contract Amendment: January 5, 2026
- Estimated Project Completion January 2026

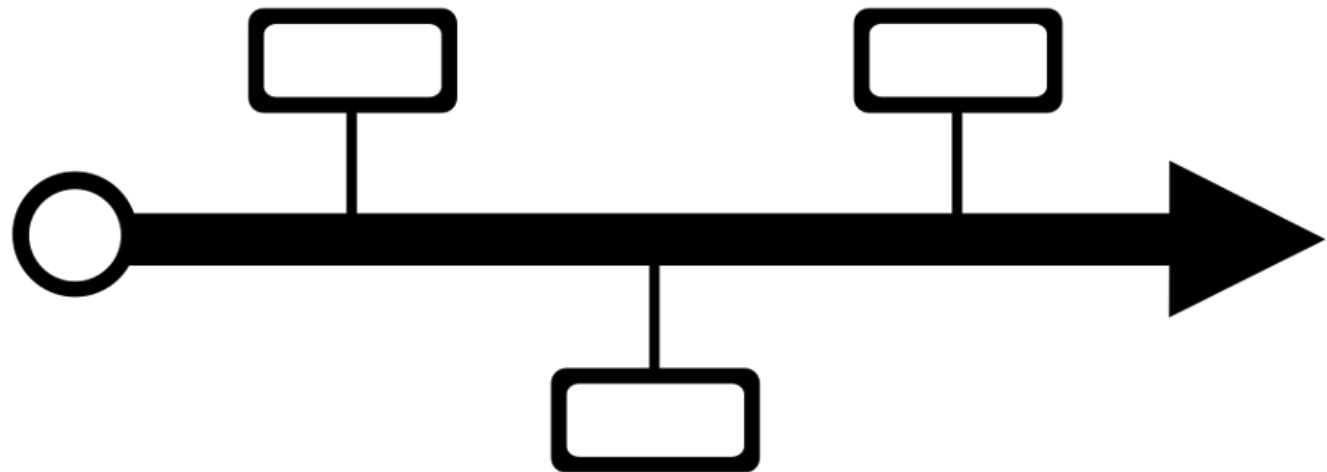

ACTION REQUESTED

Consider and take possible action on a change order to a construction contract with Pipe Crew, LLC, for the Waterline Replacement and Upsizing (Taco Casa) Project in the amount of \$13,667.60, for a revised total contract amount of \$106,892.60.



Questions/Comments

Randy Morrison, PE

Director of Capital Engineering

rmorrison@burlesontx.com

817-426-9612
