

**CHANGE ORDER NO.: 01**

Owner: Effingham County Board of Commissioners  
 Engineer: Hussey Gay Bell  
 Contractor: Southern Civil, LLC  
 Project: Hodgeville Lift Station #4 Improvements  
 Contract Name: Hodgeville Lift Station #4 Improvements  
 Date Issued: 09/19/2023

Owner's Project No.: ITB 22-105-003  
 Engineer's Project No.: 120224450

Effective Date of Change Order: 1/16/2024

The Contract is modified as follows upon execution of this Change Order.

Description: Adjustments to the scope of work include modifications to bypass pump discharge piping, installation of pump three valves and piping, rearrangement of station discharge piping, and adjustments to stub out connection for future force main connection.

Attachments:

- Revised Issued for Construction Plan Sheet 06 marked CO No. 1 – September 11, 2023
- Change Order No. 1 Summary Form

Change in Contract Price	Change in Contract Times (0 Days)
Original Contract Price: \$ <u>3,520,533.00</u>	Original Contract Times: Substantial Completion: <u>March 16, 2023</u> Ready for final payment: <u>April 15, 2023</u>
<b>[Increase] [Decrease]</b> from previously approved Change Orders No. 1 to No. <b>[Number of previous Change Order]</b> : \$ <u>N/A</u>	<b>[Increase] [Decrease]</b> from previously approved Change Orders No.1 to No. <b>[Number of previous Change Order]</b> : Substantial Completion: <u>N/A</u> Ready for final payment: <u>N/A</u>
Contract Price prior to this Change Order: \$ <u>3,520,533.00</u>	Contract Times prior to this Change Order: Substantial Completion: <u>March 16, 2023</u> Ready for final payment: <u>April 15, 2023</u>
<b>Deduction</b> this Change Order: \$ <u>38,400.00</u>	<b>[Increase]</b> this Change Order: Substantial Completion: <u>April 9, 2024</u> Ready for final payment: <u>May 9, 2024</u>
Contract Price incorporating this Change Order: \$ <u>3,482,133.00</u>	Contract Times with all approved Change Orders: Substantial Completion: <u>April 9, 2024</u> Ready for final payment: <u>May 9, 2024</u>

Recommended by Engineer

By: \_\_\_\_\_  
 Title: Project Engineer  
 Date: September 19, 2023

Accepted by Contractor

By: Math Dea  
 Title: Vice President  
 Date: 9/19/2023

Authorized by Owner

By: Wesley M. Cobble  
 Title: Chairman  
 Date: 01/16/2024

Approved by Funding Agency (if applicable)


By: \_\_\_\_\_  
 Title: \_\_\_\_\_  
 Date: \_\_\_\_\_

**Hodgeville Lift Station #4 Change Order No. 01 Summary**

<b>Item No.</b>	<b>Description</b>	<b>Qty</b>	<b>Unit</b>	<b>Unit Cost</b>	<b>Total Cost</b>
1	12-inch RJ DIP Force Main installed by Open-Cut	(-)8	LF	\$100.00	(\$800.00)
2	18-inch RJ PVC Force Main installed by Open-Cut	(-)20	LF	\$150.00	(\$3,000.00)
3	18-inch C900 PVC Force Main installed in 24-inch Steel Casing installed by Jack and Bore	(-)40	LF	\$1,125.00	(\$45,000.00)
4	12-inch RJ 45° Bend	(-)5	EA	\$950.00	(\$4,750.00)
5	12-inch RJ 22.5° Bend	(-)1	EA	\$950.00	(\$950.00)
6	12-inch RJ 11.25° Bend	(-)1	EA	\$950.00	(\$950.00)
7	12-inch RJ Wye	4	EA	\$2,010.00	(\$8,040.00)
8	18-inch x 12-inch RJ Reducer	1	EA	\$2,200.00	(\$2,200.00)
9	18-inch RJ Plug	1	EA	\$1,500.00	(\$1,500.00)
10	Adjustments to Elevated Concrete Structure Connected to Wetwell	1	LS	\$250.00	(\$250.00)
11	Relocate Generator Closer to Electrical Control Building	1	LS	\$100.00	(\$100.00)
12	12-inch RJ 90° Bend	4	EA	\$1,050.00	\$4,200.00
13	12-inch RJ Tee	4	EA	\$2,010.00	\$8,040.00
14	12-inch RJ Plug	1	EA	\$750.00	\$750.00
15	Installation of Pump No. 3 Above Ground Valves and Piping	1	LS	\$16,150.00	\$16,150.00
<b>Sum of Change</b>					<b>(\$38,400.00)</b>

- Items in red are assumed to be credited items.
- Items in black are considered as an additional price to the original bid.

- NOTES:
1. CONTRACTOR RESPONSIBLE FOR THE CONTINUED OPERATION OF THE PUMP STATION DURING CONSTRUCTION.
  2. ANY BYPASSING OF THE PUMP STATION IS THE RESPONSIBILITY OF THE CONTRACTOR.
  3. ALL BYPASSING PLANS MUST BE APPROVED BY THE OWNER PRIOR TO INSTALLATION.
  4. ALL DIP PIPING MUST BE COATED WITH 401 LINING.
  5. EXISTING WELLS AND PROPOSED WELLS ARE TO BE COATED WITH 401, OR EQUIVALENT.
  6. ALL DISTURBED AREAS WITHIN THE LIFT STATION FENCING ARE TO HAVE WEED BLOCK AND 4" OF C&G UNLESS PAVED.
  7. ALL DISTURBED AREA OUTSIDE OF THE LIFT STATION FENCING ARE TO BE SEEDED PER SHEET 14 UNLESS PAVED.

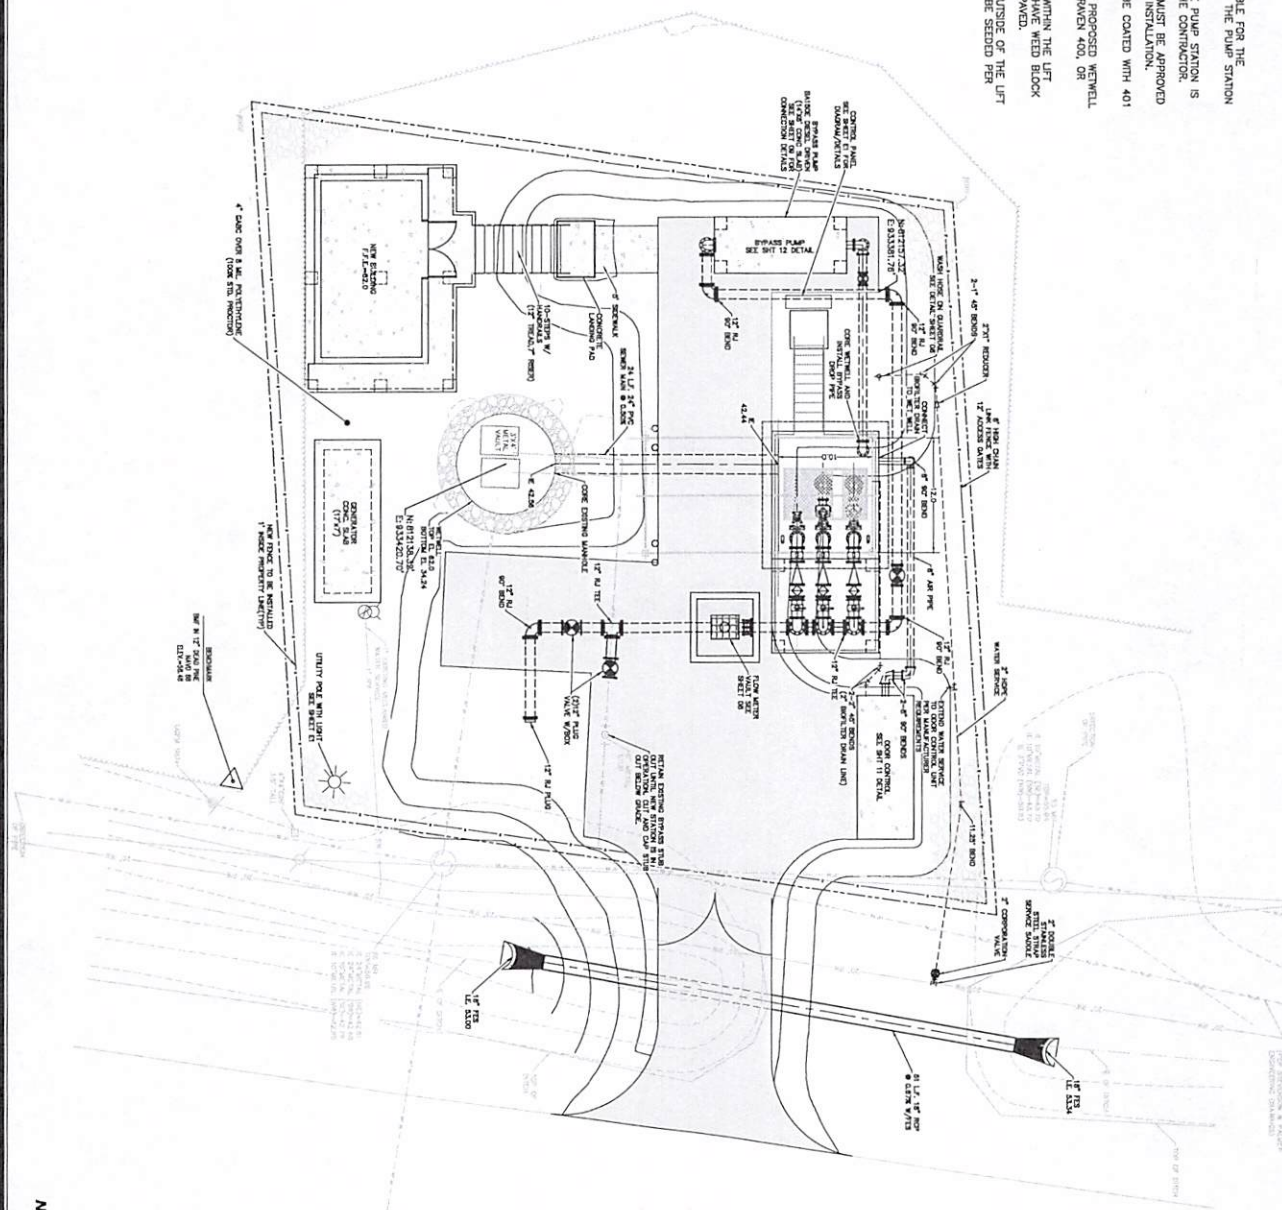

NOTE: ALL ELEVATIONS ARE NAVD 1988.  
 ISSUED FOR CONSTRUCTION JULY 28, 2022

DRAWING NUMBER <h1 style="font-size: 2em;">06</h1>	<b>HODGEVILLE LIFT STATION #4 IMPROVEMENTS</b> FOR THE EFFINGHAM COUNTY BOARD OF COMMISSIONERS <b>PROPOSED SITE PLAN</b>		REVISIONS: A CO No. 1 - SEPTEMBER 11, 2023	<b>HUSSEY GAY BELL</b> <i>Established 1958</i> 329 COMMERCIAL DRIVE, SAVANNAH, GA 31406 / T:912.354.4626		
	DATE: JULY 2022 DRAWN BY: [Name] CHECKED BY: [Name]	PROJECT NO.: [Number]	SCALE: AS SHOWN			
