



September 3, 2026

Exhibit A

Michelle Dunson, P.E., CFM
City of Madison (the "Client")
100 Hughes Road
Madison, AL 35758

**Re: Agreement Modification for Professional Engineering Services
Town Madison Blvd and I-565 Intersection Improvements**

Ms. Dunson,

Ivaldi Engineering, PLLC ("Engineer") would like to thank you for the opportunity to provide the requested modification to the agreement for professional services on the above-referenced project.

We propose to offer the following services:

1. Survey Services
2. Design Phase Services

This proposal, including the fees stated herein, is valid for 10 business days from the date of this letter. If not executed within that period, the proposal is subject to revision and re-issuance by Ivaldi. A more detailed project-specific Scope of Services and our fees is attached as Exhibit "A". Please sign the acknowledgment below to authorize the modifications to the contract described in Exhibit "A". Again, we thank you for the request. If you have any questions, please do not hesitate to contact us. We look forward to continuing to work with you on this project.

Sincerely,

A handwritten signature in blue ink, appearing to read "Eric Bonds".

Eric Bonds, P.E.
Ivaldi Engineering, PLLC
COO & Founding Partner

Acknowledgment:

Attachments

- ◆ Exhibit "A" Scope of Services
- ◆ Exhibit "B" Professional Services Agreement

Cc: File


EXHIBIT "A"
Town Madison Blvd and I-565 Intersection Improvements
PROPOSED SCOPE OF SERVICES
SEPTEMBER 3, 2026

Ivaldi's proposed scope of services is presented in the following elements:

- I. Project Description
- II. Scope of Services
- III. Time of Performance
- IV. Client's Responsibilities
- V. Deliverables
- VI. Compensation

I. PROJECT DESCRIPTION

ALDOT plan review comments received from Matthew Johnson, P.E., ALDOT Local Transportation Engineer, and associated ALDOT plan reviewers, forwarded by Michelle Dunson. The comments require revisions to the previously completed plan set to conform to ALDOT standards for locally administered projects. The comments also required an easement exhibit for the work being done outside of the Right-Of-Way in the stadium parking lot. This work was not included in the original scope of services.

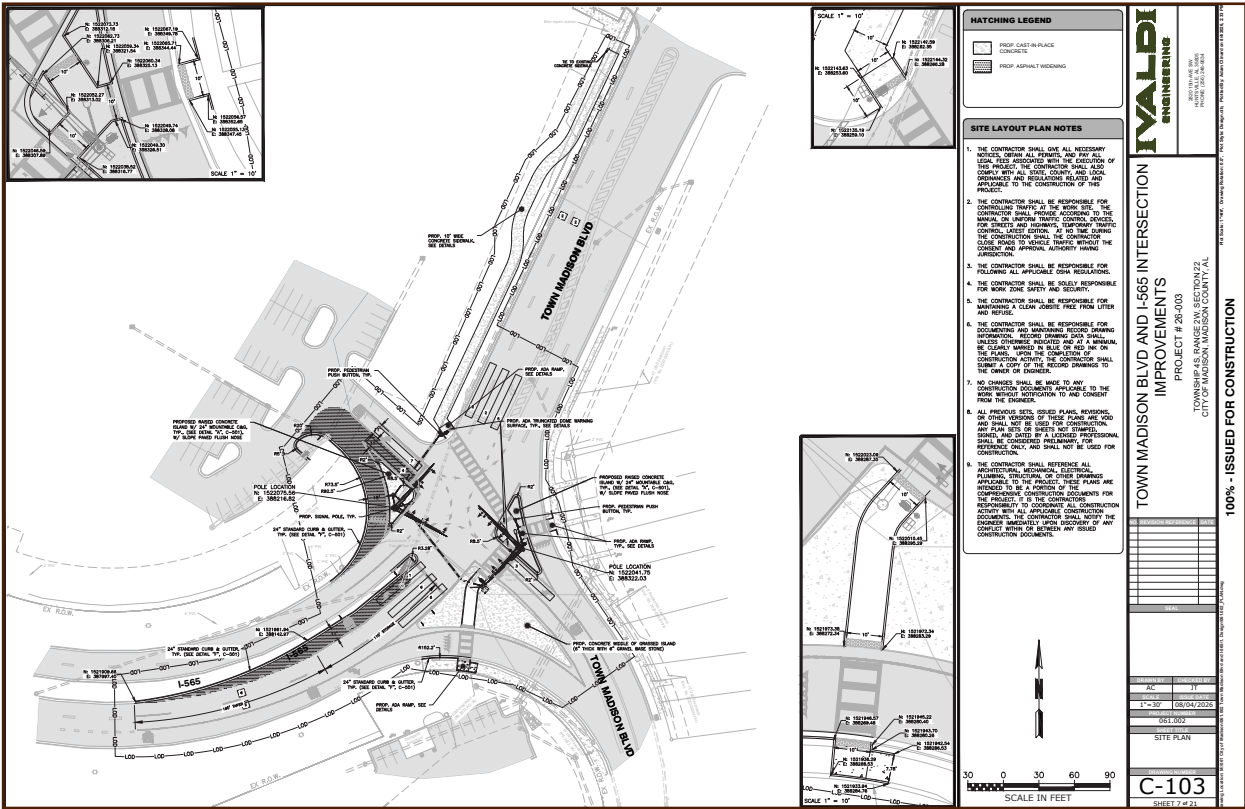

II. SCOPE OF SERVICES

1. SURVEYING SERVICES

A. SKETCHES AND EXHIBITS

The Engineer will provide 1 (one) additional exhibit describing the areas of proposed Temporary Construction Easements (TCE) and Utility and Drainage Easements for this project. This includes two (2) revisions due to review.

2. DESIGN PHASE SERVICES

A. FINAL CONSTRUCTION DOCUMENTS PHASE

The Final Construction Documents Phase represents 100% project completion.

1. PLAN FORMATTING AND DETAILS

Convert to the ALDOT standard title sheet with signature blocks for the engineer of record and City representative; replace traffic control sheets with ALDOT TCP sheets from the Traffic Control Detail Library; add project alignment and stationing across all plan sheets; and label begin project, end project, and end work locations.

2. QUANTITIES AND PAY ITEMS

Break out traffic signal items into individual ALDOT pay items with calculated quantities in lieu of lump sum; add stripe widths to permanent long-line stripe descriptions; remove the traffic control scheme item from Sheet 4; and reclassify bituminous pavement removal under unclassified excavation.

3. TRAFFIC SIGNAL PLANS

Incorporate ALDOT standard signal and ITS legend sheets and the standard traffic signal note sheet; add a removal diagram and design timings to the signal layout; reference the applicable TSOP from ALDOT standard drawings; and coordinate the City's written approval request for any manufacturer-specific signal equipment.

4. SIGNING AND PAVEMENT MARKINGS

Revise overhead street name sign details to remove directional arrows and relocate advance directional signage; consolidate signal-mounted signs onto the signal layout sheet; revise crosswalk markings to conform to ALDOT standard drawings and the MUTCD; and revise thermoplastic callouts to Class 2A.

5. ALDOT REVIEWS

We have received other comments from ALDOT that we will address via plan modification or a rebuttal letter. This scope only includes time to address current comments received by the date of this letter. Additional comments received may be considered an additional service.

III. TIME OF PERFORMANCE

Subject to your authorization, Ivaldi is prepared to begin work immediately and continue through completion. Plans are estimated to be ready for submittal to the LIA no later than 4 weeks after Ivaldi receives written notice to proceed from the Client. Client-initiated revisions to the project layout or program after our services commence may require an adjustment in fee and schedule. This schedule is based on Ivaldi's current workload and is subject to change if notice to proceed is not provided within 15 business days.

IV. COMPENSATION

FEES		
DESCRIPTION	FEE TYPE	FEE
Sketches and Exhibits	Lump Sum	\$1,320.00
Final Design	Hourly, NTE	\$11,200.00
CHANGE ORDER #2	\$12,520.00	
Original Contract	\$79,457.50	
Change Order #1	\$11,595.00	
Modified Contract CO #1	\$91,052.50	
Modified Contract CO #2	\$103,572.50	
MODIFIED CONTRACT	\$103,572.50	

