



NORMAN FORWARD Implementation Plan
May 2016
Revised 3/2023

NORMAN FORWARD

Implementation Plan

I. Executive Summary

NORMAN FORWARD is designed to improve the quality of life in Norman through renovating, expanding, constructing, and funding projects including multiple recreational facilities, libraries, parks, athletic venues, public art, trails, and swim complexes. NORMAN FORWARD also includes traffic improvements and an extension of the existing James Garner Avenue. A citizen-initiated proposal, NORMAN FORWARD will enhance the Norman community for generations to come.

Funded through a 15-year earmarked sales tax, NORMAN FORWARD includes 12 projects spanning the entire city at an estimated cost of \$148 million. It also includes other program expenses at an estimated cost of \$55.4 million. Sales tax collections began on January 1, 2016 and will continue for 15 years.

The NORMAN FORWARD program includes:

- Canadian River Park
- Central Branch Library
- East Branch Library
- Griffin Land Acquisition
- Indoor Aquatic Center
- Indoor Multi-Sport Facility
- James Garner Avenue Extension
- Parks Projects
 - Westwood Tennis Center
 - Saxon Park
 - Ruby Grant Park
 - Andrews Park
 - Existing Neighborhood Park Renovations
 - New Neighborhood Park Development
 - New Trail Development
- Senior Citizens Center
- Sports Complex Projects
 - Reaves Park
 - Softball & Football Complex
 - Griffin Park Soccer Complex
- Traffic Improvements
- Westwood Family Aquatic Center

The City is moving forward with the projects and the Implementation Plan is guiding the process. The Implementation Plan is a document to be reviewed and recommended by the NORMAN FORWARD Citizen Financial Oversight Board and adopted by the City Council, which outlines the scopes of work, conceptual budgets, and the order in which the projects or phases of projects will commence. The Implementation Plan is a living document which will be reviewed, re-evaluated, and re-adopted from time to time as projects progress and plans become realities.

As of this writing, six of the major NORMAN FORWARD projects have been completed, or are nearing completion:

- The East Branch Library
- The Central Branch Library
- The Westwood Family Aquatic Center
- The Westwood Tennis Center
- The Ruby Grant Park (Phase I)
- The Andrews Park Redevelopment

Several other NORMAN FORWARD projects are partially completed (progressing in stages) or nearing construction phases. Neighborhood park renovation projects have been completed at Oakhurst, Sonoma, Prairie Creek, Rotary, Sequoyah Trail, Vineyard and Cherry Creek parks. Several other renovations have begun at Earl Sneed, Sutton Place, William Morgan, Tull's, Eastridge and Royal Oaks parks. New park construction at Songbird Park has been completed; and we have started construction at the new park in the Summit Valley/Bellatona neighborhood (officially to be named "Bentley Park"). The NORMAN FORWARD program is already transforming the quality of life in Norman.

In February 2016, ADG, P.C. was hired as the program manager for the NORMAN FORWARD program. Since that time, ADG has attended meetings, conducted research, and analyzed data to prepare the Implementation Plan. The information in the Implementation Plan is based on currently available information as well as certain assumptions made based on anticipated requirements.

II. Background

The History of NORMAN FORWARD

The NORMAN FORWARD initiative came to City Council from community groups, stakeholders, and residents, who prepared an initial program scope using analysis and information from master plans for the libraries and parks, recreational planning professionals, traffic professionals, and research firms.

Beginning in the spring of 2015, Norman City Council began a series of Council conferences and additional public meetings to refine the program scope, financing, and funding opportunities for NORMAN FORWARD. Priority projects are included from the 2014 *Library Master Plan Update*, the 2009 *Norman Parks & Recreation Master Plan*, and additional projects designed to provide recreational and educational opportunities for Norman residents.

The program is intended to improve the quality of life for all Norman residents and visitors by providing public projects and programming that contribute to better health, more active lifestyles, intellectual and arts pursuits, and improved traffic safety. The program is funded by a 15-year, one-half percent earmarked sales tax.

On August 11, 2015, City Council voted unanimously to approve NORMAN FORWARD Ordinance O-1516-5 and Resolution R-1516-14 that called for an election to take place on October 13, 2015, to ask Norman voters to consider a temporary sales tax increase to provide funding for the projects.

The temporary one-half percent (1/2%) sales tax was approved by 72% of Norman voters. The authorized sales tax increase began on January 1, 2016.

Public Involvement

The NORMAN FORWARD Citizen Financial Oversight Board (CFOB) was created by Council resolution (R-1516-75) on December 22, 2015 to review the finances of the NORMAN FORWARD program. Their tasks include:

- Review actual and projected NORMAN FORWARD Sales Tax (NFST) revenues;
- Recommend mix of project financing including pay as you go ("paygo") and debt financing;
- Review pace and sequencing of construction of projects;
- Review Council actions related to expenditures of NFST monies;
- Recommend strategies for long term operations and maintenance of facilities;
- Report to Council from time to time as warranted and to provide an annual report to City Council;
- Perform such other duties related to NORMAN FORWARD as the City Council directs by motion or resolution;
- Assign one CFOB member to serve with and act as a liaison to certain advisory committees that Council may form from time to time regarding specific NORMAN FORWARD projects.

The Oversight Board consists of nine members, appointed by the Mayor and confirmed by City Council. Members are from various wards and have backgrounds and experience in accounting, banking, construction, auditing,

advertising, operations, and law. Two ex-officio members are part of the Board, including the Mayor (or designee) and City Manager (or designee).

Ad hoc advisory groups were appointed by the Mayor to provide additional citizen input specific to each major NORMAN FORWARD project and to City Council. One member of the Oversight Board serves on each ad hoc advisory group. Ad hoc groups have five to eleven members each. Ex-officio members include the City Manager (or designee), a CFOB member, a Park Board Member, and may include a member, or members, of specific stakeholder groups.

All Oversight Board and ad hoc advisory group meetings are open to the public and shall comply with the Oklahoma Open Meetings Act. The public is invited to attend meetings and provide input and comments to the ad hoc advisory groups and Oversight Board.

Process

The NORMAN FORWARD Implementation Plan sets the overall guidelines for program scope, project scheduling, and individual construction budgets. Site selection and land acquisition, if applicable, will be required prior to the start of design for most projects.

Certain sites may require demolition, site clearing, or other preparatory steps. Environmental testing will also be performed, as needed, prior to building design, and if necessary, environmental remediation will be completed.

The City will solicit Requests for Qualifications (RFQ) from consultants, such as architects and engineers. Responses to RFQs will be reviewed using the City's consultant selection process.

Documents produced by each consultant will undergo peer reviews conducted by the City staff and Program Manager. The purpose of these reviews is to monitor consultant plans and specifications for conformance with the design intent and the allocated budget. At selected phases of the design process, the ad hoc advisory groups and the Citizens Financial Oversight Board may receive presentations from consultants in order to review the designs.

Once the final design of a project has been approved, the City will utilize its standard competitive bidding process to solicit and award construction contracts. "Construction Manager at Risk" processes may be used, combining several of the design, bidding and construction phases, for certain projects. The architects and/or engineers will review construction progress, and the Program Manager will provide additional field observation for conformance with construction documents.

Throughout the process, the City staff and Program Manager will provide outreach to citizens through communication on the status of each project.

Communication

As with any large, capital improvement program, communication with the public is critical for the success of NORMAN FORWARD. In addition to the high level of citizen participation through the Citizens Financial Oversight Board and the ad hoc advisory groups, ongoing communication and information will be made available to the public through various avenues and outlets.

Communication methods include but are not limited to:

- A quarterly electronic newsletter to stakeholders
- Promotion and updates via print media, television, social media outlets including Facebook and Twitter
- Updates and promotion in partnership with the Norman Chamber of Commerce via the Chamber's newsletter and website
- Routine press releases about public meetings, surveys, and other updates sent to various outlets including the *Norman Transcript* and Norman News
- Updates in the City Manager's weekly report to City Council, which is also sent to the *Norman Transcript*, posted to the City Manager's webpage, and promoted on Facebook
- Updates in the City Manager's report at City Council meetings; videos from these updates are posted to the City Manager's webpage, promoted on Facebook, and uploaded to YouTube
- Routine updates to the NORMAN FORWARD website
- Branded NORMAN FORWARD construction signs
- Public construction groundbreakings and ribbon-cuttings
- Open houses, videos, and tours of projects in-progress
- Meetings posted on government access television
- Inclusion in the City of Norman Annual Report

Implementation Plan Development

The information in the Implementation Plan and Project Timeline is based on currently available information as well as certain assumptions made based on anticipated requirements. The Project Timeline, scope of work, and budgets are subject to change, as directed by Council, as the planning process progresses and more information becomes available.

Project budgets may include: conceptual estimates of consulting, architectural, and engineering services; other pre-construction costs such as environmental investigation, remediation, and geotechnical and construction testing, where required; infrastructure; land acquisition; and construction and project contingency.

The construction budgets are based on information from a number of sources including local and national cost estimating firms, industry consultants, and data from the City of Norman. Construction budgets are conceptual and are derived from anticipated scopes of work needed for complete projects. Actual project costs may vary from initial cost estimates depending on final work scopes, the bidding climate at the time of bid, inflation and other factors impacting the economy.

Debt vs. Pay-As-You-Go Financing

The Council and the citizen's Financial Oversight Board have adopted an anticipated mix of projects to be financed on the pay-as-you-go basis, versus projects to be financed through the issuance of debt to enable the projects to proceed in advance of the actual revenues being collected to pay for the projects. Generally speaking, the following major projects are anticipated to be paid for through up-front debt financing:

Central and East Branch Libraries
Westwood Family Aquatic Center and Tennis Center Improvements
Griffin Park Soccer Complex
Reaves Park Baseball/Softball Complex
Indoor Aquatic Facilities (Young Family Athletic Center)
Indoor Multi-Sport Facility (Young Family Athletic Center)
Adult Football/Softball Complex

In order to coincide with the construction schedules of the projects, it is anticipated that there will be three separate NORMAN FORWARD debt issuances. These issuances have been made:

- Norman Municipal Authority Sales Tax Revenue Note, Series 2015B (dated December, 17, 2015) - \$43,600,000
- Norman Municipal Authority Sales Tax Revenue Note, Series 2017 (dated June 27, 2017) - \$30,950,000
- Norman Municipal Authority Sales Tax Revenue Note, Series 2020 (dated December 17, 2020) - \$22,250,000

The amount of debt that was actually issued was significantly below the originally anticipated amount, resulting in interest savings to the Norman Forward program. The other NORMAN FORWARD projects and related operational costs are anticipated to be paid for on a pay-as-you-go basis, with the projects timed to meet cash flow availability schedules over the tenure of the NORMAN FORWARD sales tax collections.

III. The Projects

The projects, their respective published budgets, and current estimates are:

Project	Published Budget	Current Estimate
▪ Canadian River Park	\$2 million	\$2,000,000
▪ Central Branch Library*	\$39 million	\$34,973,616
▪ East Branch Library*	\$5.1 million	\$4,786,483
▪ Griffin Land Acquisition	\$10 million	\$2,400,000
▪ Indoor Aquatic Center**	\$14 million	\$14,000,000
▪ Indoor Multi-Sport Facility**	\$8.5 million	\$11,528,369
▪ James Garner Avenue Extension	\$6 million	\$6,151,281
▪ Parks Projects	\$26.5 million	\$24,694,277
○ Westwood Tennis Center*	\$2 million	\$1,801,277
○ Saxon Park	\$2 million	\$2,000,000
○ Ruby Grant Park*	\$6 million	\$6,146,426
○ Andrews Park*	\$2 million	\$1,446,574
○ Existing Neighborhood Park Renovations	\$6.5 million	\$6,500,000
○ New Neighborhood Park Development	\$2 million	\$2,000,000
○ New Trail Development	\$6 million	\$4,800,000
▪ Senior Citizens Center	\$0	\$7,600,000
▪ Sports Complex Projects	\$23.5 million	\$23,500,000
○ Reaves Park	\$10 million	\$10,000,000
○ Softball & Football Complex	\$2.5 million	\$2,500,000
○ Griffin Park Soccer Complex	\$11 million	\$14,000,000
▪ Traffic Improvements	\$2.7 million	\$2,700,000
▪ Westwood Family Aquatic Center*	\$12 million	\$11,763,800
TOTAL PROJECT COSTS	\$149,300,000	\$149,097,826

* Final cost

** Combined as the Young Family Athletic Center

Components of each project budget may include: consulting, architectural, and engineering services; other pre-construction costs such as environmental investigation, remediation, and geotechnical and construction testing, where required; infrastructure; land acquisition; and construction and project

contingency. Supplemental revenue from some projects are discussed in project discussions, which follow.

Potential impacts to project budgets include, but are not limited to:

- Fluctuation in sales tax revenue
- Changes in project scopes of work
- Inflation or other uncontrollable increases in cost of construction materials
- Unforeseen circumstances
- Supplemental revenue

Canadian River Park

Description

There is potential for a park area south of Lindsey Street and west of I-35 along the Canadian River. Possibilities for development include wildlife and plant life refuges, trail facilities, and other enhancements.

Scope

If land can be reasonably acquired, a park area would be developed south of Lindsey Street, west of I-35.

Published Budget \$2,000,000

Preliminary Estimated Budget

Land Acquisition / Site Prep / Infrastructure	\$205,000
A&E / Design / Testing	\$175,000
Construction & FFE	\$1,480,000
Project Contingency	\$140,000
Total Project Budget	\$2,000,000

Timing

Architecture, engineering, and site preparation are contingent upon resolution of land transfer legalities. The ability of the City to acquire land originally contemplated for this project involves resolution of legal complexities related to current ownership and transfer rights. This project is contemplated to move forward in the last half of the program.

Central Branch Library

Description

The November 2014 *Library Master Plan Update* recommended construction of library branches as part of the Pioneer Library System (PLS). PLS is a multi-county library system serving Cleveland, McClain, and Pottawatomie counties in central Oklahoma. Each library in PLS's service area is a partnership between the library system and the city where it is located; the city provides and maintains the facility and PLS provides library staff, collections, and programming.

The new Norman Central Branch Library includes public meeting rooms, learning space, a local history collection, free wireless internet, access to technology, and programming for all ages.

Scope


The new Norman Central Branch Library relocated the existing library to a more spacious and modern facility. This branch is the main branch of both Norman and the Pioneer Library System and is approximately 82,000 square feet. The location is north of Andrews Park on City-owned land, primarily the site of the former Rhodes granary.

<i>Published Budget</i>	\$39,000,000
-------------------------	--------------

<i>Final Expenditures</i>	\$34,973,616
---------------------------	--------------

Timing

The Central Branch Library opened in November, 2019 and is providing services.

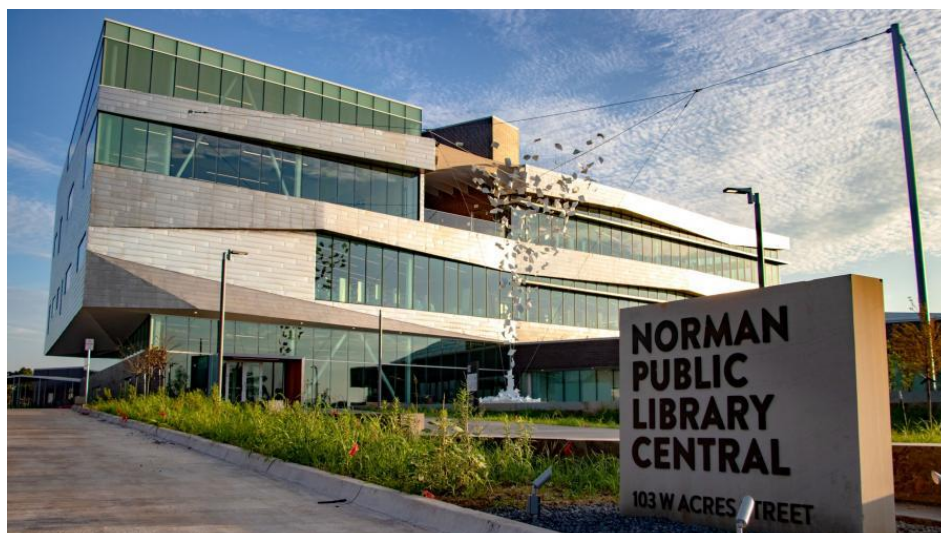

East Branch Library

Description

As the population in Norman has expanded east and west, so has the demand for library services on the east and west sides of the city. The Norman West branch opened in late 2013 and the East Branch Library expands library services to residents on the east side of the city.

The new East Branch Library opened in 2018 and includes public meeting space, free wireless internet, access to technology, and programming for all ages.

Scope

The Norman East Branch Library is approximately 12,500 square feet and located adjacent to Fire Station 9 at the intersection of Alameda and Ridge Lake Boulevard.

<i>Published Budget</i>	<i>\$5,100,000</i>
-------------------------	--------------------

<i>Final Expenditures</i>	<i>\$4,786,483</i>
---------------------------	--------------------

Timing

The East Branch Library opened in July, 2018 and is providing services.



Griffin Land Acquisition

Description

2014 Oklahoma legislation authorizes the Oklahoma Department of Mental Health and Substance Abuse Services (ODMHSAS) to sell or dispose of the Griffin property, including the current Sutton Wilderness Park, Griffin Park and Frances Cate Park. The property was proposed to be acquired by the City using NORMAN FORWARD funds, to permanently house the Griffin Park Soccer Complex and Sutton Wilderness.

Project Activities

In negotiations with the ODMHSAS, it was determined to be mutually beneficial for the City to enter into long-term leases with the ODMHSAS for the Griffin Soccer Complex land, and to maintain an existing lease for the Sutton Wilderness land. The lease agreement (Contract K-1718-136, approved on November 27, 2018) gives the City control of the property for up to a 30-year period, at which time the City has a purchase option for the land. Rental payments of \$80,000 per year, to be paid with Norman Forward funds, will apply to the ultimate purchase of the land, if so desired by the City and ODMHSAS. The Frances Cate Park land was not included in the negotiated lease for the Griffin Soccer Complex site.

The allocation of Norman Forward funds to the Griffin Land Acquisition project was reduced by the City Council from \$10,000,000 to \$2,400,000 (30 payments of \$80,000) by Resolution R-1819-110 (approved May 14, 2019) and the remaining \$7,600,000 budget was re-allocated to a Norman Forward Senior Citizen's project.

<i>Published Budget</i>	<i>\$10,000,000</i>
-------------------------	---------------------

Scope

The identified properties to be acquired are:

▪ Griffin Park & Sutton Wilderness	322.2 acres
▪ Francis Cate Park	up to 14.5 acres
<hr/>	
Total Anticipated Land Acquisition	336.7 acres

Budget

Land Acquisition	\$10,000,000
------------------	--------------

<i>Updated Cost Estimate</i>	<i>\$ 2,400,000</i>
------------------------------	---------------------

Timing

Based on the negotiated lease, rental payments to the ODMHSAS will be made annually and phased construction of the soccer complex facilities are underway. At the end of the first 15-year Norman Forward period, consideration will be made as to the purchase of the land or the continuation of the lease.

Indoor Multi-Sport and Aquatic Center (Young Family Athletic Center)

Description

The combined Indoor Multi-Sport and Aquatic Center will be named the “Young Family Athletic Center” after Norman native, NBA All-Star and University of Oklahoma alumnus Trae Young. The aquatic portion of the building will feature two pools: an 8-lane 25-meter competition pool with spectator seating and a 4-lane 25-meter pool used as a warm up pool during swim competitions. The Multi-Sport portion will each house 8 basketball courts with 12 volleyball courts.

Norman Regional Health System is developing the “NMotion” space which will serve as a sports and human performance center and physician clinic. Other Young Family Athletic Center amenities include concessions, a small retail space, administrative offices, tournament and team breakout rooms, public restrooms, and other standard support areas.

Scope

The site for the NORMAN FORWARD Young Family Athletic Center in the University North Park development has been acquired, southeast of the intersection of Rock Creek Road and 24th Avenue N.W. This site will locate the Young Family Athletic Center adjacent to a major retail and hotel lodging district, attracting regional tournaments and meets which will draw participants and their families from throughout the state of Oklahoma and the central U.S. The operating structure is dependent upon successful operating agreements between the City of Norman, Norman Public Schools, Norman Regional Health System, the Sooner Swim Club, and the chosen third-party operator, Santa Fe Family Life.

Supplemental funds have been allocated from: Norman Forward project savings; Norman Municipal Authority Revenue Bonds secured by Norman Room Tax revenue; University North Park Tax Increment Finance moneys; and a donation from the Trae Young Family Foundation, believed to be the largest private donation in Norman's history. Norman Regional Health System will pay for the portion of the project cost attributable to the “NMotion” facility.



YFAC Funding Sources

Norman Forward	\$22,500,000
Norman Forward Roads/Streets	\$328,359
Additional Norman Forward Fund Balance	\$1,500,000
Room Tax Bond	\$3,801,683
Norman Forward Trails Project	\$1,200,000
UNP TIF Fund	\$2,734,791
Trae Young Family Foundation	\$4,000,000
Norman Regional Health System	\$6,966,000
<i>Total Published Budget</i>	<i>\$43,030,000</i>

Preliminary Estimated Budget

Land Acquisition / Site Prep / Infrastructure	\$163,000
A&E / Design / Testing	\$2,425,475
Construction & FFE	\$40,018,534
Project Contingency	\$423,817
<i>Total Project Budget</i>	<i>\$43,030,000</i>

Timing

This project broke ground in July of 2021, and construction is underway with a scheduled completion of Fall 2023.

James Garner Avenue Extension

Description

The James Garner Avenue Extension will provide a north/south roadway to more efficiently carry motorists between downtown Norman and north Norman/south Oklahoma City metropolitan area. The extension will effectively create an updated entrance to the City from the north.

Scope

The extension project will extend James Garner Avenue from Acres Street, over the Robinson Street underpass, connecting to Flood Avenue. The project will include public art enhancements in commemoration of Norman native, multiple EMMY Award winning, Hall of Fame actor James Garner. The James Garner Avenue Extension will intersect with Flood Avenue with a modern roundabout north of Robinson Street.

<i>Published Budget</i>	<i>\$6,000,000</i>
<i>Railroad Quiet Zone Funds</i>	<i>\$500,000</i>
<i>Norman Utilities Authority</i>	<i>\$43,617</i>
<i>Additional Norman Forward Fund Balance</i>	<i>\$151,281</i>
<i>FHWA Funds</i>	<i>\$4,825,733</i>

Estimated Budget

<i>"Phase I" Actual Cost</i>	<i>\$1,947,283</i>
<i>"Phase II" Land Acquisition / Site Prep / Infrastructure</i>	<i>\$102,934</i>
<i>"Phase II" A&E / Design / Testing</i>	<i>\$1,402,140</i>
<i>"Phase II" Construction & FFE</i>	<i>\$7,820,546</i>
<i>"Phase II" Public Art</i>	<i>\$200,000</i>
<i>Total Project Budget</i>	<i>\$11,472,905</i>

Timing

The James Garner Extension project has been broken into "phases", to accommodate the first phase to be completed in conjunction with the opening of the new Central Branch Library. The first phase, from just south of Acres Street in the City Municipal Complex to the Central Library parking lot, has been completed. The second Phase, extending north of Robinson Street and connected to Flood Avenue, is planned to proceed in spring of 2023. City Staff has secured \$4.8 million of Federal funds for this project. The project is estimated to complete construction in spring 2024.



Parks Projects

Description

Parks all across Norman will be enhanced by NORMAN FORWARD. Additionally, new parks and trails will be developed. Plans from the Parks Master Plan will be reviewed to make sure they are still relevant to neighborhood needs.

Scope

The identified parks projects are:

- Westwood Tennis Center: conversion of two existing outdoor courts to indoor and construction of two new outdoor courts with lighting. This project has been completed (Budget: \$2,000,000; Final Cost: \$1,801,277).
- Saxon Park: develop Phase II of the Saxon Park Master Plan to include additional parking, fencing, furnishings, play area, restrooms, and event shelter (Budget: \$2,000,000).
- Ruby Grant Park: develop Phase I of the Ruby Grant Park Master Plan with utility infrastructure improvements, signage, parking, trails, practice fields, pavilion, and pedestrian lighting. This project has been completed. (Budget: \$6,000,000; Final Cost: \$6,146,426) (\$150,000 appropriated from Community Park Land Fund balance).
- Andrews Park: skate park expansion, amphitheater seating shade, landscaping, and splash pad enhancement. This project has been completed. (Budget: \$2,000,000; Final Cost: \$1,446,426).
- Existing Neighborhood Park Renovations: as per revisited 2009 Parks Master Plan recommendations. Renovations have been completed at seven parks, and two more are planned to be undertaken throughout the Norman Forward life (Budget: \$6,500,000).
- New Neighborhood Park Development – the first new neighborhood park, “Songbird Park” is complete and the new “Bentley Park” is currently underway in the Summit Valley/Bellatona neighborhood. Three more will be undertaken throughout the Norman Forward life at Southlake, Links, and Redlands. (Budget: \$2,000,000).
- New Trail Development: complete initial loop routing of Legacy Trail (Budget: \$4,800,000).

Published Budget \$25,000,000

Preliminary Estimated Budget

Land Acquisition / Site Prep / Infrastructure	\$1,440,000
A&E / Design / Testing	\$1,240,000
Construction & FFE	\$20,580,000
Project Contingency	\$1,740,000
Total Project Budget	\$25,000,000

Timing

Individual park and trail improvement projects will be undertaken on a yearly basis throughout the life of NORMAN FORWARD.

Senior Citizens Center

Description

The NORMAN FORWARD Ordinance included the following language:

To construct and to equip a Senior Center through renovation of an existing facility or construction of a new free standing facility at a location to be determined by Council, after consideration of the desires of Norman citizens who would likely use the facility, functionality of proposed facility, and feasibility including how to accomplish other voter authorized municipal complex improvements:

To be funded from proceeds that can be generated from the sale of General Obligation Bonds authorized by voters in 2008, or from revenues generated from the Norman Forward Quality of Life Projects Sales Tax of 2015, to be located in the vicinity of Andrews Park or another site shown to be reasonably available for this purpose.

The City Council began working on the Senior Citizens Center location issue early in 2016 and adopted Resolution R-1516-77, narrowing the Senior Citizens Center location options to the Existing Library site, a site in Andrews Park, and a site adjacent to the new Central Branch Library site.

After further consideration and considering the endorsement of the NORMAN FORWARD Senior Center Ad Hoc Committee, the Reaves Park Ad Hoc Committee, the Norman Senior Association, and representatives of the Medieval Fair, the Council adopted Resolution R-1819-110, which formally selected Reaves Park as the site for the Senior Center. Resolution R-1819-110 also re-programmed \$7,600,000 in funds from the Griffin Park Land Acquisition project to the Senior Citizens Center project.

In August 2021, Council approved a memorandum of understanding with the Norman Regional Health System to move the location of the Senior Center to Norman Regional's Porter Campus. The scope of the project was also expanded from a recreational center to a wellness center. The newly renamed "Senior Wellness Center" will be a part of Norman Regional's planned Porter Health Village.

The proposed 30,000 square foot center is set to include an indoor walking track and multiple fitness areas with locker rooms; multipurpose and art specific classrooms as well as lounge areas; a full kitchen for events and programming;

outdoor pickleball courts; and a lap pool. Non-profit third party operator Healthy Living & Fitness will operate the facility.


<i>Published Norman Forward Budget</i>	<i>\$0; Amended to \$7,600,000</i>
<i>CARES Act Funding</i>	<i>\$4,800,000</i>
<i>Norman Regional Land Swap Proceeds</i>	<i>\$426,000</i>
<i>Sale of 718 N Porter*</i>	<i>\$1,197,277</i>

**temporarily transferred from the General Fund due to the pending status of the sale of 718 N Porter.*

<i>Preliminary Estimated Budget</i>	
<i>Land Acquisition/Site Prep/Infrastructure</i>	<i>\$427,551</i>
<i>A&E / Design / Testing</i>	<i>\$832,000</i>
<i>Construction & FFE</i>	<i>\$12,283,002</i>
<i>Project Contingency</i>	<i>\$480,996</i>
<i>Total Project Budget</i>	<i>\$14,023,277</i>

Timing

The project officially broke ground in November 2021 and has an estimated completion date in Summer of 2023.

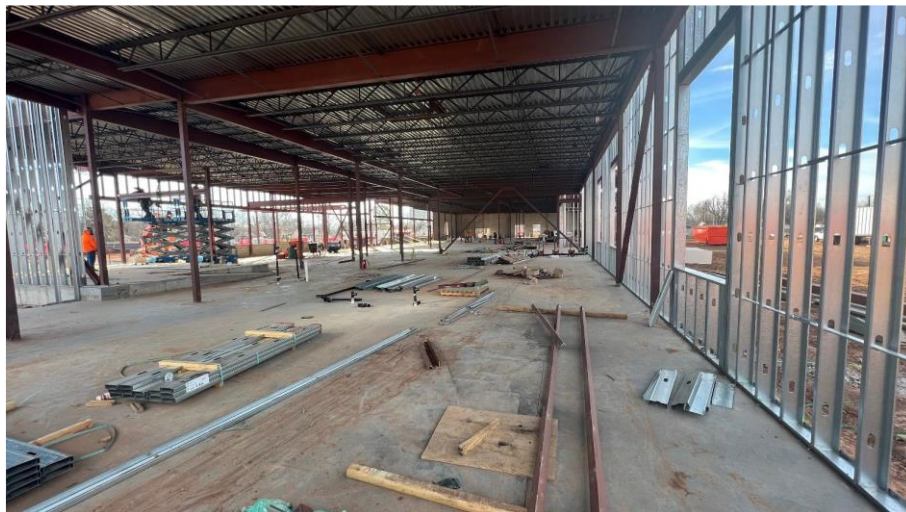

Sports Complex Projects

Description

Renovations and new construction are planned for sports complexes in multiple locations. These facilities will allow expanded space for youth soccer, youth and adult softball, adult flag football and youth football.

Scope

Due to financial reasons, the adult softball and youth football programs will no longer be a standalone complex. The expanded adult softball programs will be at Reaves Park and youth football will be at Ruby Grant Park. The identified sports complex projects are:

- Reaves Park: additional youth baseball/softball fields with lighting, restrooms, concessions, and additional parking (Budget: \$10,000,000; + \$1,250,000 for adult softball).
- Ruby Grant Park: multi-field football complex with lighting, restrooms, concessions, and parking (Budget \$1,250,000).
- Griffin Park: new outdoor soccer fields with lighting and parking. (\$11,000,000).

Published Budget \$23,500,000

Preliminary Estimated Budget

Land Acquisition / Site Prep / Infrastructure	\$1,800,000
A&E / Design / Testing	\$1,880,000
Construction & FFE	\$18,410,000
Project Contingency	\$1,410,000
Total Project Budget	\$23,500,000

Timing

Final master plans and engineering designs have been completed for the Reaves Park and Griffin Park Sports Complexes. Reconstruction of 11 of 22 soccer fields at the Griffin Park Soccer Complex has been completed, and more fields and facilities will be completed over the next few months with an estimated completion of Summer 2023. The new Parks Maintenance Facility has been completed and is relocated from Reaves Park to the City Maintenance Complex ("North Base"). Relocation of the Parks Maintenance Facility will make land available for the planned expansion of baseball and softball fields at Reaves Park which is currently scheduled to be 100% completed by Spring 2023. Relocated youth football (Ruby Grant) and adult softball (Reaves) facilities, originally planned at a new stand-alone site, are complete and nearly complete respectively.

Traffic Improvements

Description

NORMAN FORWARD includes infrastructure improvements for the city that will improve traffic flow and safety at various locations related to NORMAN FORWARD projects.

Scope

Planned projects include traffic analysis, street and storm water improvements, and traffic signals at various locations. Related NORMAN FORWARD projects are access to the Young Family Athletic Center (Trae Young Way), Griffin Park, and Reaves Park.

Published Budget \$2,700,000

Preliminary Estimated Budget

Land Acquisition / Site Prep / Infrastructure	\$270,000
A&E / Design / Testing	\$216,000
Construction & FFE	\$2,025,000
Project Contingency	\$189,000
Total Project Budget	\$2,700,000

Timing

Architecture, engineering, land acquisition, and site preparation are scheduled to begin throughout the program based on specified sites. This project is scheduled to be completed as needed for individual project sites during construction phases. Access improvements for the Griffin Soccer Complex on Robinson Street and 12th Avenue are underway. Access improvements to the YFAC, including construction of "Trae Young Drive" are also underway.

Westwood Family Aquatic Center

Description

The Westwood Family Aquatic Center project has constructed an updated, modern outdoor aquatic center. Features include a lazy river, slides, water sprays, a 50-meter lap pool, shaded shallow areas, a new bathhouse, concession areas, and additional parking. The new outdoor Aquatic Center opened in the summer of 2018 and has been enjoyed by thousands of visitors.

Scope

Based on the current budget, the pool will have approximately 18,000 square feet of water surface area and include a variety of features that have been determined through public input are also part of this project.

<i>Published Budget</i>	<i>\$12,000,000</i>
<i>Final Cost</i>	<i>\$11,755,659</i>



Other Projected Program Expenses

▪ Public Art	\$1,200,000
▪ Park Maintenance Staff	\$3,009,925
▪ Senior Center Staff	\$0
▪ Facility Maintenance Staff	\$1,562,753
▪ Capital Equipment	\$425,000
▪ Aquatic Center Operating Subsidy	\$0
▪ Project Oversight	\$3,312,000
▪ Westwood Pool/Tennis Replacement	\$455,000
▪ Facility Maintenance Contract	\$210,000
▪ Interest and Debt Service Cost	\$20,962,256
Total Other Program Expenses Budget	\$31,136,934

Projects identified for Public Art include:

- Central Branch Library
- East Branch Library
- Westwood Family Aquatic Center
- Indoor Multi-Sport Facility
- Indoor Aquatic Center
- Sports Complex Projects: Reaves Park, Griffin Park
- Park Projects: Westwood Tennis Center, Ruby Grant, Saxon & Andrews
- James Garner Avenue Extension
- Senior Wellness Center

IV. Project Timeline


As part of the Implementation Plan, steps were taken to determine the order in which the projects, or phases of projects, would take place in the program. To complete this task, the Program Manager attended Citizens Financial Oversight Board meetings, ad hoc advisory group meetings, and worked with City Staff. City Staff provided budget information critical to project sequencing. The goal is to create a logical project progress schedule within the constraints of the funding structure. Individual project's schedules are updated in their discussions above.

Potential impacts to the overall NORMAN FORWARD project timeline include, but are not limited to:

- Fluctuation in sales tax revenue
- Changes in project scopes of work
- Inflation or other increases in cost of project construction
- Other unforeseen circumstances

The chart below is updated to reflect changing time schedules for the various projects as the overall Norman Forward program moves forward.

Project Timeline

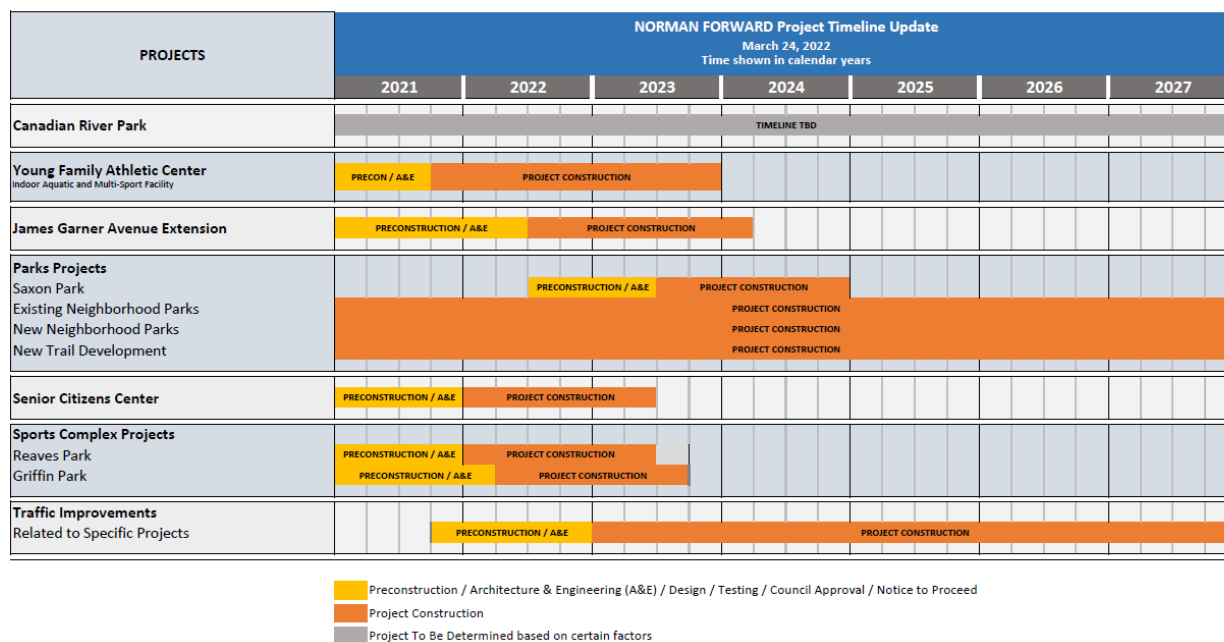

V. Conclusion

This Implementation Plan includes an introduction and history of the NORMAN FORWARD program, project descriptions, scopes of work, budgets, project phasing, and the Project Timeline. The original Implementation Plan was adopted by the City Council on June 28, 2016 (Resolution R-1516-130) and minor updates have been approved periodically by the Citizen's Financial Oversight Board (CFOB). At various points in time as significant projects are completed or changes are made, amended Implementation Plan documents will be re-submitted for Council consideration. On the recommendation of the CFOB, the Implementation Plan was formally amended on October 8, 2019 by Resolution R-1920-44 and again on April 12, 2022 by Resolution R-2122-110.

Upon the recommendation of the Citizens Financial Oversight Board and final approval by City Council, City Staff will implement and administer the 15-year plan. The Program Manager will assist City staff with programming, cost estimating, design review, and construction observation on projects outlined by their contract with the City.

This document is based on currently available information as well as certain assumptions made based on anticipated requirements. It may be further amended by City Council as new information arises or other changes occur over the 15-year life of the quality-of-life program.

Additional Information

NORMAN FORWARD, City of Norman

<https://www.normanok.gov/your-government/projects-initiatives/norman-forward>

“Norman Voters Approve Sales Tax Increase”

<http://journalrecord.com/2015/10/14/voters-approve-sales-tax-increase/>

2009 Parks and Recreation Master Plan, City of Norman

<https://www.normanok.gov/sites/default/files/documents/2020-05/ParksMasterPlan1.pdf>

Young Family Athletic Center

<https://www.normanok.gov/residents-visitors/parks-recreation/young-family-athletic-center>

Senior Wellness Center

<https://www.normanok.gov/residents-visitors/parks-recreation/senior-wellness-center>

Norman Forward CFOB Annual Report

For the period October 1, 2020 – December 31, 2021
