

1302 South J Street
Lake Worth, FL 33460



Ph: 561-689-0889
Fax: 561-689-2851

Change Order Request

Owner Co No. _____

Change Order No.: 24R1

Owner: City of Pahokee

Project: Barfield Highway

Owner Proj. No.: 2020-007

RSD Proj. No.: 01-20037

Date: 9/2/2022

Description: Cost to adjust two Fire Hydrants and associated valve stem and collar.

#	Description	Qty	Unit	Unit Price	Total Price
1.00	Fire hydrants Valve Stem and Collar adjustment	1	LS	\$ 10,188.29	\$ 10,188.29
					\$ -
					\$ -
					\$ -
					\$ -
					\$ -
					\$ -
					\$ -
					\$ -

Total: \$ 10,188.29

Original Contract Amt \$ -

Amount of this Change Order \$ 10,188.29

Amount of Previous Change Order (s) \$ -

New Total Contract Amount \$ **10,188.29**

Completion time extended 2 days

If yes, new completion date? _____

When executed by all parties, this document will become part of the above reference construction contract.

Michael Rezk

Client Signature

Michael Rezk 9/8/2022

Client Printed

Blair Simpson

Digitally signed by Blair Simpson
DN: cn=Blair Simpson, o=ROSSO
Site Development, ou,
email=bsimpson@rossositedevelop
ment.com, c=US
Date: 2022.09.22 14:29:00 -04'00'

Revisions

#	Date	By	Description
1	9/6/2022	JW	Adjusted Hrs per PBC request, also added RSD time for supervision
2	9/8/2022	JW	Adjusted Superintendent Rate

1302 South J Street
Lake Worth, FL 33460



Ph: 561-689-0889
Fax: 561-689-2851

CHANGE ORDER BREAKDOWN

Description of work: Cost to adjust two Fire Hydrants and associated valve stem and collar.

CO #: 24R1

EQUIPMENT					
#	Description	Qty	Unit	Unit Cost	Total Cost
1	Loader		HR	\$62.50	\$0.00
2	Tractor		HR	\$40.38	\$0.00
3	Roller		HR	\$56.12	\$0.00
4	Mixer		HR	\$202.61	\$0.00
5	Grader		HR	\$79.95	\$0.00
6	Backhoe		HR	\$93.41	\$0.00
7	Water Truck		HR	\$37.98	\$0.00
8	Dozer		HR	\$73.93	\$0.00
9	Paver		HR	\$61.50	\$0.00
10	Paving Roller		HR	\$40.38	\$0.00
11	Broom		HR	\$49.97	\$0.00
12	Excavator (30,000 lb)		HR	\$109.04	\$0.00
13	Excavator (70,000 lb)		HR	\$169.32	\$0.00
14	Tamp		HR	\$19.50	\$0.00
15	Saw		HR	\$19.50	\$0.00
16	Pick-Up Truck	16	HR	\$32.46	\$519.36
17	Dump Truck		HR	\$65.00	\$0.00
18	Curb Machine		HR	\$58.75	\$0.00

Equipment Subtotal \$519.36
Markup 0.150 \$77.90
EQUIPMENT TOTAL: \$597.26

LABOR					
#	Description	Qty	Unit	Unit Cost	Total Cost
1	Superintendent	16	HR	\$64.29	\$1,028.64
2	Foreman		HR	\$84.20	\$0.00
3	Operator-Road Crew		HR	\$38.06	\$0.00
4	Laborer-Road Crew		HR	\$20.79	\$0.00
5	Operator-Underground Crew		HR	\$36.24	\$0.00
6	Pipe Layer, Tailman, Laborer-Underground Crew		HR	\$26.32	\$0.00
7	Curb Machine Operator-Concrete Crew		HR	\$43.50	\$0.00
8	Finisher-Concrete Crew		HR	\$32.61	\$0.00
9	Former/Laborer-Concrete Crew		HR	\$23.65	\$0.00
10			HR		\$0.00
11			HR		\$0.00

Labor Subtotal **\$1,028.64**
Burden 0.5146 \$529.34
Markup 0.150 \$154.30
LABOR TOTAL: \$1,712.27

MATERIAL					
#	Description	Qty	Unit	Unit Cost	Total Cost
1	JD Price to Adjust (2)Fire hydrants Valve Stem and Collar	1	LS	\$6,670.24	\$6,670.24
2			LS		\$0.00
3					\$0.00
4					\$0.00
5					\$0.00
6					\$0.00
7					\$0.00

Material Subtotal \$6,670.24

Markup 0.150 \$1,000.54

MATERIAL TOTAL: \$7,670.78

SUBCONTRACTORS					
#	Description	Qty	Unit	Unit Cost	Total Cost
1		1	LS		\$0.00
2		1	LS		\$0.00
3		1	LS		\$0.00
4		1	LS		\$0.00
5		1	LS		\$0.00
6		1	LS		\$0.00
7		1	LS		\$0.00

Subcontractor Subtotal \$0.00

Markup 0.10 \$0.00

SUBCONTRACTOR TOTAL: \$0.00

Equipment Total: \$597.26

Labor Total: \$1,712.27

Material Total: \$7,670.78

Subcontractors Total: \$0.00

Bond & General Liability Insurance: \$207.98

MOT: \$0.00


Total: \$10,188.29



LABOR BURDEN

FICA	FUTA	SUTA	WC	RETIREMEN T BENEFITS	MEDICAL	HOLIDAY / VACATION / SICK	Total
7.65%	0.60%	1.08%	13.39%	4.00%	17.44%	7.30%	51.46%

In agreement with FDOT Specification section 4-3.2.1. As an officer or director of Rosso Site Development, Inc. I certify the above rates to be true and accurate.


Blair Simpson-VP

5-19-22
Date



Johnson Davis
Subcontractor Quote

Appendix 'A'



CHANGE ORDER REQUEST

Date: August 29, 2022
Customer/Owner: Rosso Site Development
Address: 1302 South J Street
City, State Zip: Lake Worth, FL 33460

Attn: Blair Simpson

Project: Barfield Hwy
Project #: 41792
Re:

J-D COR #: 27

James,

Additional Work Associated with removing and disposing of existing bollards, Raising two existing fire hydrants to a Finish Grade Elevation provided by Rosso. No bollards are figured to re-install.

DATE: TBD
TASK: (2) Existing Fire Hydrant Adjustments and Bollard Removal

1	Labor	1	LS	\$2,303.60	\$2,303.60
2	Equipment	1	LS	\$2,038.54	\$2,038.54
3	Material	1	LS	\$2,328.11	\$2,328.11
4	Subcontractors	1	LS	\$0.00	\$0.00

Total Amount of Change Order: \$6,670.24

Total Amount of Days Added to The Contract: 2

Please review and forward to the responsible parties for authorization. As always, should there be any questions or if you require any additional information please do not hesitate to contact our office.

Sincerely,

Chad Rawlinson

Chad Rawlinson
Project Manager



Johnson-Davis Inc.

Job Name: Barfield Hwy

Date: 8/29/2022

JD Job #: 41792

Description of Work: (2) Existing Fire Hydrant Adjustments and Bollard Removal

Labor

Name	Position	Standard Hours	Overtime Hours	Standard Rate	Overtime Rate	Total
Support Crew Leader		16		\$ 25.23	\$ 37.84	\$ 403.66
Support Crew Skilled Labor	SL	16		\$ 17.86	\$ 26.79	\$ 285.80
Superintendent		4		\$ 69.26	\$ 103.89	\$ 277.04
Operator - Excavator	Oper-Exc	16		\$ 26.41	\$ 39.62	\$ 422.64
0	0			\$ -	\$ -	\$ -
				\$ -	\$ -	\$ -
				\$ -	\$ -	\$ -
				\$ -	\$ -	\$ -
				\$ -	\$ -	\$ -
				\$ -	\$ -	\$ -

Labor Subtotal \$ 1,389.13

Burden 0.442 \$ 614.00

Markup on Labor 15.0% \$ 300.47

Labor Total \$ 2,303.60

Equipment

Description	Qty	Hours	Rate	Total
Superintendent Vehicle	1	4	\$ 45.86	\$ 183.44
Support Crew Truck with Hand Tools	1	16	\$ 34.00	\$ 544.00
40-46 Dump Trailer	1	16	\$ 9.74	\$ 155.84
Tamper	1	16	\$ 6.37	\$ 101.92
20-88 Takeuchi TB260	1	16	\$ 47.34	\$ 757.44
Cut off Saw 14"	1	4	\$ 7.50	\$ 30.00
			\$ -	\$ -
			\$ -	\$ -
			\$ -	\$ -
			\$ -	\$ -

Equipment Subtotal: \$ 1,772.64

Markup on Equipment 15.0% \$ 265.90

Equipment Total \$ 2,038.54

Material

Description	Qty	Unit	Rate	Total
Fire Hydrant Extensions 24"	2	EA	\$ 562.00	\$ 1,124.00
Misc Bolts and Nuts	2	EA	\$ 50.00	\$ 100.00
2' Valve Stem Extensions	2	EA	\$ 192.00	\$ 384.00
Valve Box & Lid	2	EA	\$ 185.00	\$ 370.00
0		0	\$ -	\$ -
0		0	\$ -	\$ -
0		0	\$ -	\$ -
			\$ -	\$ -
			\$ -	\$ -
			\$ -	\$ -
			\$ -	\$ -

Material Subtotal: \$ 1,978.00

Tax 7% \$ 138.46

Markup on Material 10.0% \$ 211.65

Material Total \$ 2,328.11

Subcontractor

Description	Qty	Unit	Rate	Total
				\$ -
				\$ -

Subcontractor Subtotal: \$ -

Markup on Subcontractors (up to \$50,000.00) 10.0% \$ -

Markup on Subcontractors (after \$50,000.00) 5.0%

Subcontractor Total \$ -

Total: \$ 6,670.24

Comments:

This proposal does not include any installation of bollards. It is assumed that the average height that the hydrants need to be raise are 24". No additional money is included for any additional restraints that need to be installed. T.B.D. May be additional costs. Layout and confirmation of F.G. by Rosso.



JOHNSON-DAVIS INC.

Contractors

604 HILLBRATH DRIVE

LANTANA, FL 33462-1694

PHONE: 561-588-1170 FAX: 561-585-5252

CU-C043087

Subject: Labor Burden Certification

I, John P. Stanley, the Chief Financial Officer of Johnson-Davis, Inc., certify that the following statements are true and correct. The following information is submitted pursuant to Specification 4-3.2.1:

Burden Rate Breakdown									
Workers Compensation	State Unemployment & Federal	FICA	Vacation , Holiday, Personal Time, Bereavement Pay	Health / Dental Insurance	Life Insurance	401(K)	G/L Ins.	Disability Insurance	DFWP
0.065	0.062	0.0765	0.07	0.095	.0017	0.04	0.022	0	0.01

TOTAL BURDEN RATE = 44.2%

If you have any questions or require any additional information, feel free to contact me.

Thank you,

John Stanley
Chief Financial Officer



LARISA DITU PELKEY
Commission # HH 178111
Expires January 22, 2026
Bonded Thru Budget Notary Services

State of Florida, County of Palm Beach

Sworn and subscribed before me this 09 day of March, 2019

Notary Public

Personally known to me

My Commission Expires:

01.22.24



Heavy Construction

Underground Utilities

Main office: 604 Hillbrath Drive- Lantana, FL 33462 • Phone: 561-588-1170 • Fax: 561-585-5252
Ft. Pierce Office: 863 S. Kings Hwy- Ft. Pierce, FL 34945 • Phone: 772-468-9200 • Fax: 772-468-9202



2022 Equipment Rates for FDOT Jobs	
Description	Hourly Rate
Trucks	
Superintendent Vehicle	\$45.86
Foreman Truck with Hand Tools	\$46.09
Support Crew Truck with Hand Tools	\$34.00
Field Mechanic Service Truck	\$42.86
45-104 Tandem Truck Tractor	\$67.94
45-115 Single Axle Truck Tractor	\$68.41
45-117 Tri-Axle Truck Tractor	\$69.20
45-128 Tandem Flat Bed (24") Truck	\$39.20
45-164 Tri-Axle Dump Truck - Steel Body	\$71.29
45-249 Tri-Axle Truck Tractor	\$70.09
45-279 Tandem Tractor	\$70.81
45-280 Single Axle Tractor	\$70.91
45-331 Tri-Axle Dump Truck	\$73.40
40-27 Loadboy Trailer	\$38.50
40-32 Loadboy Trailer	\$38.66
40-28, Jeep for Loadboy Trailer	\$9.80
40-34/39 Flatbed Trailer	\$8.22
40-12 Drop Deck Trailer	\$17.28
40-44 Aluminum Dump Trailer	\$9.23
40-24 Steel Dump Trailer	\$9.30
40-46 Dump Trailer	\$9.74
40-42 Small Equipment Trailer -16,000 LBS	\$2.57
Rubber Tire Excavators	
25-61 CAT 420D IT (Combination Backhoe)	\$46.77
25-52 CAT 430D IT (Combination Backhoe)	\$62.86
25-57 CAT 420F IT (Combination Backhoe)	\$55.81
20-57 Liebherr R912 Excavator (Rubber Tire)	\$104.93
20-63 John Deere 220D Excavator (Rubber Tire)	\$167.49
20-75 Liebherr A950C	\$104.93
Track Excavators	
20-37 Liebherr R934 HD SL Excavator	\$148.34
20-39 Inert-Drain 6050HT (Sock Machine)	\$94.02
20-40 Liebherr R912 HD SL Excavator	\$133.98
20-44 Liebherr R944 HD SL Excavator	\$152.71
20-48 Liebherr R944 HD SL Excavator	\$147.05
20-50 Liebherr R934 B HD SL Excavator	\$150.33
20-53 Liebherr R944 B HD SL Excavator	\$147.36
20-54 Liebherr R934 B HD SL Excavator	\$150.33
20-55 Liebherr R954 C HD Excavator	\$207.14
20-68 Komatsu PC360-6 LC-10 Excavator	\$133.70
20-59 Caterpillar 328D Excavator	\$156.16
20-60 Caterpillar 336DL Excavator	\$158.23
20-65 Komatsu PC360-6 LC-10 Excavator	\$152.89
20-68 Komatsu PC390-6 LC-10 Excavator	\$160.87
20-69 Komatsu PC240-6 LC-11 Excavator	\$145.09
20-70 Komatsu PC390-6 LC-11 Excavator	\$170.40
20-71 Komatsu PC390-6 LC-11 Excavator	\$170.97
20-72 Komatsu PC138-6 LC-12 Excavator	\$113.53
20-73 Komatsu PC290-6 LC-11 Excavator	\$160.53
20-74 Komatsu PC138-6 LC-11 Excavator	\$105.22
20-77 Caterpillar 320DL Excavator	\$138.85
20-78 Caterpillar 325 Excavator	\$136.47
20-79 Komatsu PC238-6 LC-11 Excavator	\$124.04
20-80 Komatsu PC138-6 LC-11 Excavator	\$105.22
20-81 Caterpillar 307E2 Excavator	\$67.72
20-82 John Deere 350G LC	\$161.67
20-84 John Deere 50G	\$41.18
20-86 John Deere 345G	\$161.67
20-87 John Deere 380G	\$221.99
Wheel Loaders	
30-30 John Deere 644H Loader	\$66.30
30-32 Liebherr L544 Loader	\$56.13
30-32 Volvo L70 Loader	\$49.20
30-34 Liebherr L538 Loader	\$55.12
30-36 Volvo L90E Loader	\$56.04
30-37 Volvo L110E Loader	\$71.11
30-38 Komatsu WA380-6 Loader	\$64.08
30-39 Komatsu WA380-6 Loader	\$64.71
30-40 Caterpillar 950H Loader	\$70.41
30-42 Komatsu WA320-6 Loader	\$55.12
30-43 Komatsu WA380-7 Loader	\$74.10
30-44 Komatsu WA200-7 Loader	\$58.47
30-45 Komatsu WA320-7 Loader	\$59.86
30-46 Caterpillar 938K Loader	\$87.44
30-47 Komatsu WA200-7 Loader	\$59.63
30-48 Komatsu WA380-7 Loader	\$80.62
30-50 Komatsu WA380-8 Loader	\$99.30
30-50 Caterpillar CAT 926M Loader	\$42.64
30-51 Komatsu WA-320-8 Loader	\$71.42
30-52 Komatsu WA-270-8 Loader	\$75.49
30-53 Caterpillar 930M Loader	\$72.61
30-54 Caterpillar 930M Loader	\$72.61
30-55 John Deere 524L	\$68.20
30-56 John Deere 544L	\$69.06
30-57 John Deere 524L	\$68.20
30-58 John Deere 544L	\$69.06
30-59 John Deere 644L	\$91.09
30-60 John Deere 644L	\$91.09
Mini Excavators / Bobcats / Dozer	
35-01 John Deere 650 H-LGP Dozer	\$63.39
35-01 Bobcat 913G	\$32.37
35-01 Bobcat T300	\$39.83
35-61 Mini-Hoe Kubota KX913R1S (30 HP Kubota)	\$19.30
35-62 Mini-Hoe Kubota KX080-3 (70 HP Kubota)	\$76.53
35-64 Mini-Hoe Kubota KX913R2 (30 HP Kubota)	\$19.03
35-66 Mini-Hoe Kubota KX121-3ST (30 HP Kubota)	\$24.06
20-67 Caterpillar 305E2 (11k LBS Mini)	\$47.38
20-89 Takeuchi TB260	\$47.34
Specialty Equipment	
75-20 Ford Box Blade Tractor 3910	\$33.38
82-145 Water Truck (2000 gal)	\$63.01
82-157 Water Truck (2000 gal)	\$63.01
85-177 APE Power Unit 260	\$15.57
85-229 Hydraulic Hammer ICE BE	\$93.72
85-230 Rotary Heat Auger ICE EX26	\$263.40
Water Trailer (1000 gal)	\$15.55
Vibratory Rollers	
75-30 Ingersoll Rand SD40 Vibratory Roller	\$42.07
75-31 Dynapac CA121D Vibratory Roller	\$37.07
75-32 Dynapac CA121D Vibratory Roller	\$37.43
75-34 Dynapac CA121D Vibratory Roller	\$37.26
75-34 Dynapac C200D, double drum	\$15.34
75-35 Volvo SD45D Vibratory Roller single drum	\$35.68
75-36 Volvo SD45D Vibratory Roller single drum	\$35.70
Pumps	
Well Point Header and Points (No Pump)	\$12.00
10" Well Point Pump & Disch Hose - (24 Hrs/day)	\$36.71
8" Well Point Pump & Disch Hose - (24 Hrs/day)	\$40.59
8" Quiet Pack Well Point Pump & Disch Hose - (24 Hrs/day)	\$36.29
6" Well Point Pump & Disch Hose - (24 Hrs/day)	\$35.56
12" Hydraulic Pump & Hoses (8hr/day minimum)	\$55.29
8" Hydraulic Pump & Hoses (8hr/day minimum)	\$45.59
6" Hydraulic Pump & Hoses (8hr/day minimum)	\$36.74
4" Hydraulic Pump & Hoses (8hr/day minimum)	\$38.00
4" Jet Pump & Hoses	\$20.82
4" Double Diaphragm & Hoses	\$13.52
3" Trash Pump & Hoses	\$6.58
Vibratory Hammer	\$93.72
Rental Equipment	
Shoring Plate 1"x6"x20"	\$23.00
Shoring Plate 1"x6"x16"	\$20.00
Shoring Plate 1"x6"x12"	\$19.00
Shoring Plate 1"x6"x10"	\$18.00
Stone Boat 1/2 CYL	\$85.00
Manhole Box 6"x10"x4"	\$80.00
Trench Shield Box 24"x6"x6"	\$120.00
Trench Shield Box 24"x6"x4"	\$185.00
Trench Shield Box 20"x6"x4"	\$115.00
Trench Shield Box 10"x6"x4"	\$110.00
Trench Shield Box 10"x28"x6"	\$250.00
Trench Shield Box 10"x24"x6"	\$140.00
Trench Shield Box 8"x24"x6"	\$100.00
Trench Shield Box 8"x16"x4"	\$110.00
Pipe Piles - Airbag for drainage 12"-18"	\$65.00
Pipe Piles - Airbag for drainage 18"-24"	\$95.00
Pipe Piles - Airbag for drainage 15'-30'	\$130.00
Pipe Piles - Airbag for drainage 24"-48"	\$190.00
Pipe Piles - Airbag for drainage 48"-72" (w/ lift line)	\$593.00
Pipe Piles - Airbag for sewer pipe (pass through)	\$750.00
Pipe Piles - Airbag for sewer pipe (solid chub)	\$255.00
Small Equipment	
Air Compressor	\$19.21
Tamper	\$6.37
Light Plant (8hr/day minimum)	\$10.16
Walking Saw	\$9.53
Cut off Saw 14"	\$7.50
Generator	\$4.85

2022 Labor Rates for FDOT Jobs

Labor		Standard	Overtime
Superintendent		\$69.26	\$103.89
Foreman	Foreman	\$43.15	\$64.72
Arnold, Roger	Foreman	\$45.00	\$67.50
Brady, Jeff	Foreman	\$44.55	\$66.83
Ceance, Chescal	Foreman	\$50.60	\$75.90
Dort,Wisler	Foreman	\$44.16	\$66.24
Fernandez, Pablo	Foreman	\$50.00	\$75.00
Henrisme,Jacky	Foreman	\$44.16	\$66.24
Hernandez, Jose R	Foreman	\$50.00	\$75.00
Hernandez, Odilon	Foreman	\$50.60	\$75.90
Lashley, Stern	Foreman	\$44.00	\$66.00
Molina, Moises	Foreman	\$27.50	\$41.25
Tharpe, Richard	Foreman	\$27.50	\$41.25
Thelisonrt,Ariesthene	Foreman	\$41.00	\$61.50
Pierson,Rickey	Foreman	\$41.00	\$61.50
Rothermel, David	Foreman	\$44.00	\$66.00
Operator - Excavator	Oper-Exc	\$26.41	\$39.62
Arce, Alfonso	Oper-Exc	\$28.00	\$42.00
Brasfield, Alexander	Oper-Exc	\$24.20	\$36.30
Cuadrado del Valle, Juan	Oper-Exc	\$26.10	\$39.15
Gerken, David	Oper-Exc	\$26.10	\$39.15
Guerrero, Lorenzo	Oper-Exc	\$28.00	\$42.00
Guerrero Oseguera, Agustin	Oper-Exc	\$23.50	\$35.25
Hester, Anthony	Oper-Exc	\$26.10	\$39.15
Kobbe, Nickolas	Oper-Exc	\$26.10	\$39.15
Lewis, Delroy	Oper-Exc	\$26.10	\$39.15
MCDonald, Phil	Oper-Exc	\$28.16	\$42.24
Mullan, Christopher	Oper-Exc	\$28.00	\$42.00
Nava Rivera,Alejandro	Oper-Exc	\$28.00	\$42.00
Parkinson, Siegfried (Pete)	Oper-Exc	\$28.19	\$42.29
Stephens, Napoleon	Oper-Exc	\$24.20	\$36.30
Thomas, Alva	Oper-Exc	\$26.10	\$39.15
Walker, Jeffrey	Oper-Exc	\$26.10	\$39.15
Villodo, Eduardo	Oper-Exc	\$26.10	\$39.15
Operator - Loader	Oper-Ldr	\$22.63	\$33.94
Briggs, Dustin	Oper-Ldr	\$22.60	\$33.90
Davio, Gordon	Oper-Ldr	\$25.32	\$37.98
Edmond, Eugene	Oper-Ldr	\$21.00	\$31.50
Franco, Jose	Oper-Ldr	\$21.00	\$31.50
Jean, Jeannot	Oper-Ldr	\$22.60	\$33.90
Martinez, Jorge	Oper-Ldr	\$22.60	\$33.90
Montes, Carlos	Oper-Ldr	\$22.60	\$33.90
Morales, Eloy	Oper-Ldr	\$22.60	\$33.90
Pinder, Gregory	Oper-Ldr	\$25.00	\$37.50
Santiago, Jessie	Oper-Ldr	\$22.60	\$33.90
Wells, Nathaniel	Oper-Ldr	\$21.00	\$31.50
Pipe Layer	PL	\$24.85	\$37.27
Arana Pineda,Jesus	PL	\$22.60	\$33.90
Arce, Santos	PL	\$28.00	\$42.00
Atha, Zachary	PL	\$22.60	\$33.90
Carr, Vincent	PL	\$24.82	\$37.23
Castanon, Walter	PL	\$22.60	\$33.90
Castro Flores, Ramon	PL	\$22.60	\$33.90
Ceance, Chedo	PL	\$25.00	\$37.50
Colville, Christopher	PL	\$25.00	\$37.50
Dieujeste,Willy	PL	\$22.00	\$33.00
MacRoy Jr., Elijah	PL	\$25.00	\$37.50
Morales Hernandez,Pedro	PL	\$25.00	\$37.50
Pascual, Andres	PL	\$28.31	\$42.47
Raphael, Mainiau	PL	\$25.00	\$37.50
Ruiz, Luis	PL	\$25.00	\$37.50
Samuel, Antonio	PL	\$28.57	\$42.86
Steen, Ronald	PL	\$25.00	\$37.50
Theophilus,Assmic	PL	\$25.00	\$37.50
Velasquez, Tranquilino	PL	\$25.16	\$37.74
Skilled Laborer	SL	\$19.78	\$29.67
Barragan Ocegüera,Juan	SL	\$21.20	\$31.80
Bucio, Fernando	SL	\$20.00	\$30.00
Calcerrada Diaz, Yurisander	SL	\$20.00	\$30.00
Carmey, Mau/Juan	SL	\$20.00	\$30.00
Castanon, Walter	SL	\$21.20	\$31.80
Dumarsais, Oslin	SL	\$16.00	\$24.00
Garcia, Genaro	SL	\$21.20	\$31.80
Gonzalez Dominguez, Rafael	SL	\$21.20	\$31.80
Henrisme, Jackens	SL	\$17.50	\$26.25
Hernandez Villanueva,Luis	SL	\$21.20	\$31.80
Jean, Jean Robert	SL	\$17.50	\$26.25
Julceus, Jerome	SL	\$17.50	\$26.25
Lewis Jr, Delroy	SL	\$16.00	\$24.00
Lormeus, Jacquecy	SL	\$21.20	\$31.80
Louisca, Renel	SL	\$20.00	\$30.00
McClanahan, Trevor	SL	\$21.20	\$31.80
Molina Rios,Jesus	SL	\$21.20	\$31.80
Nozistene, Frederic	SL	\$20.00	\$30.00
Ocegüera, Juan Barragan	SL	\$21.20	\$31.80
Osuna, Gustavo	SL	\$22.00	\$33.00
Palma Bustillo,Miguel	SL	\$20.00	\$30.00
Philemons, Kechener	SL	\$20.00	\$30.00
Pierre Louis, Fadoul	SL	\$17.50	\$26.25
Pierre Louis, Famuel	SL	\$21.20	\$31.80
Piersaint,Yvon	SL	\$17.50	\$26.25
Robinson, Corey	SL	\$16.00	\$24.00
Roundtree, Jarrod	SL	\$21.20	\$31.80
Ruiz Fonseca,Angel	SL	\$20.00	\$30.00
Saint Pierre, Kenol	SL	\$21.20	\$31.80
Saint Pierre, Obens	SL	\$17.50	\$26.25
Servilus,Desir	SL	\$21.20	\$31.80
Simmons, Anthony	SL	\$20.00	\$30.00
Thomas, Alva	SL	\$20.00	\$30.00
Torres Garcia, Jorge	SL	\$21.20	\$31.80
Toyo, Jean	SL	\$20.00	\$30.00
Turenne, Ernst	SL	\$20.00	\$30.00
Yanez, Adriel	SL	\$20.00	\$30.00
Support Crew Leader	CL	\$25.23	\$37.84
Arce, Magdalena	CL	\$27.00	\$40.50
Davis, Jerry	CL	\$25.80	\$38.70
Gil Vazquez,Humberto/ Carp	CL	\$25.30	\$37.95
Harp, Kenneth	CL	\$25.30	\$37.95
Lester, John	CL	\$22.60	\$33.90
Molina, Moises	CL	\$25.30	\$37.95
Pierre, Robens	CL	\$25.30	\$37.95
Support Crew Skilled Labor	SL	\$17.86	\$26.79
Henrisme, Jackens	SL	\$17.50	\$26.25
Michel, Thomas	SL	\$16.00	\$24.00
Phanor, Aniel	SL	\$20.00	\$30.00
Philius, Grady	SL	\$17.50	\$26.25
Philemons, Kechener	SL	\$16.40	\$24.60
Regisme, Duquene	SL	\$20.00	\$30.00
Rodriguez, Araceli	SL	\$18.00	\$27.00
Thomas, Gregory	SL	\$17.50	\$26.25
Truck Driver	D	\$22.65	\$33.97
Clemmons Sr., Derrick	D	\$20.40	\$30.60
Feliciano, Eddie	D	\$21.82	\$32.73
Miller, Howard	D	\$25.57	\$38.36
Tracy, Steven	D	\$22.80	\$34.20



RFI 31 Response

Appendix 'B'



CONSTRUCTION REQUEST FOR INFORMATION

RFI #: 31	CONTRACTOR COMPANY: Rosso Site Development	RFI REQUESTER: James Washington	RFI DATE: 08/02/22
PROJECT NAME: Barfield Hwy	OWNER: City of Pahokee	PROJ #: City: 2020-07 RSD: 01-20037	

REQUESTED INFORMATION/CLARIFICATION:

The existing Fire Hydrant Flange shown in the attached is 1ft below sidewalk grade and 2ft away and the bollards will conflict with the installation of the proposed sidewalk. RSD would like to know if the EOR would like to raise/relocate the Fire Hydrant and remove the (2) two Bollards that are in conflict with the proposed sidewalk? The blue shaded area is current route of sidewalk.
Please advise RSD on how to proceed.

RESPONSE:


See Email thread for response from PBC.

Robert Audette, PE


See follow up email 8/15 below on additional FH to be adjusted.

Robert

Fire Hydrant Elevation & Bollard Conflict

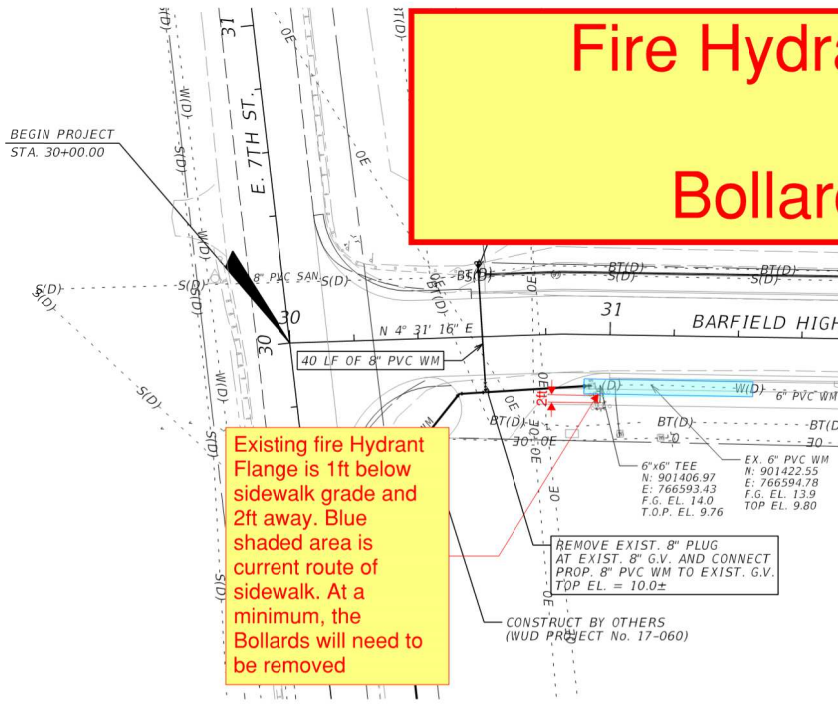

Existing fire Hydrant Flange is 1ft below sidewalk grade and 2ft away. Blue shaded area is current route of sidewalk. At a minimum, the Bollards will need to be removed

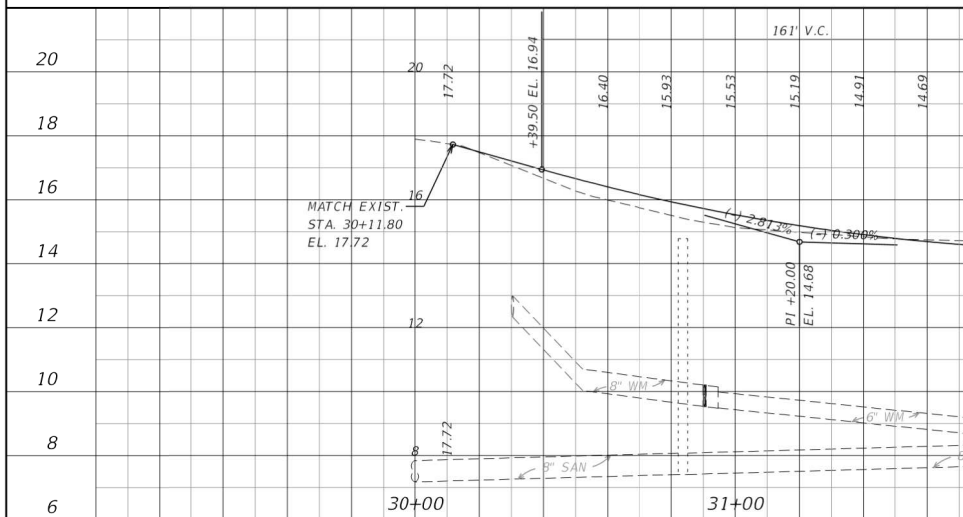

REVISIONS		RODERICK MYRICK, P.E.	
DATE	DESCRIPTION	DATE	DESCRIPTION

AE ENGINEERING, INC.
219 N. NEWMAN STREET, 4TH FL.
JACKSONVILLE, FL 32202
CERTIFICATE OF AUTHORIZATION



Robert Audette

Subject: FW: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

Thanks,

Robert
Cell: (786) 397-3521

From: Michael N. Rezk <MRezk@pbcwater.com>
Sent: Monday, August 15, 2022 9:40 AM
To: Robert Audette <raudette@momentumcei.com>
Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>; Chuck Gant <cgant@pbcwater.com>; Charlie Tran <ctran@aeengineeringinc.com>; Jackie Michels <JMichels@pbcwater.com>
Subject: RE: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

Robert,

Please see the email below from Chuck for FH at sta 35+40. Please have the contractor provide a cost estimate for both FH needed work.

Regards,

Michael Rezk

From: Chuck Gant <cgant@pbcwater.com>
Sent: Thursday, August 11, 2022 10:51 AM
To: Robert Audette <raudette@momentumcei.com>; Charlie Tran <ctran@aeengineeringinc.com>; Michael N. Rezk <MRezk@pbcwater.com>
Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>
Subject: RE: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

Fire hydrant at sta 35+40. Remove all bollards, raise hydrant & valve box.

chuck

From: Robert Audette <raudette@momentumcei.com>
Sent: Tuesday, August 2, 2022 12:20 PM
To: Charlie Tran <ctran@aeengineeringinc.com>; Michael N. Rezk <MRezk@pbcwater.com>
Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Chuck Gant <cgant@pbcwater.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>
Subject: FW: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

***** Note: This email was sent from a source external to Palm Beach County. Links or attachments should not be accessed unless expected from a trusted source. *****

Michael, Charlie,

Please see attached RFI. Let me know if flange height adjustment is needed and if 4 or 2 bollards need to be removed. This may be a Chuck call. He can also verify the FH at 35+40 Rt to see if the slope is ok as constructed around the FH.

Thanks,

Robert
Cell: (786) 397-3521

From: Julie Eimers <jeimers@rossositedevelopment.com>

Sent: Tuesday, August 2, 2022 11:51 AM

To: Robert Audette <raudette@momentumcei.com>; Charlie Tran <ctran@aeengineeringinc.com>

Cc: James Washington <JWashington@rossositedevelopment.com>; Jim Lewis <james.lewis@dot.state.fl.us>; Rod Myrick <rod@aeengineeringinc.com>

Subject: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01)

Please find attached RFI #31 for the Barfield Hwy project. Direction is needed for existing hydrant height and bollards that are in conflict with the sidewalk.

Thank you,

Julie Eimers
Project Manager



1302 South J Street
Lake Worth, FL 33460
P (561) 689-0889
F (561) 689-2851

Under Florida law, e-mail addresses are public records. If you do not want your e-mail address released in response to a public records request, do not send electronic mail to this entity. Instead, contact this office by phone or in writing.

Robert Audette

From: Robert Audette
Sent: Tuesday, August 9, 2022 10:49 AM
To: James Washington; Julie Eimers
Cc: Jongelene Adams; Mohammad Farhadtooski; Jim Lewis; Michael N. Rezk
Subject: FW: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753
Attachments: 5093_C010-C014.pdf; 20037-31 RFI_Existing Fire Hydrant Bollards Response.pdf
Follow Up Flag: Follow up
Flag Status: Flagged

Julie, James,

Response to your RFI is found below.

Let me know if you are willing to do the FH + Bollard removal and valve adjustments by using the Manhole Adjust pay item 425-5-1 for simplicity. If not, please provide your cost estimate for review by PBC. FH and valves will need to comply to county standards found in the plan.

Thanks,

Robert
Cell: (786) 397-3521

From: Michael N. Rezk <MRezk@pbcwater.com>
Sent: Tuesday, August 9, 2022 9:28 AM
To: Robert Audette <raudette@momentumcei.com>
Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>; Charlie Tran <ctran@aeengineeringinc.com>; Chuck Gant <cgant@pbcwater.com>; Jackie Michels <JMichels@pbcwater.com>
Subject: RE: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

Robert,

We haven't verified yet the FH at sta 35+40 but for FH at sta 31-/+ please do the following:

- The FH will need to be raised.
- Bollards to be removed.
- See attached record drawings, the existing valve boxes to be adjusted.

We will let you know what work needs to be done for FH at sta 35+50 then please have the contractor submit a cost estimate for the CO prior to the work in case we don't have bid items for that type of work.

Regards,

Michael Rezk

From: Chuck Gant <cgant@pbcwater.com>

Sent: Tuesday, August 9, 2022 7:08 AM

To: Robert Audette <raudette@momentumcei.com>; Charlie Tran <ctran@aeengineeringinc.com>; Michael N. Rezk <MRezk@pbcwater.com>

Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>

Subject: RE: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

Robert,

Don't forget to raise the valve boxes in this area also.

Chuck

From: Robert Audette <raudette@momentumcei.com>

Sent: Monday, August 8, 2022 2:41 PM

To: Charlie Tran <ctran@aeengineeringinc.com>; Michael N. Rezk <MRezk@pbcwater.com>

Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Chuck Gant <cgant@pbcwater.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>

Subject: RE: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

***** Note: This email was sent from a source external to Palm Beach County. Links or attachments should not be accessed unless expected from a trusted source. *****

Hello Michael,

I spoke with Chuck and he said to remove all 4 bollards and to adjust the FH height. Please confirm on behalf of the County for the RFI response. He'll check the other FH later this week.

Thanks,

Robert

Cell: (786) 397-3521

From: Robert Audette

Sent: Tuesday, August 2, 2022 12:20 PM

To: Charlie Tran <ctran@aeengineeringinc.com>; Michael N. Rezk <mrezk@pbcwater.com>

Cc: Myrick, Rod (AE) <rod@aeengineeringinc.com>; Jongelene Adams <jadams@cityofpahokee.com>; Chuck Gant <cgant@pbcwater.com>; Mohammad Farhadtooski <mfarhadtooski@momentumcei.com>

Subject: FW: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01), G-1753

Michael, Charlie,

Please see attached RFI. Let me know if flange height adjustment is needed and if 4 or 2 bollards need to be removed. This may be a Chuck call. He can also verify the FH at 35+40 Rt to see if the slope is ok as constructed around the FH.

Thanks,

Robert

Cell: (786) 397-3521

From: Julie Eimers <jeimers@rossositedevelopment.com>

Sent: Tuesday, August 2, 2022 11:51 AM

To: Robert Audette <raudette@momentumcei.com>; Charlie Tran <ctran@aeengineeringinc.com>

Cc: James Washington <JWashington@rossositedevelopment.com>; Jim Lewis <james.lewis@dot.state.fl.us>; Rod Myrick <rod@aeengineeringinc.com>

Subject: Barfield Hwy - RFI #31 Existing Hydrant Bollard Conflict (FM#442030-1-54-01)

Please find attached RFI #31 for the Barfield Hwy project. Direction is needed for existing hydrant height and bollards that are in conflict with the sidewalk.

Thank you,

Julie Eimers

Project Manager



1302 South J Street
Lake Worth, FL 33460
P (561) 689-0889
F (561) 689-2851

Under Florida law, e-mail addresses are public records. If you do not want your e-mail address released in response to a public records request, do not send electronic mail to this entity. Instead, contact this office by phone or in writing.
